Exide Technologies, Vernon, CA
Draft Closure Plan
June 11, 2015

DTSC

South Coast AQMD

Topics To Be Discussed

- Closure Plan Overview
- Exide's Proposed Plan
- Proposed Plan - Improvements
- Next Steps
- Technical Advisor

DTSC

South Coast AQMD

What is a Closure Plan?

- Closure Plan is part of the Permitting process
- Closure Plan Requirements:
  - Performance Standards
  - Financial Assurance
  - Detailed plan for the entire process

DTSC

South Coast AQMD

Where is DTSC in the Closure Plan process for Exide?

- Exide submitted the Closure Plan on May 15th
- DTSC has 30 days to review the Plan

DTSC

South Coast AQMD

Components of Closure Plan

- Removal of Inventory and Wastes
- Decontamination
- Deconstruction

DTSC

South Coast AQMD

Pre-Closure Plan Work

Removal of Stored Material

DTSC

South Coast AQMD

DTSC

South Coast AQMD

Closure Plan (Proposed)

Removal and management of waste

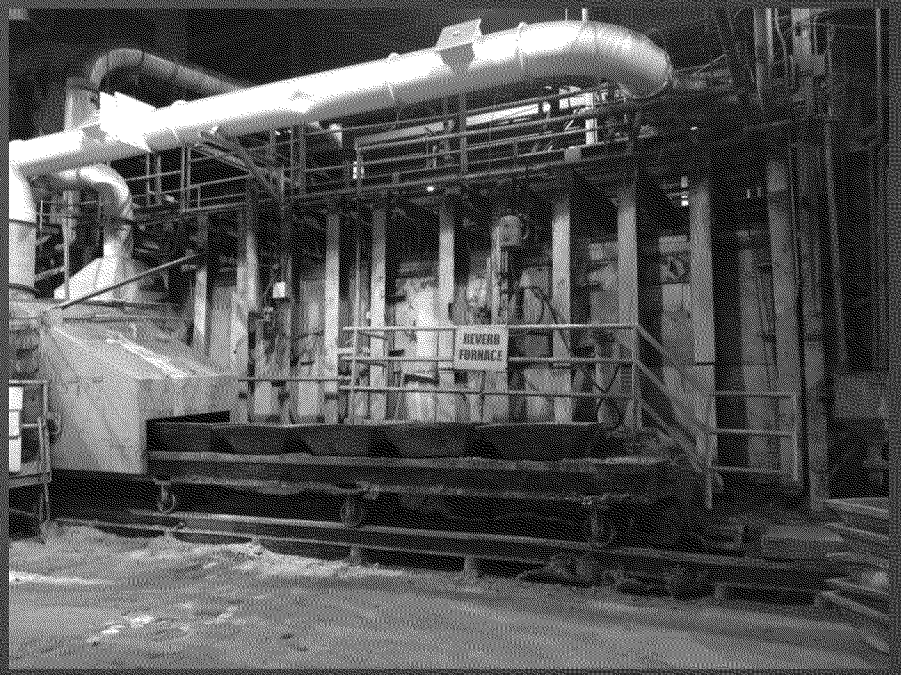

DTSC

South Coast AQMD

DTSC

South Coast AQMD

Closure Plan (Proposed)

Unit Decontamination

DTSC

South Coast AQMD

Closure Plan (Proposed)

Unit Decontamination

DTSC

South Coast AQMD

Closure Plan (Proposed)

Confirmation Sampling

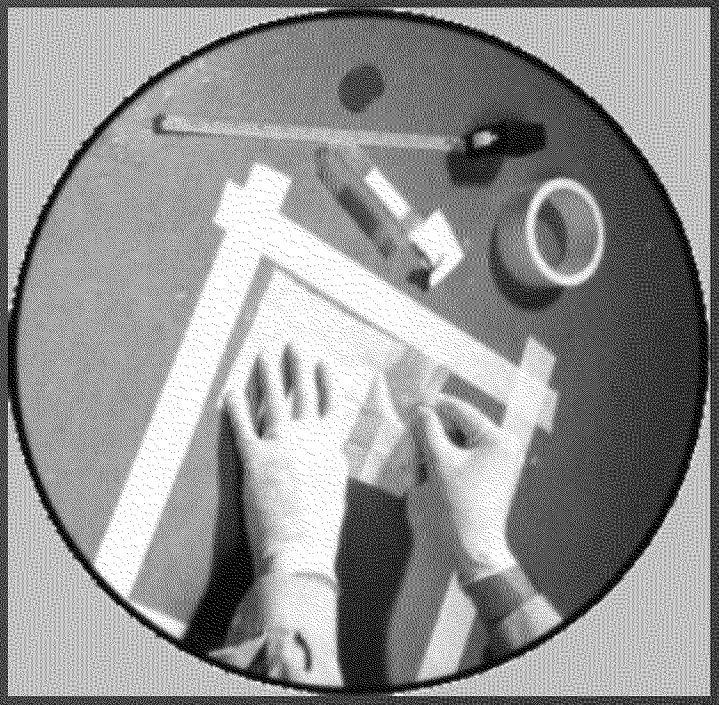

http://www.arushaconstruction.com/lead-dust-wipe-clearance.html

https://cna.ca/news/uranium-mines-and-mills-subject-to-strict-regulations/

DTSC

South Coast AQMD

Closure Plan (Proposed)

Removal of RCRA Units for Re-use:

- Paste Thickening Unit
- Reverb Furnace
- Blast Furnace
- Hammer Mill
- Flocculation Tank
- Rotary Kiln
- Surge Tank
- Kettles

DTSC

South Coast AQMD

Closure Plan (Proposed)

Containment Area and Building Decontaminatio

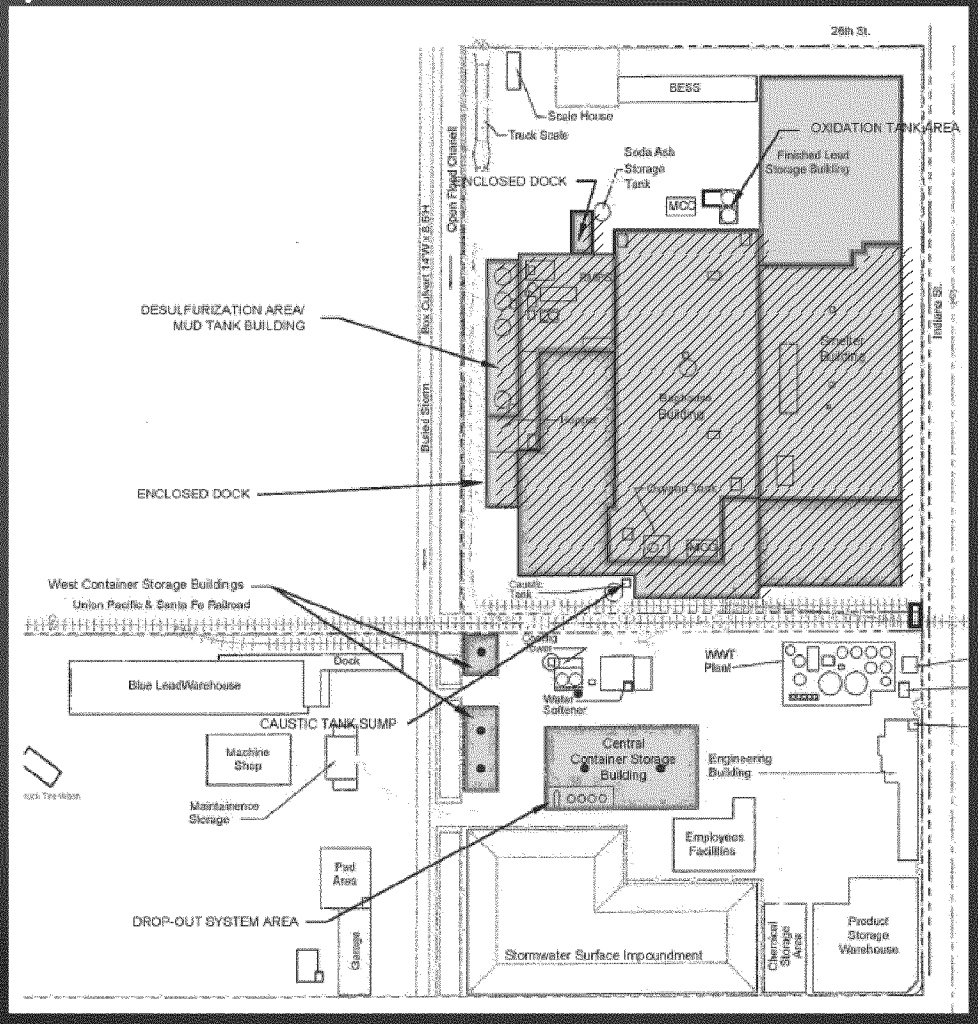

DTSC

South Coast AQMD

Closure Plan (Proposed)

Confirmation Sampling of Containment Area and Building

http://www.gemalab-qc.com/apps/photos/photo?photoid=156855780

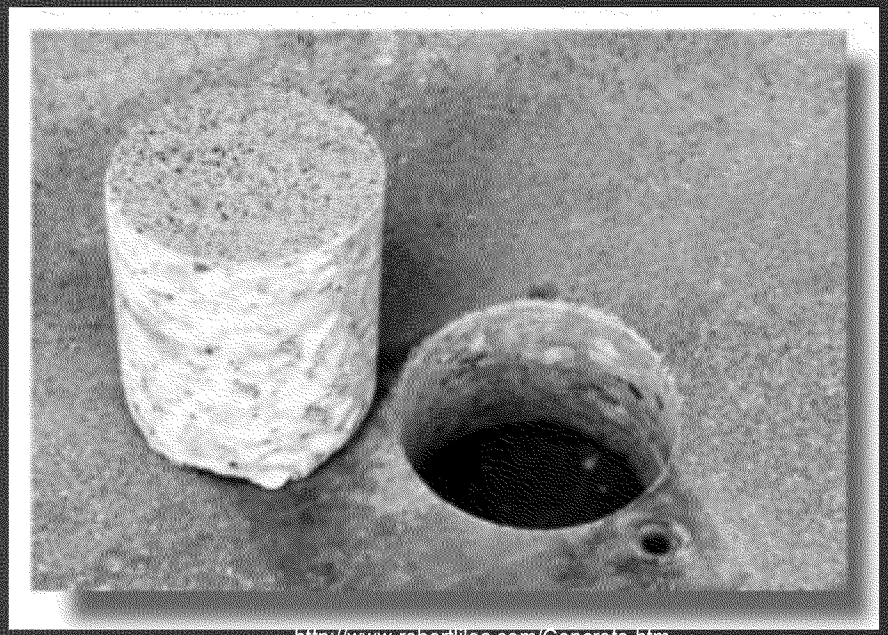

http://www.robertliles.com/Concrete.htm

http://concreteinspectors.com/faqs/

DTSC

South Coast AQMD

Closure Plan (Proposed)

Soil Sampling

Concrete

Soil Sample 0-1’

Soil Sample 1-2’

Soil Sample 2-3’

Soil Sample 6-7’

https://ndep.nv.gov/failoh/photos.htm

DTSC

South Coast AQMD

Closure Plan (Proposed)

Air Sampling

- Real-time air monitoring with movable monitors
- Current fence line monitors
- Personal air monitors

http://www.tsi.com/dusttrak-ii-aerosol-monitor-8532/

DTSC

South Coast AQMD

Closure Plan (Proposed)

Building Deconstruction

DTSC

South Coast AQMD

Closure Plan (Proposed)

Stormwater System Decontamination

- 3,100 linear feet of piping
- Surface Impoundment liner

http://www.waterworld.com/articles/print/products/2012/10/joint-seals.html

DTSC

South Coast AQMD

Proposed Plan - Improvements

- Cleaner standards
- Less waste left in place
- Improved Sampling and Analysis Plans
- Better characterization before reuse
- Submittal of plans to determine background levels

The list of deficiencies will be posted on DTSC's Website

DTSC

South Coast AQMD

Next Steps

- DTSC to Issue a Notice of Deficiency (NOD)
- Exide has 15 days to revise the Closure Plan and re-submit to DTSC
- DTSC to review revised plan
- DTSC will impose a Plan that will be Protective of the Community

DTSC

South Coast AQMD

Technical Advisor

- Update on selection
- July 1 target date

DTSC

South Coast AQMD
