Water Facilities Projects Milestone Schedule

Activity ID	Activity Name
	Water Facilities Projects Milestone Schedule
	Water Facilities Projects
	WC 1211 Ashburton Reservoir Tanks
A1010	Tank Design
A1005	Site Prep Design
A1000	30% Design
A1001	60% Design
A1002	90% Design
A1003	Design Completion
A1020	Construction NTP
A1021	Site Prep
A1025	Shutdown
A1022	Tank Construction
	WC 1173 GUILFORD RESERVOIR IMPROVEMENTS
A1147	Construction (No shut-down By-Pass)
	WC 1204 Druid Water Tanks
A1030	30% Design
A1031	60% Design
A1032	90% Design
A1033	Design Completion
A1034	Construction NTP
A1040	WC 1204 Druid Tanks Construction(No Shut-downs)
	ASHBURTON PUMPING STATION
A1144	Design
A1146	Construction
A1145	Shutdown (Partial)
	Cromwell Water Pumping Station Improvements
A1124	Station Out of Service (Tunnel Repairs, Electrical Installation) shutdov
A1125	Station In Service (Site Preparation/Bldg Construction)
A1126	Station Out of Service (Pumps/Piping Replacement) Shutdown
A1127	Station In Service (Project Completion)
	Guilford Water Pumping Station Rehabilitation
A1080	Temporary Sodium Hypochlorite Feed Equipment Install.
A1090	Construction Phase 1
A1093	Partial Shutdown
A1094	Construction Phase 3
A1092	Construction Phase 2
A1096	Construction Phase 4
A1110	Construction Phase 5
	VERNON PUMPING STATION
A1148	Design
A1151	Construction
A1150	Shutdown

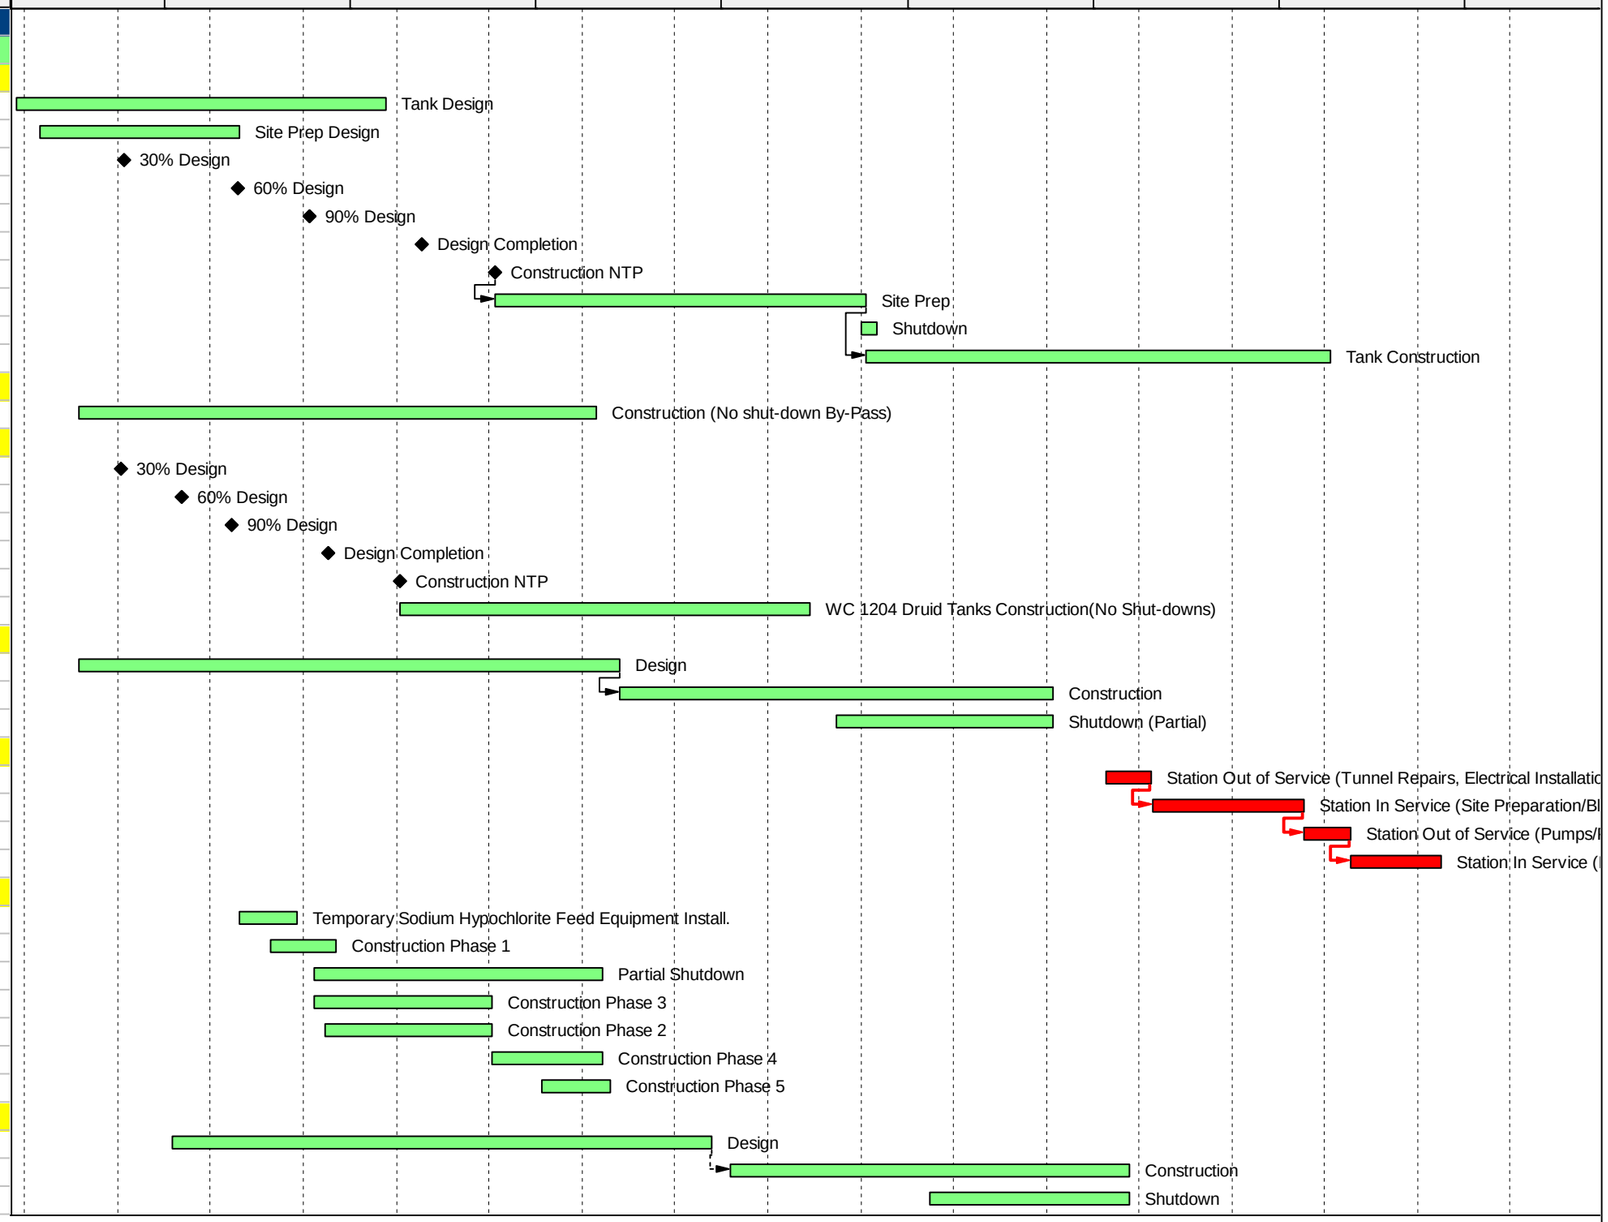

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
