GENERAL SERVICES ADMINISTRATION PUBLIC BUILDINGS SERVICE SUPPLEMENTAL LEASE AGREEMENT	SUPPLEMENTAL AGREEMENT NO.: 1	DATE: 12/11/2012
	TO LEASE NO.: GS-11B-12545	

ADDRESS OF PREMISES: 9800 Medical Center Drive, Rockville, MD 20850-6386

THIS AGREEMENT, made and entered into this date by and between: ARE-Maryland No. 24, LLC

whose address is: 385 E. Colorado Boulevard, Suite 299
Pasadena, CA 91101-6104

Hereinafter called the Lessor, and the UNITED STATES OF AMERICA, hereinafter called the Government:

WHEREAS, the parties hereto desire to amend the above Lease..

NOW THEREFORE, these parties for the considerations hereafter mentioned covenant and agree that the said Lease is amended, effective __ September 17, 2012 _, as follows :

1. Paragraph 6 of the Lease is hereby amended to include the following:

   K. Primavera Project Schedule for Forrester Construction Project 9800 08272012 Start Date 08AUG12 and Data Date 28AUG12.

2. The Contracting Officer issued issued a Notice to Proceed (NTP) for construction on September 17, 2012. With the inclusion of 6(K) to the Lease, the Lessor will ensure phased substantial completion per the Project Schedule dated August 8, 2012.

This document will not constitute an obligation until the date of execution by the Government, which execution shall be within thirty (30) days of the Government's receipt of the SLA executed by the Lessor. Therefore, while payments may be made retroactively, no monies whatsoever are due until thirty (30) days after the date of execution by the Government. Any amount due will not accrue interest until that time.

All other terms and conditions of the Lease shall remain in force and effect.

IN WITNESS WHEREOF, the parties subscribed their names as of the above date.

LESSOR: ARE-Maryland No. 24, LLC, a Delaware limited liability company
BY: ALEXANDRIA REAL ESTATE EQUITIES, L.P., a Delaware limited partnership, managing member
BY: ARE-QRS CORP., a Maryland corporation, general partner

BY (b) (6) [redacted]
(Signature)

Eric S. Johnson
Vice President
Real Estate Legal Affairs
(Title)

IN THE PRESENCE OF (witnessed by :)

(b) (6) [redacted]
(Signature)

385 E. Colorad Blvd., Suite 299, Pasadena, CA 91706
(Address)

UNITED STATES OF AMERICA

BY (b) (6) [redacted]
(Signature)

Contracting Officer
(Official Title)

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
9800 LEASE SPACE FOR MULTI. PROGRAMS						
MILESTONES						
MSA0000	NOTICE OF AWARD	0	0	21MAY12 A		
MSA1000	NOTICE TO PROCEED/MOBILIZATION	15	3	13AUG12 A	30AUG12	
MSA0010	CONSTRUCTION COMMENCEMENT	0	0	31AUG12		
MSA0990	SUBSTANTIAL COMPLETION	0	0		03JUN13 *	
MSSW025	START SITEWORK	0	0	31AUG12		
MSSW030	SITEWORK COMPLETION	0	0		01FEB13	
MS10015	START BLDG B 3FLR	0	0	05SEP12		
MS10020	BLDG B SUBSTANTIAL COMPLETION	0	0		29JAN13	
MS10050	BLDG B TENANT OCCUPANCY	0	0		19FEB13	OWNR
MS20035	START BLDG A 2FLR	0	0	06SEP12		
MS2R050	BLDG A ROOFTOP COMPLETION	0	0		15MAR13	
MS20040	BLDG A 2FLR COMPLETION	0	0		23MAY13	
MS20050	BLDG A SUBSTANTIAL COMPLETION	0	0		27MAY13	
MS2R045	START BLDG A ROOFTOP	0	0	28MAY13		
MS20060	BLDG A TENANT OCCUPANCY	1	1	11JUN13	11JUN13	OWNR
MS2C065	START BLDG C 2FL	0	0	11SEP12		
MSC3075	START BLDG C 3FL	0	0	17SEP12		
MSCL055	START BLDG C LOWER LEVEL COMPLETION	0	0	26SEP12		
MSCP085	START BLDG C PENTHOUSE & ROOF	0	0	13NOV12		
MSCL060	BLDG C LOWER LEVEL COMPLETION	0	0		05APR13	
MSCP090	BLDG C PENTHOUSE & ROOF COMPLETION	0	0		27MAY13	
MSC3080	BLDG C 3FL COMPLETION	0	0		28MAY13	
CLSC1040	BLDG C SUBSTANTIAL COMPLETION	0	0		03JUN13	
MS2C070	BLDG C 2FL COMPLETION	0	0		03JUN13	
MS2C080	BLDG C TENANT OCCUPANCY	1	1	24JUN13	24JUN13	
PROCUREMENT						

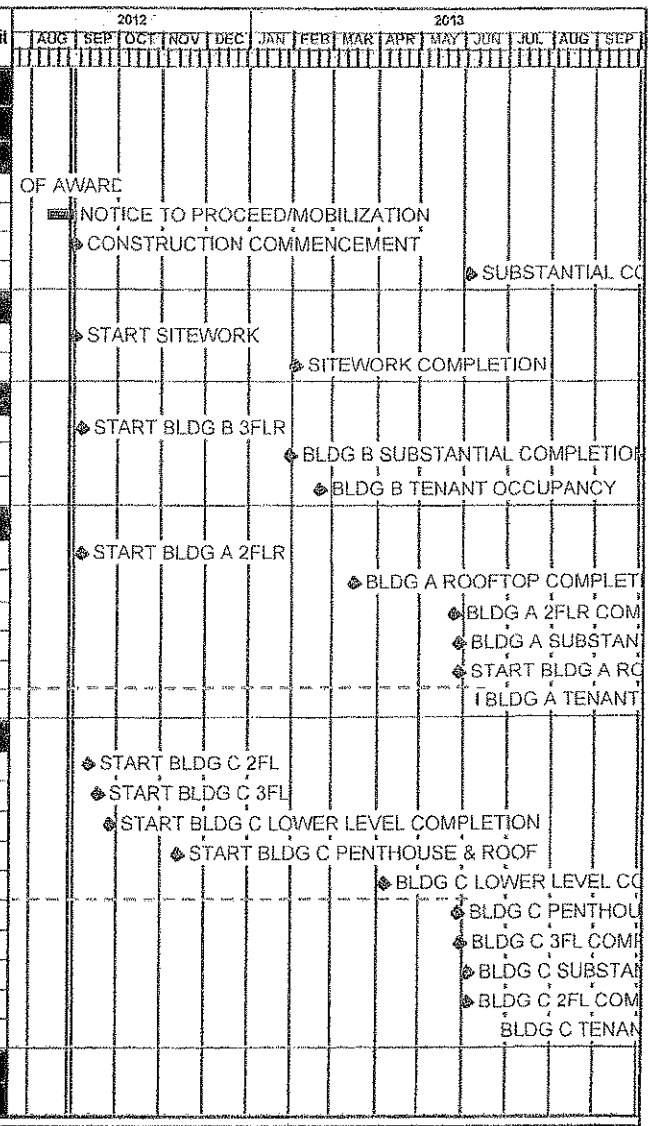

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	1A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
PR1150	PROCURE DEMOUNTABLE PARTITION	15	0	09MAY12 A	16JUN12 A	DEMP
PR1010	PROCURE DOORS, FRAMES, HARDWARE	30	0	21MAY12 A	12JUN12 A	DOOR
PR1170	PROCURE PAINTING SUBCONTRACTOR	50	0	21MAY12 A	20JUL12 A	PAIN
PR1130	PROCURE OPERABLE PARTITION SUBCONTRACTOR	35	0	21MAY12 A	27JUL12 A	OPER
PR1040	PROCURE DEMOLITION SUBCONTRACTOR	20	0	21MAY12 A	03AUG12 A	DEMO
PR1000	PROCURE BIM CONSULTANT	10	0	21MAY12 A	13AUG12 A	BIM
PR1020	PROCURE MECHANICAL SUBCONTRACTOR	20	0	21MAY12 A	13AUG12 A	MECH
PR1030	PROCURE ELECTRICAL SUBCONTRACTOR	20	0	21MAY12 A	13AUG12 A	ELEC
PR1050	PROCURE LABORATORY CASEWORK/EQUIPMENT	20	0	21MAY12 A	13AUG12 A	CASE
PR1100	PROCURE STEEL SUBCONTRACTOR	35	0	21MAY12 A	13AUG12 A	SSTL
PR1070	PROCURE DRYWALL SUBCONTRACTOR	25	0	21MAY12 A	21AUG12 A	DRYW
PR1190	PROCURE WINDOW / GLAZING SUBCONTRACTOR	40	0	21MAY12 A	22AUG12 A	WIND
PR1110	PROCURE SITEWORK SUBCONTRACTOR	20	0	21MAY12 A	26AUG12 A	SITE
PR1080	PROCURE COLD ROOM SUBCONTRACTOR	45	1	21MAY12 A	28AUG12	MECH
PR1060	PROCURE FIRE PROTECTION SUBCONTRACTOR	20	2	21MAY12 A	29AUG12	FRPT
PR1120	PROCURE MILLWORK SUBCONTRACTOR	30	5	21MAY12 A	03SEP12	MILL
PR1180	PROCURE MASONRY SUBCONTRACTOR	40	5	21MAY12 A	03SEP12	MASN
PR1090	PROCURE STERILIZER SUBCONTRACTOR	45	10	21MAY12 A	10SEP12	MECH
PR1140	PROCURE CONCRETE SUBCONTRACTOR	35	10	21MAY12 A	10SEP12	CONC
PR1160	PROCURE FLOORING SUBCONTRACTOR	55	10	21MAY12 A	10SEP12	FLRG
SUBMITTALS						
SU1270	SUBMIT DEMOUNTABLE PARTITIONS	10	0	21MAY12 A	02JUL12 A	DEMP
SU1010	SUBMIT DOORS, FRAMES, HARDWARE	10	0	21MAY12 A	06JUL12 A	DOOR
SU1050	SUBMIT LAB CASEWORK BLDG C AND EQUIPMENT	25	0	09JUL12 A	01AUG12 A	CASE
SU1440	SUBMIT LAB CASEWORK BLDG A	32	0	09JUL12 A	10AUG12 A	CASE
SU1060	SUBMIT FUME HOODS/LABORATORY EQUIPMENT	25	0	09JUL12 A	22AUG12 A	CASE
SU1300	SUBMIT INTERIOR PAINT	10	0	16JUL12 A	27JUL12 A	PAIN
SU1000	SUBMIT BIM BASELINE ARCHITECTURAL MODEL	23	2	16JUL12 A	29AUG12	BIM
SU1240	SUBMIT OPERABLE PARTITION	10	0	30JUL12 A	10AUG12 A	OPER
SU1180	SUBMIT LIGHTING	10	3	30JUL12 A	30AUG12	ELEC
SU1100	SUBMIT AHU'S	10	0	08AUG12 A	17AUG12 A	MECH
SU1150	SUBMIT TERMINAL AIR UNITS	10	5	15AUG12 A	03SEP12	MECH
SU1220	SUBMIT STUD FRAMING AND DRYWALL	10	5	15AUG12 A	03SEP12	DRYW
SU1130	SUBMIT CHILLERS	10	2	20AUG12 A	29AUG12	MECH

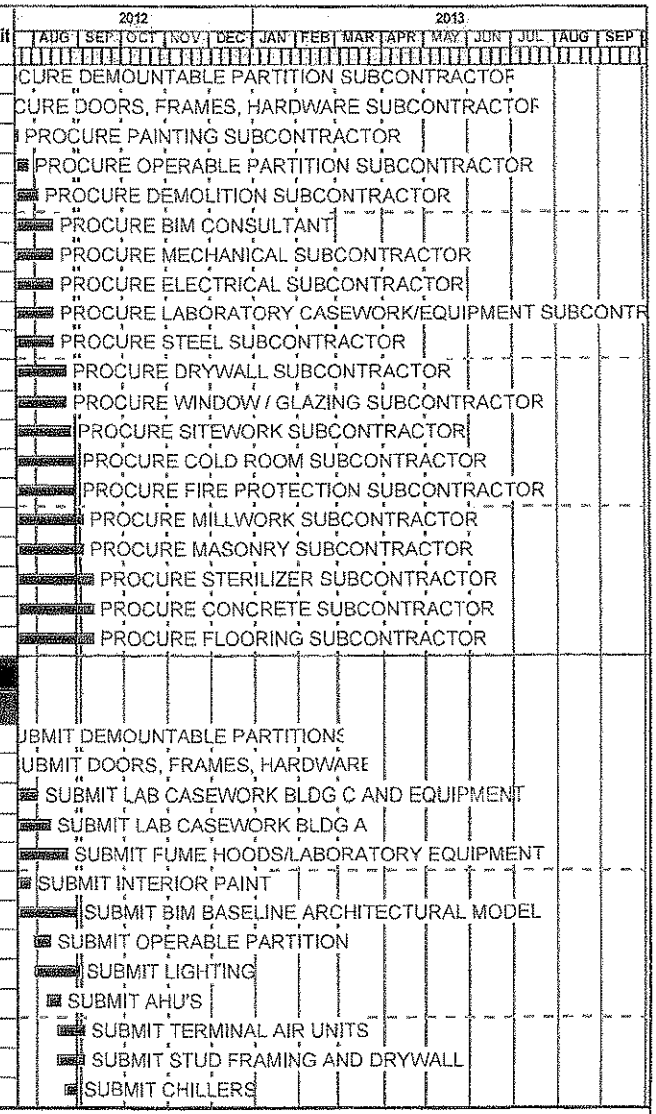

			Date	Revision	Checked	Approved
Data date	28AUG12	9800 LEASE SPACE FOR MULTI. PROGRAMS				
Start date	08AUG12					
Finish date	24JUN13	9800 08272012				
Project name	9800 08272012					
Page number	2A	FORRESTER CONSTRUCTION				
© Primavera Systems, Inc.						

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibility
SU1040	SUBMIT STRUCTURAL STEEL	10	10	28AUG12	10SEP12	SSTL
SU1090	SUBMIT BULK CHEMICAL STORAGE UNITS	10	10	28AUG12	10SEP12	MECH
SU1110	SUBMIT RTU'S	10	10	28AUG12	10SEP12	MECH
SU1120	SUBMIT EXHAUST FANS	10	10	28AUG12	10SEP12	MECH
SU1140	SUBMIT BOILERS	10	10	28AUG12	10SEP12	MECH
SU1160	SUBMIT DUCTWORK BUILDING B	10	10	28AUG12	10SEP12	MECH
SU1170	SUBMIT DUCTWORK	10	10	28AUG12	10SEP12	MECH
SU1190	SUBMIT GENERATOR	10	10	28AUG12	10SEP12	ELEC
SU1200	SUBMIT NITROGEN SYSTEM	10	10	28AUG12	10SEP12	MECH
SU1210	SUBMIT CO2 MANIFOLD	10	10	28AUG12	10SEP12	MECH
SU1280	SUBMIT CEILING GRID & TILE	10	10	28AUG12	10SEP12	CLGT
SU1310	SUBMIT REVERSE OSMOSIS SYSTEM	10	10	28AUG12	10SEP12	MECH
SU1320	SUBMIT WATER HEATERS	10	10	28AUG12	10SEP12	MECH
SU1330	SUBMIT TRANSFORMERS AND PANELS	10	10	28AUG12	10SEP12	ELEC
SU1350	SUBMIT VACUUM SYSTEM	10	10	28AUG12	10SEP12	MECH
SU1360	SUBMIT FCUS	10	10	28AUG12	10SEP12	MECH
SU1370	SUBMIT PUMPHOUSE	10	10	28AUG12	10SEP12	MECH
SU1380	SUBMIT ACCU/CONDENSING UNIT	10	10	28AUG12	10SEP12	MECH
SU1390	SUBMIT FIRE ALARM	10	10	28AUG12	10SEP12	FIRE
SU1400	SUBMIT R, G, D'S	10	10	28AUG12	10SEP12	MECH
SU1410	SUBMIT VFD'S	10	10	28AUG12	10SEP12	ELEC
SU1420	SUBMIT WINDOWS	10	10	28AUG12	10SEP12	WIND
SU1080	SUBMIT COLD ROOMS	10	10	29AUG12	11SEP12	MECH
SU1250	SUBMIT FIRE PROTECTION PRODUCT DATA	10	10	30AUG12	12SEP12	FRPT
SU1020	SUBMIT 3D MEP DRAWINGS BUILDING A/C	15	15	30AUG12	19SEP12	BIM
SU1230	SUBMIT ARCHITECTURAL MILLWORK	10	10	04SEP12	17SEP12	MILL
SU1340	SUBMIT MASONRY	10	10	04SEP12	17SEP12	MASN
SU1070	SUBMIT AUTOCLAVE	10	10	11SEP12	24SEP12	LABE
SU1260	SUBMIT CONCRETE MIX DESIGN	10	10	11SEP12	24SEP12	CONC
SU1290	SUBMIT VCT, SHEET VINYL, CARPET	10	10	11SEP12	24SEP12	CARP
REVIEW AND APPROVE						
RA1010	REVIEW & APPROVE DOORS, FRAMES, HARDWARE	10	2	31JUL12 A	03SEP12	ARCH
RA1260	REVIEW AND APPROVE DEMOUNTABLE PARTITIONS	10	10	13AUG12 A	13SEP12	ARCH
RA1110	REVIEW & APPROVE CHILLERS	15	15	13AUG12 A	19SEP12	ARCH

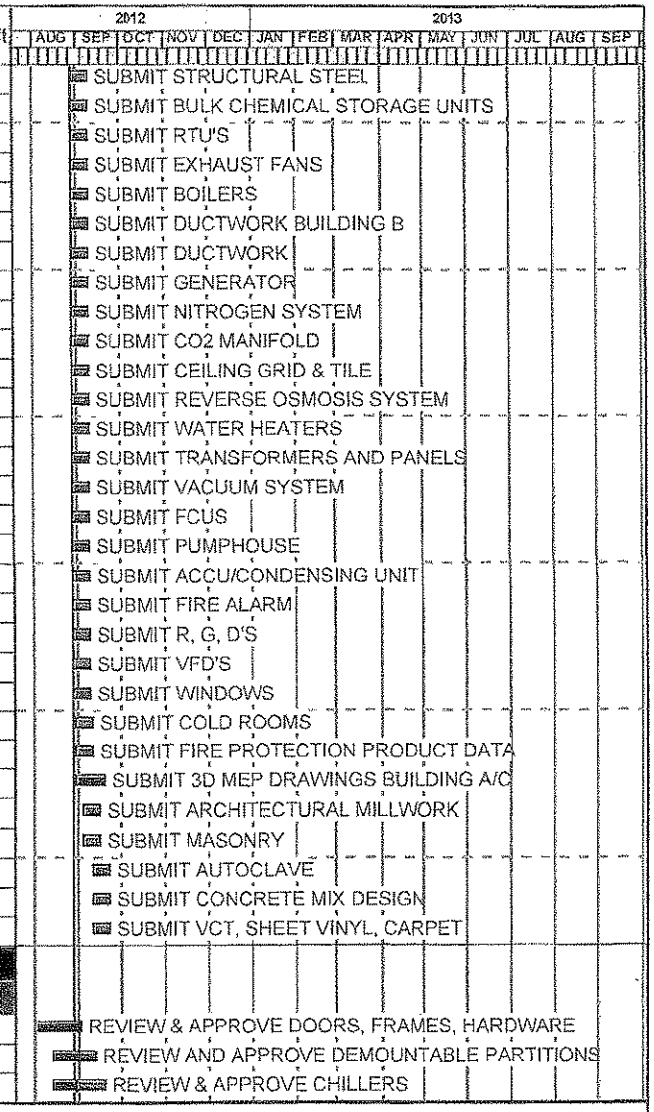

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	3A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
RA1040	REVIEW & APPROVE FUME HOODS/LABORATORY	10	10	22AUG12 A	10SEP12	ARCH
RA1410	REVIEW & APPROVE LAB CASEWORK BLDG A	10	10	22AUG12 A	10SEP12	ARCH
RA1030	REVIEW & APPROVE LAB CASEWORK BLDG C	15	15	22AUG12 A	17SEP12	ARCH
RA1080	REVIEW & APPROVE AHU'S	15	15	22AUG12 A	17SEP12	ARCH
RA1230	REVIEW & APPROVE OPERABLE PARTITION	10	10	28AUG12	10SEP12	ARCH
RA1290	REVIEW & APPROVE INTERIOR PAINT	10	10	28AUG12	10SEP12	ARCH
RA1170	REVIEW & APPROVE LIGHTING	15	15	31AUG12	20SEP12	ARCH
RA1210	REVIEW & APPROVE STUD FRAMING AND DRYWALL	10	10	04SEP12	17SEP12	ARCH
RA1130	REVIEW & APPROVE TERMINAL AIR UNITS	15	15	04SEP12	24SEP12	ARCH
RA1140	REVIEW & APPROVE DUCTWORK BUILDING B	10	10	11SEP12	24SEP12	ARCH
RA1150	REVIEW & APPROVE R, G, D'S	10	10	11SEP12	24SEP12	ARCH
RA1160	REVIEW & APPROVE DUCTWORK	10	10	11SEP12	24SEP12	ARCH
RA1200	REVIEW & APPROVE CO2 MANIFOLD & TANKS	10	10	11SEP12	24SEP12	ARCH
RA1270	REVIEW & APPROVE CEILING GRID & TILE	10	10	11SEP12	24SEP12	ARCH
RA1350	REVIEW & APPROVE FCU'S	10	10	11SEP12	24SEP12	ARCH
RA1380	REVIEW & APPROVE FIRE ALARM	10	10	11SEP12	24SEP12	ARCH
RA1390	REVIEW & APPROVE VFD'S	10	10	11SEP12	24SEP12	ARCH
RA1400	REVIEW & APPROVE WINDOWS	10	10	11SEP12	24SEP12	ARCH
RA1020	REVIEW & APPROVE STRUCTURAL STEEL	15	15	11SEP12	01OCT12	ARCH
RA1070	REVIEW & APPROVE BULK CHEMICAL STORAGE UNITS	15	15	11SEP12	01OCT12	ARCH
RA1090	REVIEW & APPROVE RTU'S	15	15	11SEP12	01OCT12	ARCH
RA1100	REVIEW & APPROVE EXHAUST FANS	15	15	11SEP12	01OCT12	ARCH
RA1120	REVIEW & APPROVE BOILERS	15	15	11SEP12	01OCT12	ARCH
RA1180	REVIEW & APPROVE GENERATOR	15	15	11SEP12	01OCT12	ARCH
RA1190	REVIEW & APPROVE NITROGEN SYSTEM	15	15	11SEP12	01OCT12	ARCH
RA1300	REVIEW & APPROVE REVERSE OSMOSIS	15	15	11SEP12	01OCT12	ARCH
RA1310	REVIEW & APPROVE WATER HEATERS	15	15	11SEP12	01OCT12	ARCH
RA1320	REVIEW & APPROVE TRANSFORMERS AND PANELS	15	15	11SEP12	01OCT12	ARCH
RA1340	REVIEW & APPROVE VACUUM SYSTEM	15	15	11SEP12	01OCT12	ARCH
RA1360	REVIEW & APPROVE PUMPHOUSE	15	15	11SEP12	01OCT12	ARCH
RA1370	REVIEW & APPROVE ACCU/CONDENSING UNIT	15	15	11SEP12	01OCT12	ARCH
RA1060	REVIEW & APPROVE COLD ROOMS	10	10	12SEP12	25SEP12	ARCH
RA1240	REVIEW & APPROVE FIRE PROTECTION PRODUCT	10	10	13SEP12	26SEP12	ARCH
RA1220	REVIEW & APPROVE ARCHITECTURAL MILLWORK	10	10	18SEP12	01OCT12	ARCH
RA1330	REVIEW & APPROVE MASONRY	10	10	18SEP12	01OCT12	ARCH
RA1000	REVIEW AND FINALIZE BIM	15	15	20SEP12	10OCT12	ARCH

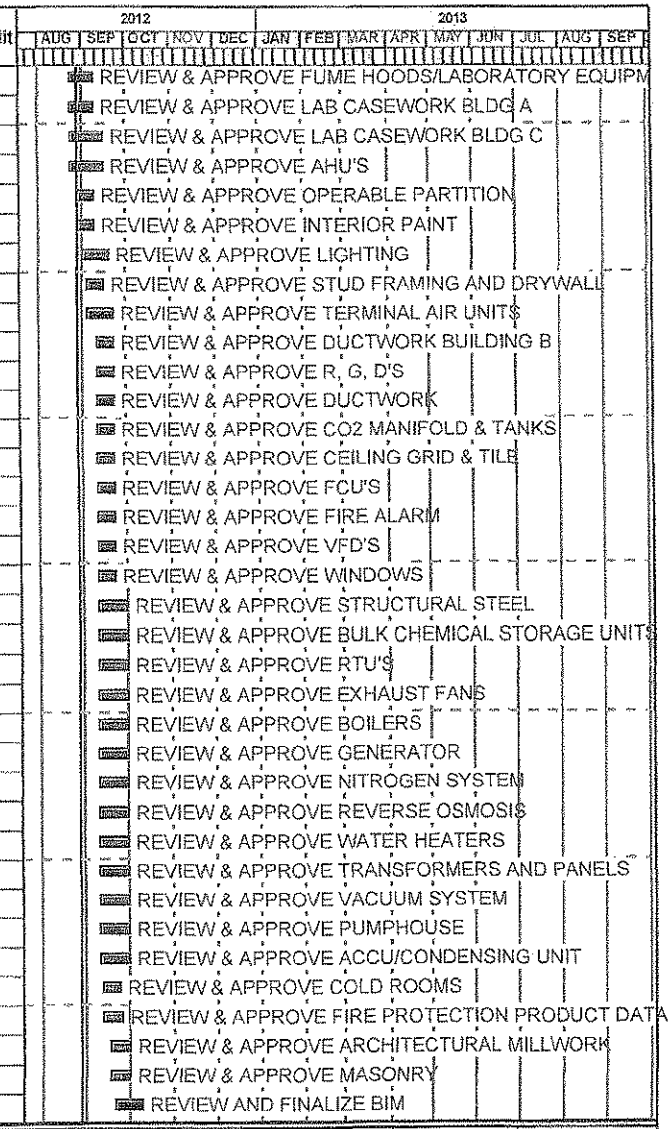

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	4A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
RA1050	REVIEW & APPROVE AUTOCLAVE	10	10	25SEP12	08OCT12	ARCH
RA1250	REVIEW & APPROVECONCRETE MIX DESIGN	10	10	25SEP12	08OCT12	ARCH
RA1280	REVIEW & APPROVE VCT, SHEET VINYL, CARPET	10	10	25SEP12	08OCT12	ARCH
FABRICATION AND DELIVERY						
FD1240	DELIVER HOLLOW METAL FRAMES - (BUILDING B)	35	30	21AUG12 A	15OCT12	DOOR
FD1000	F&D HOLLOW MTL FRMS-(BLDGS A&C)	30	30	04SEP12	15OCT12	DOOR
FD1010	F&D DOORS & HARDWARE (BUILDING B)	45	45	04SEP12	05NOV12	DOOR
FD1260	DELIVER DOORS & HARDWARE - (BUILDING A&C)	45	45	04SEP12	05NOV12	DOOR
FD1300	DELIVER INTERIOR PAINT	10	10	11SEP12	24SEP12	PAIN
FD1210	FABRICATE & DELIVER OPERABLE PARTN (BUILDING	50	50	11SEP12	19NOV12	OPER
FD1470	FABRICATE AND DELIVER CASEWORK CORES A	55	55	11SEP12	26NOV12	CASE
FD1500	FABRICATE AND DELIVER SHELVING AND TRIM A	55	55	11SEP12	26NOV12	CASE
FD1480	FABRICATE AND DELIVER LAB CABINETS &	60	60	11SEP12	03DEC12	CASE
FD1040	FABRICATE & DELIVER FUME HOODS/LABORATORY	75	75	11SEP12	26DEC12	CASE
FD1250	DEMOUNTABLE PARTITIONS (BUILDING B)	50	50	14SEP12	22NOV12	DEMP
FD1190	FABRICATE AND DELIVER STUD FRAMING AND	10	10	18SEP12	01OCT12	DRYW
FD1080	FABRICATE AND DELIVER AHU'S	45	45	18SEP12	19NOV12	MECH
FD1030	FABRICATE AND DELIVER LAB CASEWORK CORES C	60	60	18SEP12	10DEC12	CASE
FD1460	FABRICATE AND DELIVER LAB CABINETS &	60	60	18SEP12	10DEC12	CASE
FD1490	FABRICATE AND DELIVER SHELVING AND TRIM C	60	60	18SEP12	10DEC12	CASE
FD1110	FABRICATE AND DELIVER CHILLERS	70	70	20SEP12	28DEC12	MECH
FD1520	FABRICATE AND DELIVER LIGHTING - (BUILDING B)	40	40	21SEP12	15NOV12	ELEC
FD1150	FABRICATE AND DELIVER LIGHTING	60	60	21SEP12	13DEC12	ELEC
FD1310	FABRICATE AND DELIVER DUCTWORK BUILDING B	10	10	25SEP12	08OCT12	MECH
FD1510	FABRICATE CEILING GRID	15	15	25SEP12	15OCT12	
FD1430	FABRICATE AND DELIVER R, G, D'S	25	25	25SEP12	29OCT12	MECH
FD1420	FABRICATE AND DELIVER FIRE ALARM COMPONENTS	30	30	25SEP12	05NOV12	FIRE
FD1450	FABRICATE AND DELIVER WINDOWS	35	35	25SEP12	12NOV12	WIND
FD1130	FABRICATE AND DELIVER TERMINAL AIR UNITS	40	40	25SEP12	19NOV12	MECH
FD1390	FABRICATE AND DELIVER FCU'S	40	40	25SEP12	19NOV12	MECH
FD1180	FABRICATE AND DELIVER CO2 MANIFOLD & TANKS	50	50	25SEP12	03DEC12	MECH
FD1440	FABRICATE AND DELIVER VFD'S	50	50	25SEP12	03DEC12	MECH
FD1370	FABRICATE AND DELIVER CONDENSING UNIT CURBS	20	20	26SEP12	23OCT12	MECH
FD1060	FABRICATE AND DELIVER COLD ROOMS	50	50	26SEP12	04DEC12	MECH

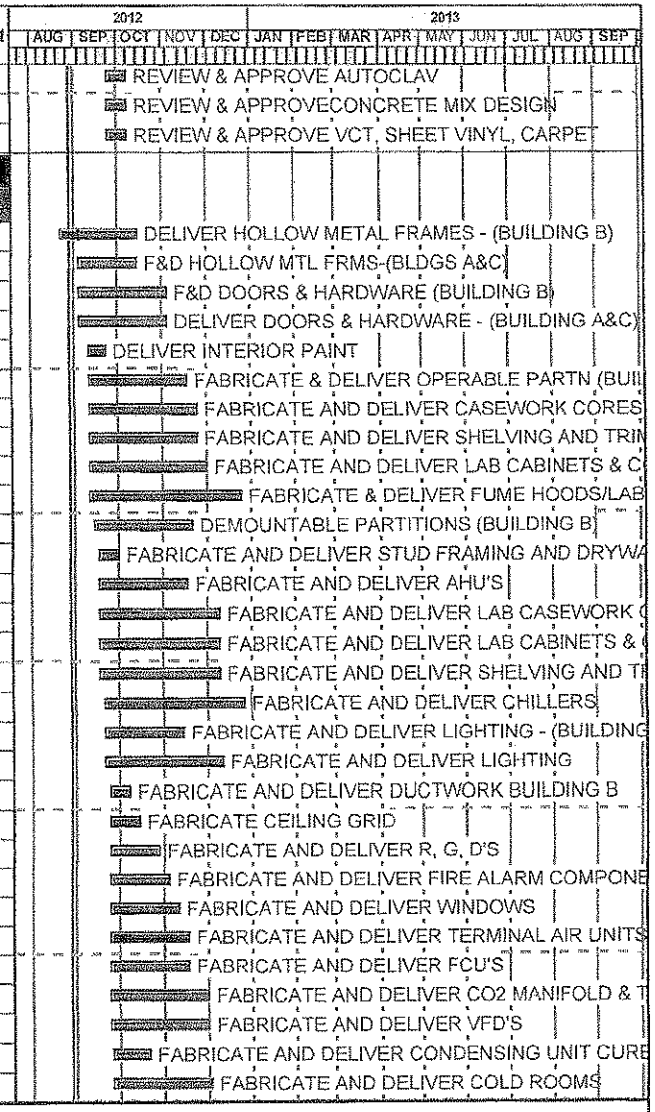

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	5A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
FD1220	FABRICATE AND DELIVER SPRINKLER PIPING AND	15	15	27SEP12	17OCT12	SPRK
FD1360	FABRICATE AND DELIVER MASONRY	20	20	02OCT12	29OCT12	MASN
FD1020	FABRICATE AND DELIVER STRUCTURAL STEEL	30	30	02OCT12	12NOV12	SSTL
FD1120	FABRICATE AND DELIVER BOILERS	30	30	02OCT12	12NOV12	MECH
FD1070	FABRICATE AND DELIVER BULK CHEM STORAGE	40	40	02OCT12	26NOV12	MECH
FD1200	FABRICATE AND DELIVER ARCH MILLWORK	40	40	02OCT12	26NOV12	MILL
FD1320	DELIVER RTU CURBS	40	40	02OCT12	26NOV12	MECH
FD1340	FABRICATE AND DELIVER WATER HEATERS	40	40	02OCT12	26NOV12	MECH
FD1380	FABRICATE AND DELIVER VACUUM SYSTEM	40	40	02OCT12	26NOV12	MECH
FD1410	FABRICATE AND DELIVER ACCU/CONDENSING UNIT	40	40	02OCT12	26NOV12	MECH
FD1170	FABRICATE AND DELIVER NITROGEN SYSTEM	50	50	02OCT12	10DEC12	MECH
FD1350	FABRICATE AND DELIVER PANELS AND	50	50	02OCT12	10DEC12	ELEC
FD1400	FABRICATE AND DELIVER PUMPHOUSE	50	50	02OCT12	10DEC12	MECH
FD1330	FABRICATE AND DELIVER REVERSE OSMOSIS	60	60	02OCT12	26DEC12	MECH
FD1100	FABRICATE AND DELIVER EXHAUST FANS	70	70	02OCT12	10JAN13	MECH
FD1090	FABRICATE AND DELIVER RTU'S	75	75	02OCT12	17JAN13	MECH
FD1160	FABRICATE AND DELIVER GENERATOR	75	75	02OCT12	17JAN13	ELEC
FD1230	DELIVER CONCRETE	5	5	09OCT12	15OCT12	CONC
FD1280	DELIVER VCT	20	20	09OCT12	05NOV12	FLRG
FD1290	DELIVER SHEET VINYL	20	20	09OCT12	05NOV12	FLRG
FD1270	FABRICATE AND DELIVER CARPET	30	30	09OCT12	19NOV12	CARP
FD1050	FABRICATE AND DELIVER AUTOCLAVE	55	55	09OCT12	26DEC12	LABE
FD1140	FABRICATE AND DELIVER DUCTWORK BUILDINGS A &	15	15	11OCT12	31OCT12	MECH
CONSTRUCTION						
SW1000	SEDIMENT AND EROSION CONTROL	1	1	31AUG12	31AUG12	SITE
SW1020	TEMPORARY ACCESS ROADS	2	2	03SEP12	04SEP12	SITE
CY1000	PROTECT TREES TO REMAIN	1	1	03SEP12	03SEP12	SITE
CY1020	REMOVE TREES	3	3	03SEP12	05SEP12	SITE
CY1060	REMOVE SELECT BRICK AT EXISTING BUILDING	8	8	06SEP12	17SEP12	DEMO
CY1080	X RAY EXISTING CONCRETE FOR STEEL	2	2	18SEP12	19SEP12	CONC
CY1260	REROUTE SITE LIGHTING FOR PEPCO EQUIPMENT	3	3	24SEP12	26SEP12	SITE
CY1300	INSTALL 15 WAY DUCTBANK	5	5	27SEP12	03OCT12	MECH
CY1280	INST UNDERGROUND ELEC CONDUIT FROM PEPCO	15	15	27SEP12	17OCT12	ELEC

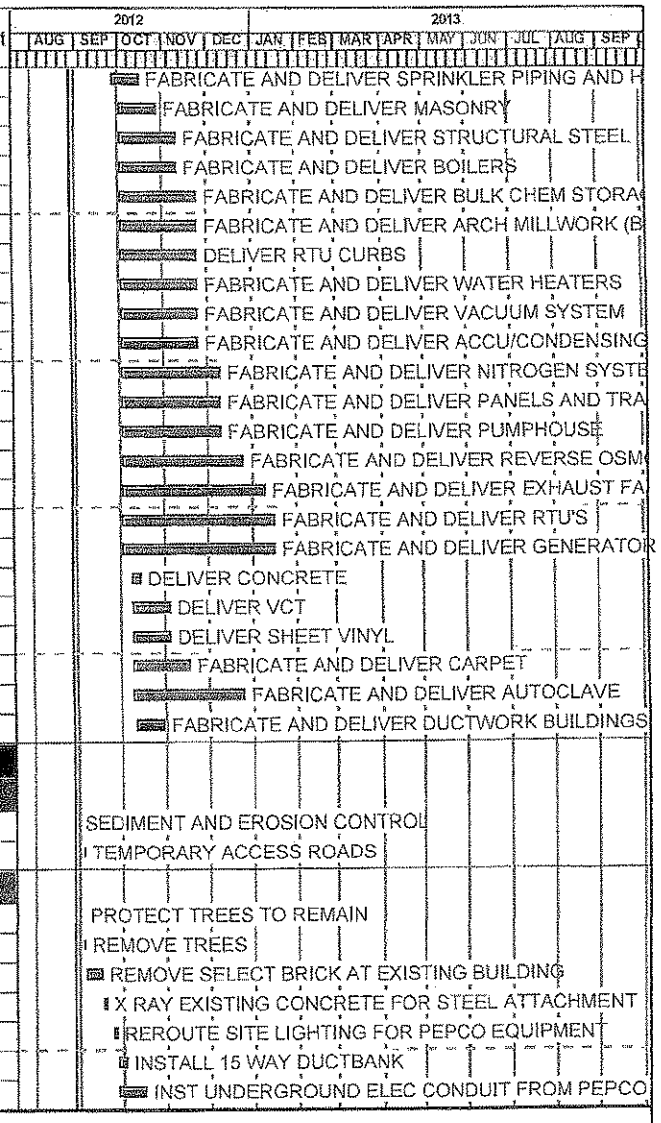

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	6A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
CY1040	PLACE CONCRETE FND FOR EQUIP / PIPE SUPPORTS	15	15	16OCT12	05NOV12	CONC
CY1320	INSTALL WIRING FOR NEW PEPCO SERVICES	5	5	18OCT12	24OCT12	ELEC
CY1380	PLACE CONCRETE FOUNDATIONS FOR SCREENWALL	10	10	18OCT12	31OCT12	CONC
CY1340	INSTALL BOLLARDS FOR PEPCO EQUIPMENT	3	3	25OCT12	29OCT12	MMTL
CY1360	INSTALL PEPCO EQUIPMENT	5	5	30OCT12	05NOV12	ELEC
CY1400	INSTALL CMU AND BRICK AT SCREENWALL	10	10	01NOV12	14NOV12	MASN
CY1100	INSTALL STEEL PIPE SUPPORTS	15	15	13NOV12	03DEC12	SSTL
CY1420	INSTALL GATES	5	5	15NOV12	21NOV12	FENC
CY1440	METAL PANEL AT PIPE CHASE	5	5	15NOV12	21NOV12	MECH
CY1480	INSTALL ELECTRICAL CONDUIT TO EQUIPMENT	10	10	15NOV12	28NOV12	ELEC
CY1500	PULL ELECTRICAL WIRING TO EQUIPMENT	10	10	29NOV12	12DEC12	ELEC
CY1460	INSTALL RELOCATED SIGNS	2	2	13DEC12	14DEC12	SIGN
CY1520	INSTALL ELECTRICAL DEVICES AT EQUIPMENT	5	5	13DEC12	19DEC12	ELEC
CY1540	INSTALL LIGHTS AND SWITCHES	5	5	20DEC12	28DEC12	ELEC
CY1120	INSTALL CHILLERS	5	5	31DEC12	07JAN13	MECH
CY1140	INSTALL PUMPHOUSE	2	2	08JAN13	09JAN13	MECH
CY1240	ROUGH IN MECHANICAL PIPING	15	15	10JAN13	30JAN13	MECH
CY1160	INSTALL GENERATOR	5	5	18JAN13	24JAN13	ELEC
CY1180	INSTALL FUEL STORAGE TANK	2	2	25JAN13	28JAN13	MECH
CY1200	INSTALL CONDENSING UNIT	2	2	29JAN13	30JAN13	MECH
CY1250	START UP CONDENSING UNIT	1	1	31JAN13	31JAN13	COMM
CY1220	INSTALL AIR COOLED CHILLER UNIT	2	2	31JAN13	01FEB13	MECH
CY1230	START UP AIR COOLED CHILLER UNIT	1	1	04FEB13	04FEB13	COMM
N2Y1000	PLACE CONCRETE PADS FOR N2 EQUIPMENT	5	5	06NOV12	12NOV12	CONC
N2Y1020	INSTALL N2 TANK	2	2	11DEC12	12DEC12	MECH
N2Y1040	INSTALL AMBIENT VAPORIZER	2	2	13DEC12	14DEC12	MECH
N2Y1060	INSTALL REGULATOR MANIFOLD	2	2	17DEC12	18DEC12	MECH
N2Y1080	INSTALL VAPORIZER SWITCHOVER MANIFOLD	2	2	19DEC12	20DEC12	MECH
N2Y1081	ROUGH IN PIPE	2	2	21DEC12	26DEC12	MECH
N2Y1100	PLACE CONCRETE FOUNDATIONS FOR SCREENWALL	5	5	27DEC12	03JAN13	CONC
N2Y1120	INSATLL CMU AND BRICK AT SCREENWALL	5	5	04JAN13	10JAN13	MASN
N2Y1140	INSTALL GATE	2	2	11JAN13	14JAN13	FENC
N2Y1160	INSTALL BOLLARDS	2	2	15JAN13	16JAN13	MMTL
N2Y1180	INSTALL ELECTRICAL CONDUIT TO EQUIPMENT	3	3	17JAN13	21JAN13	ELEC
N2Y1200	PULL ELECTRICAL WIRING TO EQUIPMENT	3	3	22JAN13	24JAN13	ELEC

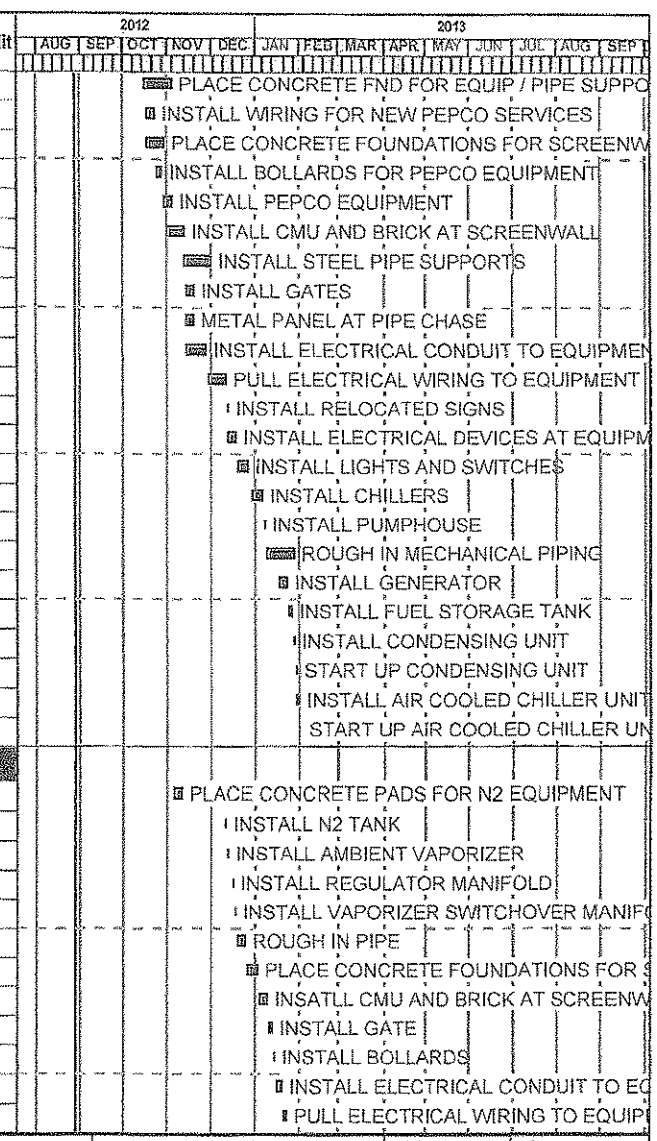

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	7A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
N2Y1220	INSTALL ELECTRICAL DEVICES AT EQUIPMENT	3	3	25JAN13	29JAN13	ELEC
N2Y1240	INSTALL LIGHTS AND SWITCHES	3	3	30JAN13	01FEB13	ELEC
Phase 2						
CO2Y1000	CONCRETE PAD FOR CO2 EQUIPMENT	5	5	13NOV12	19NOV12	CONC
CO2Y1020	INSTALL CO2 TANK	2	2	04DEC12	05DEC12	MECH
CO2Y1040	INSTALL ELECTRIC VAPORIZER	2	2	06DEC12	07DEC12	ELEC
CO2Y1060	INSTALL CHANGOVER CONTROL PANEL	2	2	10DEC12	11DEC12	ELEC
CO2Y1080	INSTALL DUAL REGULATOR ASSEMBLY	2	2	12DEC12	13DEC12	ELEC
CO2Y1100	INSTALL CYLINDER WITH HEADER	2	2	14DEC12	17DEC12	MECH
CO2Y1120	INSTALL CHAINLINK FENCE AND GATE	2	2	18DEC12	19DEC12	FENC
CO2Y1140	ELECTRICAL CONDUIT TO EQUIPMENT	3	3	20DEC12	26DEC12	ELEC
CO2Y1160	PULL ELECTRICAL WIRING TO EQUIPMENT	3	3	27DEC12	31DEC12	ELEC
CO2Y1180	INSTALL ELECTRICAL DEVICES AT EQUIPMET	3	3	02JAN13	04JAN13	ELEC
CO2Y1200	INSTALL LIGHTS AND SWITCHES	3	3	07JAN13	09JAN13	ELEC
Tenant						
B1000	TEMPORARILY REMOVE EXISTING WINDOWS	1	1	05SEP12	05SEP12	WIND
B1020	TEMPORARY PARTITIONS AND DOORS	5	5	06SEP12	12SEP12	DOOR
B1040	CAP AND SAFE ELECTRICAL	10	10	13SEP12	26SEP12	ELEC
B1060	CAP AND SAFE PLUMBING	10	10	13SEP12	26SEP12	PLBG
B1080	CAP AND SAFE SPRINKLER	10	10	13SEP12	26SEP12	SPRK
B1100	DEMO ARCHITECTURAL	10	10	20SEP12	03OCT12	DEMO
B1120	DEMO MECHANICAL	10	10	21SEP12	04OCT12	DEMO
B1140	DEMO ELECTRICAL	10	10	21SEP12	04OCT12	DEMO
B1160	DEMO PLUMBING	10	10	21SEP12	04OCT12	DEMO
B1180	DEMO SPRINKLER	10	10	21SEP12	04OCT12	DEMO
B1420	FRAME PARTITIONS	7	7	02OCT12	10OCT12	DRYW
B1500	IN WALL FIRE ALARM ROUGH IN	8	8	04OCT12	15OCT12	FIRE
B1520	IN WALL VOICE/DATA ROUGH IN	6	8	04OCT12	15OCT12	OWNR
B1540	IN WALL SECURITY ROUGH IN	8	8	04OCT12	15OCT12	OWNR
B1200	LAYOUT PARTITIONS	5	5	05OCT12 *	11OCT12	DRYW
B1240	UNDERSLAB ELECTRICAL ROUGH IN FOR	5	5	05OCT12	11OCT12	ELEC
B1280	DUCTWORK ROUGH IN - TRUNK	7	7	09OCT12	17OCT12	MECH
B1260	INSTALL SUPPORT FOR FOLDING PARTITION	3	3	12OCT12	16OCT12	MMTL
B1220	UNDERSLAB PLUMBING ROUGH IN	5	5	12OCT12	18OCT12	MECH
B1480	IN WALL ELECTRICAL ROUGH IN	5	5	12OCT12	18OCT12	ELEC

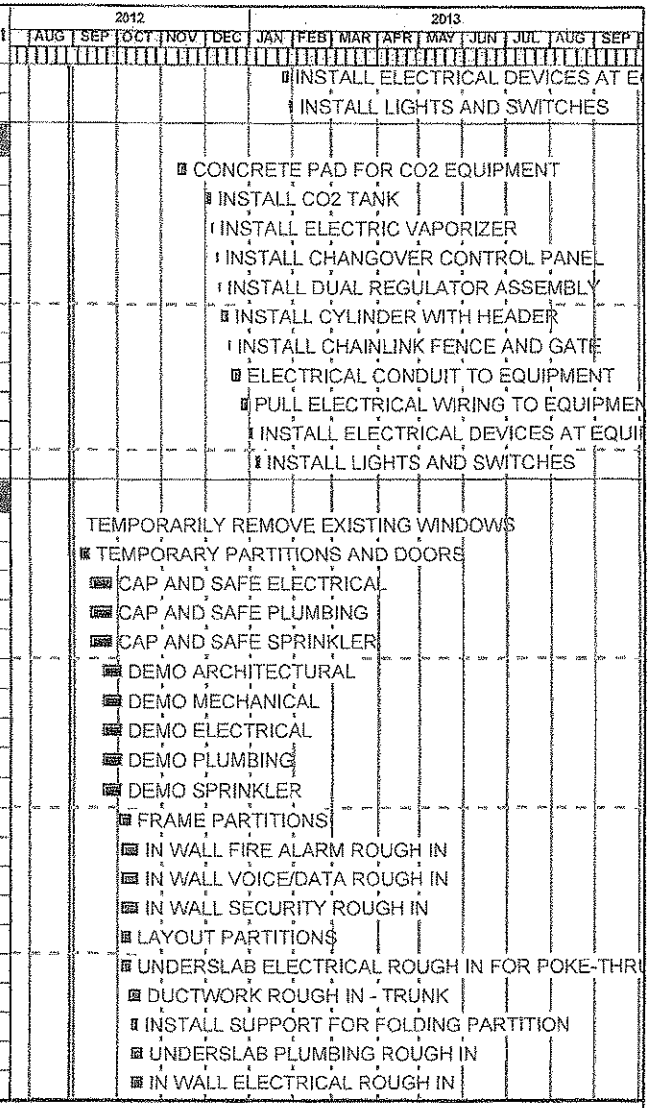

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	8A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI, PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
B1460	INSTALL HOLLOW METAL FRAMES	5	5	16OCT12	22OCT12	DOOR
B1820	PULL VOICE/DATA WIRE	5	5	16OCT12	22OCT12	OWNR
B1840	PULL SECURITY WIRE	5	5	16OCT12	22OCT12	OWNR
B1900	PULL FIRE ALARM WIRE	5	5	16OCT12	22OCT12	FIRE
B1400	ABOVE CEILING SPRINKLER ROUGH IN	7	7	18OCT12	26OCT12	SPRK
B1440	IN WALL BLOCKING	1	1	19OCT12	19OCT12	DRYW
B1580	IN WALL ELECTRICAL INSPECTION	1	1	19OCT12	19OCT12	OWNR
B1560	IN WALL PLUMBING ROUGH IN	3	3	19OCT12	23OCT12	PLBG
B1800	PULL ELECTRICAL WIRE	5	5	19OCT12	25OCT12	ELEC
B1620	FRAMING INSPECTION	1	1	22OCT12	22OCT12	OWNR
B1640	INSTALL FIRST SIDE DRYWALL	5	5	23OCT12	29OCT12	DRYW
B1380	ABOVE CEILING PLUMBING ROUGH IN	7	7	23OCT12	31OCT12	PLBG
B1940	INSTALL VOICE/DATA DEVICES	8	8	23OCT12	01NOV12	ELEC
B1320	ABOVE CEILING ELECTRICAL ROUGH IN	10	10	23OCT12	05NOV12	ELEC
B1340	ABOVE CEILING FIRE ALARM ROUGH IN	10	10	23OCT12	05NOV12	FIRE
B1360	ABOVE CEILING SECURITY ROUGH IN	10	10	23OCT12	05NOV12	SECU
B1600	IN WALL PLUMBING INSPECTION	1	1	24OCT12	24OCT12	OWNR
B1920	INSTALL ELECTRICAL DEVICES	8	8	26OCT12	06NOV12	ELEC
B2160	SPRINKLER HYDROSTATIC TEST AND INSPECTION	1	1	29OCT12	29OCT12	OWNR
B1680	INSTALL INSULATION	2	2	30OCT12	31OCT12	INSU
B1660	FRAME DRYWALL CEILINGS AND BULKHEADS	5	5	30OCT12	05NOV12	DRYW
B1700	INSULATION INSPECTION	1	1	01NOV12	01NOV12	OWNR
B1720	INSTALL SECOND SIDE DRYWALL	4	4	02NOV12	07NOV12	DRYW
B2580	INSTALL WOOD DOORS	3	3	06NOV12	08NOV12	DOOR
B2600	INSTALL HARDWARE	4	4	06NOV12	09NOV12	DOOR
B1740	TAPE AND FINISH	7	7	08NOV12	16NOV12	DRYW
B2640	INSTALL GLASS AT BORROW LIGHTS	1	1	09NOV12	09NOV12	ELEC
B1760	INSTALL ACOUSTICAL SEALANT	2	2	19NOV12	20NOV12	DRYW
B1780	PRIME AND FIRST COAT PAINT	4	4	19NOV12	22NOV12	PAIN
B1300	INSTALL AIR TERMINAL BOXES	5	5	20NOV12	26NOV12	MECH
B1880	INSTALL FIRE ALARM PANEL	2	2	23NOV12	26NOV12	FIRE
B1960	INSTALL CEILING GRID	5	5	27NOV12	03DEC12	CLGT
B1860	MECHANICAL CONTROL WIRING	10	10	27NOV12	10DEC12	MECH
B2000	INSTALL GRILLES, REGISTERS, AND DIFFUSERS	5	5	29NOV12	05DEC12	MECH
B2020	INSTALL LIGHTS	8	8	29NOV12	10DEC12	ELEC
B2040	INSTALL SPRINKLER HEADS	5	5	30NOV12	06DEC12	SPRK

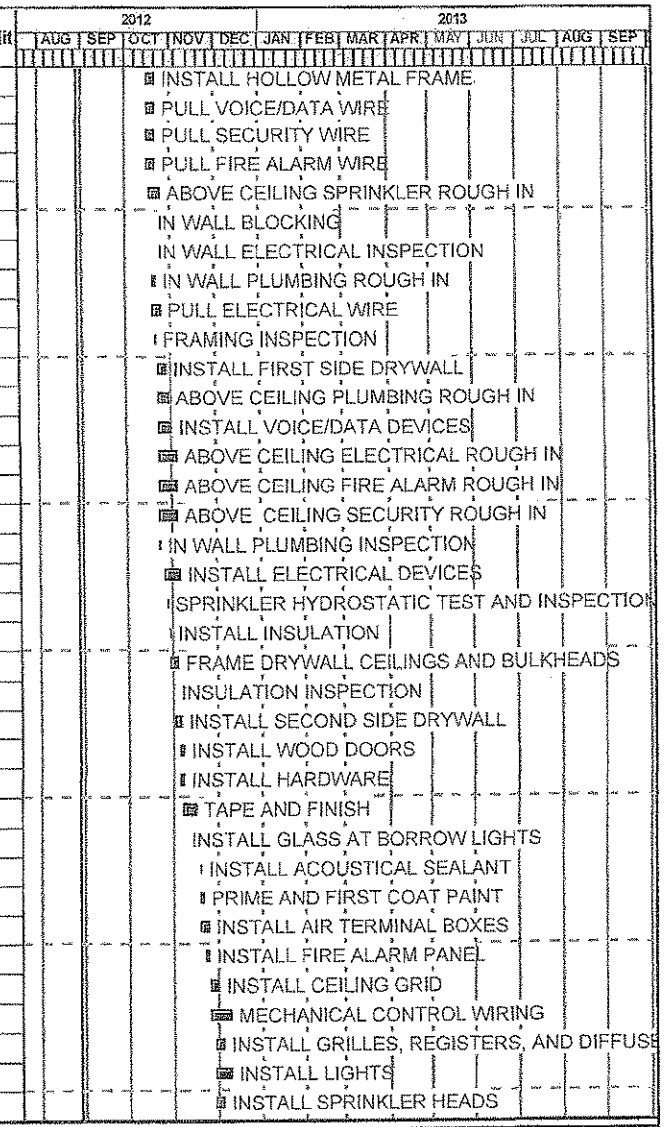

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	9A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
B2060	INSTALL PROJECTORS	1	1	04DEC12	04DEC12	PROJ
B1980	INSTALL OPERABLE PARTITION TRACK	2	2	04DEC12	05DEC12	OPER
B2080	INSTALL PROJECTOR SCREENS	1	1	05DEC12	05DEC12	PROJ
B2100	ABOVE CEILING MECHANICAL INSPECTION	1	1	06DEC12	06DEC12	OWNR
B2140	ABOVE CEILING PLUMBING INSPECTION	1	1	06DEC12	06DEC12	OWNR
B2120	ABOVE CEILING ELECTRICAL INSPECTION	1	1	11DEC12	11DEC12	OWNR
B2180	ABOVE CEILING BUILDING INSPECTION	1	1	11DEC12	11DEC12	OWNR
B2200	INSTALL DRYWALL CEILINGS AND BULKHEADS	4	4	12DEC12	17DEC12	DRYW
B2220	INSTALL CEILING TILE	4	4	12DEC12	17DEC12	CLGT
B2240	POINT UP WALLS	3	3	18DEC12	20DEC12	DRYW
B2320	INSTALL FIRE ALARM DEVICES	3	3	21DEC12	27DEC12	FIRE
B2260	FINAL PAINT	5	5	21DEC12	31DEC12	PAIN
B2400	INST MILLWORK/CASEWORK AT COFFEE	5	5	27DEC12	03JAN13	MILL
B2820	FINAL FIRE MARSHALL INSPECTION	1	1	28DEC12	28DEC12	OWNR
B2540	INSTALLVISUAL DISPLAY CABINET AT CONFERENCE	2	2	02JAN13	03JAN13	ARCH
B2660	INSTALL SIGNAGE	2	2	02JAN13	03JAN13	SIGN
B2280	INSTALL ELECTRICAL COVER PLATES	5	5	02JAN13	08JAN13	ELEC
B2300	INSTALL VOICE/DATA DEVICES & COVER PLATES	5	5	02JAN13	08JAN13	OWNR
B2340	INSTALL THERMOSTATS	5	5	02JAN13	08JAN13	ELEC
B2360	INSTALL CARD READERS	5	5	02JAN13	08JAN13	OWNR
B2380	INSTALL CARPET	7	7	02JAN13	10JAN13	CARP
B2440	INSTALL MILLWORK AT BREAKROOM	5	5	04JAN13	10JAN13	MILL
B2560	INSTALL SOUND ABSORBING WALL UNITS AT	5	5	04JAN13	10JAN13	DRYW
B2350	TESTING OF VOICE/DATA PORTS	5	5	09JAN13	15JAN13	OWNR
B2720	TEST AND BALANCE	10	10	09JAN13	22JAN13	MECH
B2460	INSTALL SINKS	2	2	11JAN13	14JAN13	PLBG
B2500	INSTALL OPERABLE PARTITION	3	3	11JAN13	15JAN13	OPER
B2620	FRAMELESS GLASS DOOR AND HARDWARE	3	3	11JAN13	15JAN13	DOOR
B2420	INSTALL VINYL COMPOSITION TILE	4	4	11JAN13	16JAN13	FLRG
B2520	DEMOUNTABLE PARTITIONS	7	7	11JAN13	21JAN13	DEMP
B2730	TENANT REVIEW & ACCEPTANCE OF SECURITY/TELE	5	5	16JAN13	22JAN13	OWNR
B2480	INSTALL VINYL BASE	3	3	17JAN13	21JAN13	FLRG
B2760	FINAL ELECTRICAL INSPECTION	1	1	22JAN13	22JAN13	OWNR
B2780	FINAL PLUMBING INSPECTION	1	1	22JAN13	22JAN13	OWNR
B2700	FINAL CLEAN	3	3	22JAN13	24JAN13	FORR
B2800	FINAL BUILDING INSPECTION	1	1	23JAN13	23JAN13	OWNR

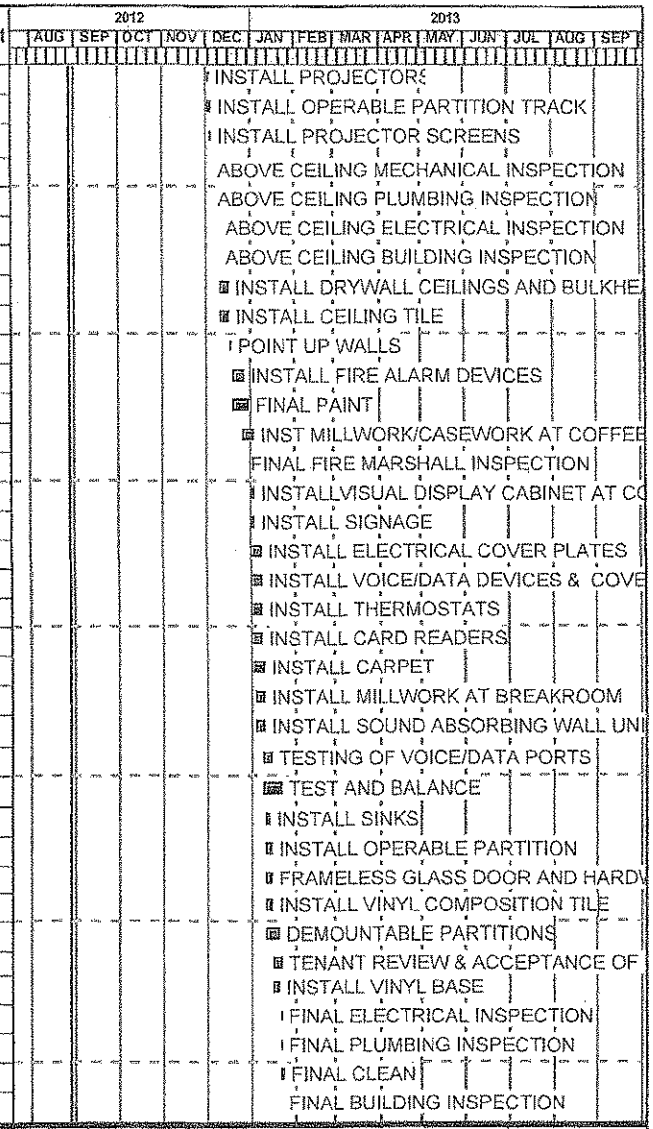

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	10A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
B2740	COMMISSIONING	5	5	23JAN13	29JAN13	MECH
B2680	PUNCHLIST	15	15	30JAN13	19FEB13	FORR
Build Units A						
A1000	TEMPORARILY REMOVE EXISTING WINDOWS	1	1	06SEP12	06SEP12	WIND
A1020	TEMPORARY PARTITIONS AND DOORS	3	3	07SEP12	11SEP12	DOOR
A1040	CAP AND SAFE MECHANICAL	10	10	12SEP12	25SEP12	MECH
A1060	CAP AND SAFE ELECTRICAL	10	10	12SEP12	25SEP12	ELEC
A1080	CAP AND SAFE PLUMBING	10	10	12SEP12	25SEP12	PLBG
A1100	CAP AND SAFE SPRINKLER	10	10	12SEP12	25SEP12	SPRK
A1120	DEMO ARCHITECTURAL	10	10	26SEP12	09OCT12	DEMO
A1140	DEMO MECHANICAL	10	10	10OCT12	23OCT12	DEMO
A1160	DEMO ELECTRICAL	10	10	10OCT12	23OCT12	DEMO
A1180	DEMO PLUMBING	10	10	10OCT12	23OCT12	DEMO
A1200	DEMO SPRINKLER	10	10	10OCT12	23OCT12	DEMO
A1220	LAYOUT PARTITIONS	6	6	24OCT12	31OCT12	DRYW
A1240	BELOW SLAB WASTE ROUGH IN	10	10	01NOV12	14NOV12	MECH
A1260	DUCTWORK ROUGH IN	15	15	01NOV12	21NOV12	MECH
A1540	FRAME PARTITIONS	10	10	02NOV12	15NOV12	DRYW
A1580	INSTALL HOLLOW METAL FRAMES	10	10	07NOV12	20NOV12	DOOR
A1600	IN WALL LAB WATER ROUGH IN	10	10	14NOV12	27NOV12	MECH
A1620	IN WALL LAB GAS ROUGH IN	10	10	14NOV12	27NOV12	MECH
A1640	IN WALL ELECTRICAL ROUGH IN	10	10	14NOV12	27NOV12	ELEC
A1660	IN WALL FIRE ALARM ROUGH IN	10	10	14NOV12	27NOV12	FIRE
A1680	IN WALL VOICE/DATA ROUGH IN	10	10	14NOV12	27NOV12	OWNR
A1700	IN WALL SECURITY ROUGH IN	10	10	14NOV12	27NOV12	OWNR
A1720	IN WALL PLUMBING ROUGH IN	10	10	15NOV12	28NOV12	PLBG
A1380	ABOVE CEILING LAB WATER PIPE ROUGH IN	20	20	15NOV12	12DEC12	MECH
A1400	ABOVE CEILING LAB GAS ROUGH IN	20	20	15NOV12	12DEC12	MECH
A1420	ABOVE CEILING ELECTRICAL ROUGH IN	20	20	15NOV12	12DEC12	ELEC
A1460	ABOVE CEILING FIRE ALARM ROUGH IN	20	20	15NOV12	12DEC12	FIRE
A1480	ABOVE CEILING SECURITY ROUGH IN	20	20	15NOV12	12DEC12	SECU
A1280	INSTALL AIR TERMINAL UNITS	15	15	20NOV12	10DEC12	MECH
A1560	IN WALL BLOCKING	5	5	22NOV12	28NOV12	DRYW
A1500	ABOVE CEILING SPRINKLER ROUGH IN	20	20	22NOV12	19DEC12	SPRK
A1740	IN WALL ELECTRICAL INSPECTION	1	1	28NOV12	28NOV12	OWNR
A2000	PULL ELECTRICAL WIRE	10	10	28NOV12	11DEC12	ELEC

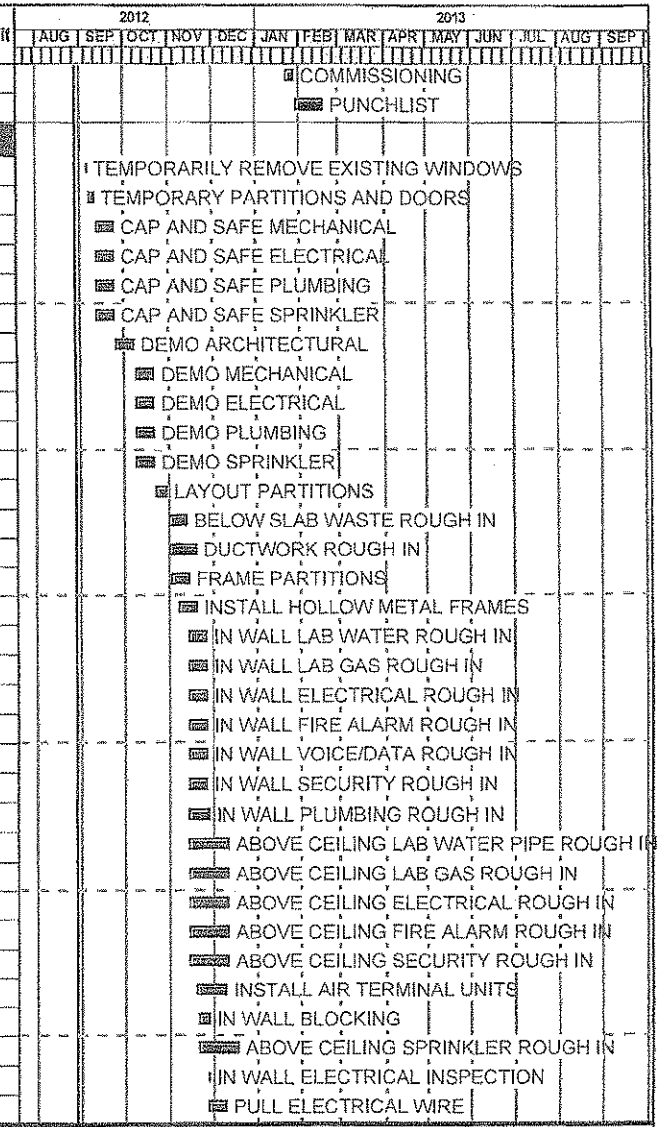

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	11A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
A2020	PULL VOICE/DATA WIRE	10	10	28NOV12	11DEC12	OWNR
A2040	PULL SECURITY WIRE	10	10	28NOV12	11DEC12	OWNR
A2100	PULL FIRE ALARM WIRE	10	10	28NOV12	11DEC12	FIRE
A1760	IN WALL PLUMBING INSPECTION	1	1	29NOV12	29NOV12	OWNR
A1780	FRAMING INSPECTION	1	1	29NOV12	29NOV12	OWNR
A1440	CABLE TRAY ROUGH IN	5	5	29NOV12	05DEC12	ELEC
A1520	ABOVE CEILING LAB WASTE VENT ROUGH IN	20	20	29NOV12	28DEC12	MECH
A1800	INSTALL FIRST SIDE DRYWALL	7	7	30NOV12	10DEC12	DRYW
A1300	HYDRONIC PIPE ROUGH IN	10	10	04DEC12	17DEC12	MECH
A1820	INSTALL INSULATION	7	7	06DEC12	14DEC12	INSU
A1320	INSTALL FAN COILS	5	5	11DEC12	17DEC12	ELEC
A2060	PULL MECHANICAL CONTROL WIRE	10	10	11DEC12	26DEC12	MECH
A2120	INSTALL ELECTRICAL DEVICES	7	7	12DEC12	20DEC12	ELEC
A2140	INSTALL VOICE/DATA DEVICES	7	7	12DEC12	20DEC12	OWNR
A1840	INSULATION INSPECTION	1	1	17DEC12	17DEC12	OWNR
A1340	REFRIGERANT PIPE ROUGH IN	5	5	18DEC12	26DEC12	MECH
A1360	ABOVE CEILING CONDENSATE ROUGH IN	5	5	18DEC12	26DEC12	MECH
A1860	SECOND SIDE DRYWALL	7	7	18DEC12	28DEC12	DRYW
A1880	TAPE AND FINISH	10	10	18DEC12	03JAN13	DRYW
A2320	SPRINKLER HYDROSTATIC TEST AND INSPECTION	1	1	20DEC12	20DEC12	OWNR
A2300	ABOVE CEILING PLUMBING INSPECTION	1	1	27DEC12	27DEC12	OWNR
A1940	PRIME AND FIRST COAT PAINT	5	5	27DEC12	03JAN13	PAIN
A1900	INSTALL ACOUSTICAL SEALANT	3	3	31DEC12	03JAN13	DRYW
A1920	FIRESTOPPING	5	5	31DEC12	07JAN13	MECH
A2160	INSTALL OVERHEAD SERVICE CARRIER SUPPORT	5	5	31DEC12	07JAN13	MECH
A2180	INSTALL CEILING GRID	8	8	03JAN13	14JAN13	CLGT
A1960	INSTALL ELECTRICAL TRANSFORMER	3	3	04JAN13	08JAN13	ELEC
A2080	INSTALL FIRE ALARM PANEL	3	3	04JAN13	08JAN13	FIRE
A2200	INSTALL GRILLES, REGISTERS, AND DIFFUSERS	8	8	09JAN13	18JAN13	MECH
A2220	INSTALL LIGHTS	10	10	09JAN13	22JAN13	ELEC
A2240	INSTALL SPRINKLER HEADS	4	4	15JAN13	18JAN13	SPRK
A1980	INSTALL ELECTRICAL PANELS	5	5	16JAN13	22JAN13	ELEC
A2260	ABOVE CEILING MECHANICAL INSPECTION	1	1	21JAN13	21JAN13	OWNR
A2280	ABOVE CEILING ELECTRICAL INSPECTION	1	1	23JAN13	23JAN13	OWNR
A2340	ABOVE CEILING BUILDING INSPECTION	1	1	23JAN13	23JAN13	OWNR
A2360	INSTALL CEILING TILE	7	7	24JAN13	01FEB13	CLGT

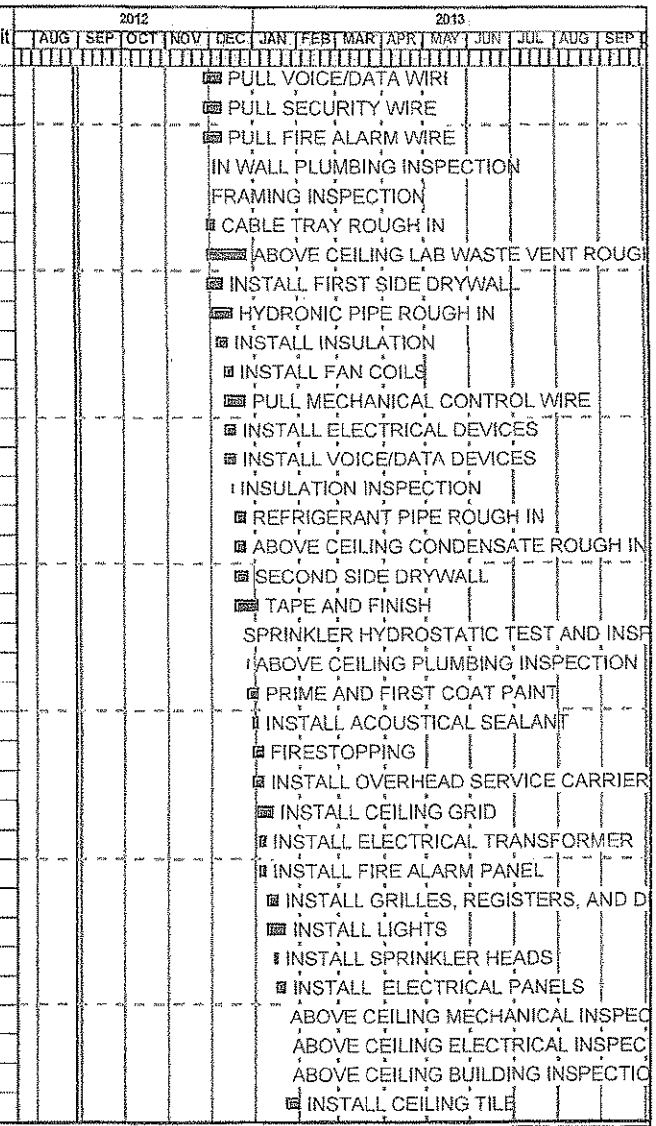

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	12A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
A2600	INSTALL OVERHEAD SERVICE CARRIERS	10	10	24JAN13	06FEB13	MECH
A2520	INSTALL VINYL COMPOSITION TILE	7	7	29JAN13	06FEB13	FLRG
A2380	POINT UP WALLS	4	4	31JAN13	05FEB13	DRYW
A2920	INSTALL EMERGENCY SHOWERS	3	3	04FEB13	06FEB13	PLBG
A2400	FINAL PAINT	5	5	06FEB13	12FEB13	PAIN
A2540	SHEET VINYL	2	2	07FEB13	08FEB13	FLRG
A2620	INSTALL LABORATORY CASEWORK CORES	5	5	07FEB13	13FEB13	CASE
A2560	INSTALL CARPET	2	2	11FEB13	12FEB13	CARP
A3000	INSTALL FIRE EXTINGUISHER CABINETS	2	2	13FEB13	14FEB13	FIRE
A3020	INSTALL SIGNAGE	2	2	13FEB13	14FEB13	SIGN
A2420	INSTALL ELECTRICAL COVER PLATES	4	4	13FEB13	18FEB13	ELEC
A2440	INSTALL VOICE/DATA COVER PLATES	4	4	13FEB13	18FEB13	OWNR
A3040	INSTALL WALL/CORNER GUARDS	4	4	13FEB13	18FEB13	DRYW
A2460	INSTALL FIRE ALARM DEVICES	5	5	13FEB13	19FEB13	FIRE
A2480	INSTALL THERMOSTATS	5	5	13FEB13	19FEB13	ELEC
A2500	INSTALL CARD READERS	5	5	13FEB13	19FEB13	OWNR
A2650	INSTALL LABORATORY CABINETS AND COUNTERS	20	20	13FEB13	12MAR13	CASE
A2680	INSTALL LAB GAS ROUGH IN AT CASEWORK	15	15	20FEB13	12MAR13	MECH
A2700	INSTALL LAB WASTE ROUGH IN AT CASEWORK	15	15	20FEB13	12MAR13	MECH
A2720	INSTALL LAB WASTE ROUGH IN AT CASEWORK	15	15	20FEB13	12MAR13	MECH
A2740	ELECTRICAL ROUGH IN AT CASEWORK	15	15	20FEB13	12MAR13	ELEC
A2760	VOICE/DATA ROUGH IN AT CASEWORK	15	15	20FEB13	12MAR13	OWNR
A2660	LAB GAS CYLINDER RESTRAINT	2	2	13MAR13	14MAR13	MECH
A2580	INSTALL VINYL BASE	3	3	13MAR13	15MAR13	FLRG
A2640	INSTALL FUME HOODS	3	3	13MAR13	15MAR13	CASE
A2780	INSTALL LAB GAS TURRETS AT CASEWORK	5	5	13MAR13	19MAR13	MECH
A2800	PLUMBING FIXTURES AT CASEWORK	5	5	13MAR13	19MAR13	PLBG
A2630	INSTALL LABORATORY SHELVING AND TRIM	10	10	13MAR13	26MAR13	CASE
A2880	ELECTRICAL SURFACE METAL RACEWAY DEVICES	10	10	13MAR13	26MAR13	ELEC
A2900	INSTALL LAB EQUIPMENT	4	4	27MAR13	01APR13	CASE
A2820	INSTALL ELECTRICAL DEVICES/COVERS AT	5	5	27MAR13	02APR13	ELEC
A2840	INSTALL VOICE/DATA DEVICES/COVERS AT	5	5	27MAR13	02APR13	OWNR
A2860	INSTALL LIGHTS AT CASEWORK	5	5	27MAR13	02APR13	ELEC
A2940	INSTALL DOORS	5	5	02APR13	08APR13	DOOR
A2960	INSTALL HARDWARE	5	5	02APR13	08APR13	DOOR
A3160	FINAL ELECTRICAL INSPECTION	1	1	03APR13	03APR13	OWNR

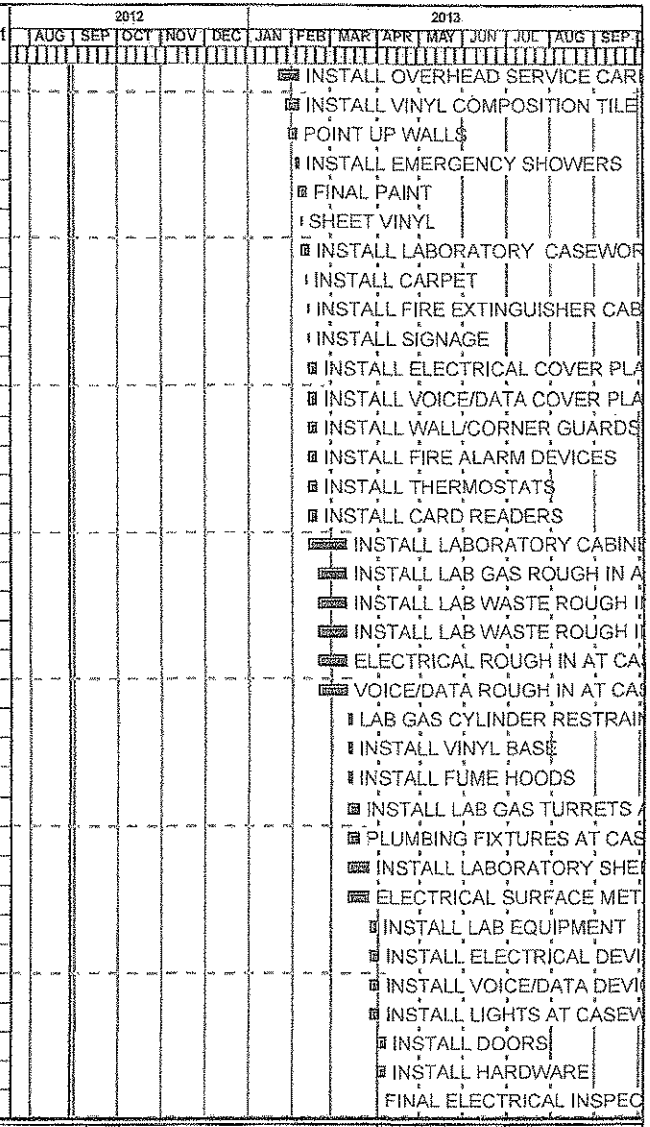

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	13A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
A3180	FINAL PLUMBING INSPECTION	1	1	03APR13	03APR13	OWNR
A2870	TESTING OF VOICE/DATA PORTS	5	5	03APR13	09APR13	OWNR
A2980	INSTALL GLASS AT BORROW LIGHTS	3	3	09APR13	11APR13	ELEC
A3190	REVIEW AND ACCEPTANCE OF SECURITY/ TELE DATA	5	5	10APR13	16APR13	OWNR
A3220	FINAL FIRE MARSHALL INSPECTION	1	1	12APR13	12APR13	OWNR
A3080	FINAL CLEAN	5	5	12APR13	18APR13	FORR
A3100	TEST AND BALANCE	10	10	12APR13	25APR13	MECH
A3200	FINAL BUILDING INSPECTION	1	1	15APR13	15APR13	OWNR
A3120	COMMISSIONING	20	20	26APR13	23MAY13	MECH
A3140	VALIDATION	10	10	10MAY13	23MAY13	OWNR
A3060	PUNCHLIST	10	10	28MAY13	10JUN13	FORR
BUILDING ROOF						
AR1000	LAYOUT MECHANICAL ROOF EQUIPMENT	3	3	02OCT12	04OCT12	MECH
AR1020	TEMPOPRARILY REMOVE AREAS OF EXISTING ROOF	5	5	05OCT12	11OCT12	ROOF
AR1080	ROOF HATCH	2	2	12OCT12	15OCT12	ROOF
AR1100	INSTALL WINDOW CLEANING ANCHORS	5	5	12OCT12	18OCT12	WIND
AR1040	POUR HOUSEKEEPING PADS	3	3	16OCT12	18OCT12	CONC
AR1200	SET CONDENSING UNITS	2	2	27NOV12	28NOV12	MECH
AR1060	MECHANICAL EQUIPMENT CURBS	3	3	27NOV12	29NOV12	MECH
AR1180	SET HUMIDIFIERS	2	2	30NOV12	03DEC12	MECH
AR1140	SET EXHAUST FANS	5	5	11JAN13	17JAN13	ELEC
AR1160	INSTALL VARIABLE FREQUENCY DRIVES	2	2	18JAN13	21JAN13	ELEC
AR1120	SET ROOF TOP UNITS	10	10	22JAN13	04FEB13	MECH
AR1260	ROOF PENETRATIONS/OPENINGS FOR PIPE/DUCT	2	2	05FEB13	06FEB13	MECH
AR1240	NATURAL GAS ROUGH IN	7	7	07FEB13	15FEB13	MECH
AR1220	DUCTWORK ROUGH IN	8	8	07FEB13	18FEB13	MECH
AR1280	INSTALL STEEL FRAMING FOR SCREEN WALL	10	10	19FEB13	04MAR13	SSTL
AR1320	ROOF PATCHING	12	12	19FEB13	06MAR13	ROOF
AR1300	SCREEN WALL PANEL	7	7	07MAR13	15MAR13	LOUV
BUILDING MECHANICAL ROOM						
AM1000	LAYOUT EQUIPMENT IN MECHANICAL ROOM	2	2	05OCT12	08OCT12	MECH
AM1160	INSTALL FLOOR DRAINS	4	4	09OCT12	12OCT12	PLBG
AM1020	POUR HOUSEKEEPING PADS	3	3	16OCT12	18OCT12	CONC
AM1060	SET WATER HEATERS	4	4	27NOV12	30NOV12	MECH
AM1100	INSTALL EXPANSION TANK	2	2	03DEC12	04DEC12	MECH

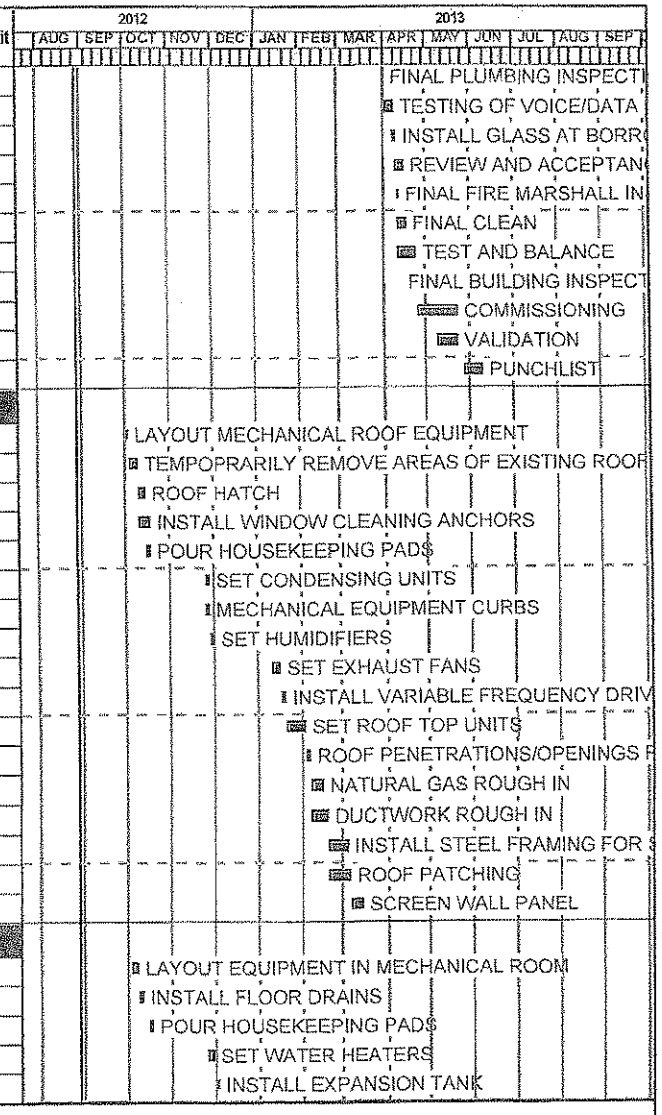

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	14A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
AM1061	DOMESTIC HOT WATER WATER PIPING	7	7	03DEC12	11DEC12	MECH
AM1040	INSTALL TRANSFORMER AND ELECTRICAL PANEL	4	4	11DEC12	14DEC12	ELEC
AM1080	INSTALL RECIRCULATING PUMP	2	2	12DEC12	13DEC12	MECH
AM1140	INSTALL AIR TERMINAL UNITS BACKFLOW	2	2	12DEC12	13DEC12	MECH
AM1120	SET REVERSE OSMOSIS AND DEIONIZATION EQUIP.	10	10	02JAN13	15JAN13	MECH
AM1130	REVERSE OSMOSIS PIPING ROUGH IN	10	10	16JAN13	29JAN13	MECH
BUILDING C ROOF AREA AT PENTHOUSE EAST						
CRA1300	CONDENS. UNIT/EXHAUST FAN/INTAKE HOOD CURBS	2	2	24OCT12	25OCT12	MECH
CRA1340	REFRIGERANT PIPE PENETRATIONS	1	1	26OCT12	26OCT12	MECH
CRA1320	DUCTWORK SUPPORT FOR FLUE STACK	2	2	26OCT12	29OCT12	MECH
CRA1000	TEMPORARILY REMOVE AREAS OF EXISTING ROOF	2	2	30OCT12	31OCT12	ROOF
CRA1020	X RAY EXISTING CONCRETE FOR CURB	2	2	01NOV12	02NOV12	CONC
CRA1040	CONCRETE CURB	5	5	05NOV12	09NOV12	CONC
CRA1060	TEMPORARILY REMOVE AREAS OF EXISTING BRICK	2	2	13NOV12	14NOV12	MASN
CRA1120	MECHANICAL UNIT PLATFORMS	3	3	13NOV12	15NOV12	MECH
CRA1140	ROOF SCREEN SUPPORT	5	5	13NOV12	19NOV12	SSTL
CRA1080	X RAY EXISTING CONCRETE FOR STEEL	2	2	15NOV12	16NOV12	CONC
CRA1100	INSTALL STRUCTURAL STEEL AND METAL DECK	10	10	19NOV12	30NOV12	SSTL
CRA1360	INSTALL WINDOW CLEANING ANCHORS	4	4	20NOV12	23NOV12	WIND
CRA1380	PEDESTAL BASE FOR WINDOW WASH OUTRIGGERS	4	4	20NOV12	23NOV12	WIND
CRA1400	INSTALL ROOF DRAINS	2	2	03DEC12	04DEC12	MECH
CRA1180	INSTALL METAL STUD FRAMING	10	10	03DEC12	14DEC12	DRYW
CRA1200	INSTALL EXTERIOR HOLLOW METAL DOOR FRAMES	3	3	10DEC12	12DEC12	DOOR
CRA1220	INSTALL EXTERIOR SHEATHING	5	5	17DEC12	21DEC12	ROOF
CRA1240	INSTALL VAPOR BARRIER	3	3	26DEC12	28DEC12	ROOF
CRA1260	INSTALL MASONRY VENEER	10	10	31DEC12	14JAN13	MASN
CRA1440	INSTALL EXTERIOR DOORS AND HARDWARE	2	2	15JAN13	16JAN13	DOOR
CRA1460	INSTALL WINDOWS	2	2	15JAN13	16JAN13	WIND
CRA1280	INSTALL WOOD BLOCKING AT TOP OF WALLS	3	3	15JAN13	17JAN13	DRYW
CRA1420	INSTALL ROOFING	5	5	18JAN13	24JAN13	ROOF
CRA1480	REMOVE EXISTING INTAKE LOUVER	2	2	25JAN13	28JAN13	DEMO
CRA1520	REMOVE EXISTING ROOF DRAINS	2	2	29JAN13	30JAN13	ROOF
CRA1540	REMOVE EXISTING WINDOW CLEANING ANCHORS	2	2	31JAN13	01FEB13	WIND
CRA1560	REMOVE EXISTING LIGHTNING PROTECTION	2	2	04FEB13	05FEB13	ELEC
CRA1500	REMOVE EXISTING ROOFING	3	3	06FEB13	08FEB13	ROOF
CRA1580	REMOVE EXISTING MASONRY WALL	5	5	11FEB13	15FEB13	MASN

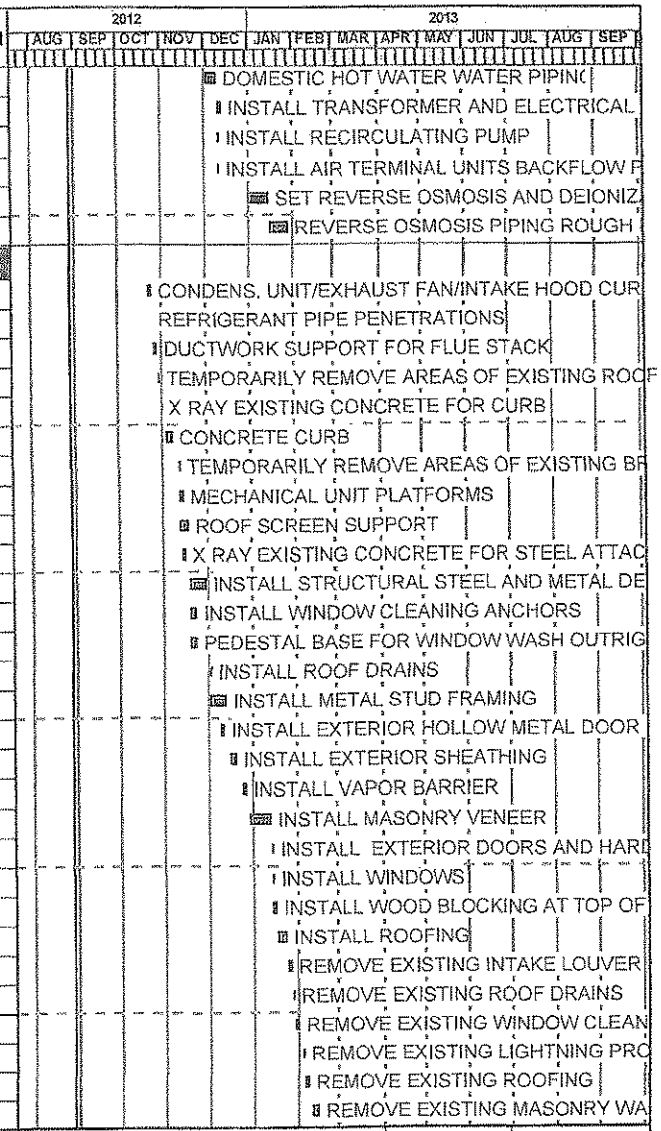

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	15A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
CRA1600	DISCONNECT AND SAFE ELECTRICAL	3	3	18FEB13	20FEB13	ELEC
CRA1620	REMOVE EXISTING MECHANICAL EQUIPMENT	3	3	21FEB13	25FEB13	MECH
CRA1640	REMOVE EXISTING DUCTWORK	3	3	26FEB13	28FEB13	MECH
CRA1920	INSTALL ELECTRICAL PANELS	2	2	01MAR13	04MAR13	ELEC
CRA1660	POUR HOUSEKEEPING PADS	4	4	01MAR13	06MAR13	CONC
CRA1680	INSTALL AIR HANDLING UNIT	6	6	07MAR13	14MAR13	MECH
CRA1700	INSTALL EXHAUST FANS	6	6	15MAR13	22MAR13	ELEC
CRA1780	ROUGH IN DUCTWORK	8	8	15MAR13	26MAR13	MECH
CRA1720	INSTALL UNIT HEATERS	4	4	25MAR13	28MAR13	ELEC
CRA1820	ROUGH IN STORM AND WASTE PIPING	3	3	27MAR13	29MAR13	MECH
CRA1800	ROUGH IN MECHANICAL PIPING	8	8	27MAR13	05APR13	MECH
CRA1900	ELECTRICAL CONDUIT ROUGH IN	10	10	27MAR13	09APR13	ELEC
CRA1740	INSTALL CONDENSING UNITS	4	4	29MAR13	03APR13	MECH
CRA1840	INSTALL VACUUM EQUIPMENT	3	3	01APR13	03APR13	MECH
CRA1860	ROUGH IN LAB WATER PIPE	2	2	04APR13	05APR13	MECH
CRA1760	INSTALL FAN COIL UNIT	4	4	04APR13	09APR13	MECH
CRA1880	ROUGH IN SPRINKLER PIPE	6	6	08APR13	15APR13	SPRK
CRA1160	SCREEN WALL PANEL	5	5	10APR13	16APR13	LOUV
CRA1940	PULL ELECTRICAL WIRING	6	6	10APR13	17APR13	ELEC
CRA2000	INSTALL FIRE ALARM CONDUIT	5	5	17APR13	23APR13	FIRE
CRA1960	INSTALL ELECTRICAL DEVICES	3	3	18APR13	22APR13	ELEC
CRA1980	INSTALL LIGHT FIXTURES	3	3	18APR13	22APR13	ELEC
CRA2020	INSTALL FIRE ALARM WIRING	5	5	24APR13	30APR13	FIRE
CRA2040	INSTALL FIRE ALARM DEVICES	4	4	01MAY13	06MAY13	FIRE
CRA2060	INSATLL DRYWAL AT ROOMS 404 405 AND 406	4	4	07MAY13	10MAY13	DRYW
CRA2080	TAPE AND FINISH AT ROOMS 404 405 AND 406	6	6	13MAY13	20MAY13	DRYW
CRA2100	PAINT AT ROOMS 404 405 AND 406	3	3	21MAY13	23MAY13	PAIN
CRA2102C	SEAL CONCRETE FLOORS	2	2	24MAY13	27MAY13	CONC
[illegible]	[illegible]					
CRB1000	TEMPORARILY REMOVE AREAS OF EXISTING ROOF	2	2	01NOV12	02NOV12	ROOF
CRB1020	REMOVE EXHAUST FANS AND DUCTWORK	4	4	01NOV12	06NOV12	MECH
CRB1040	X RAY EXISTING CONCRETE FOR CURB	2	2	05NOV12	06NOV12	CONC
CRB1060	PLACE CONCRETE CURB	5	5	12NOV12	16NOV12	CONC
CRB1080	TEMPORARILY REMOVE AREAS OF EXISTING BRICK	2	2	15NOV12	16NOV12	MASN
CRB1140	INSTALL MECHANICAL UNIT PLATFORMS	6	6	16NOV12	23NOV12	MECH
CRB1100	X RAY EXISTING CONCRETE FOR STEEL	2	2	19NOV12	20NOV12	CONC

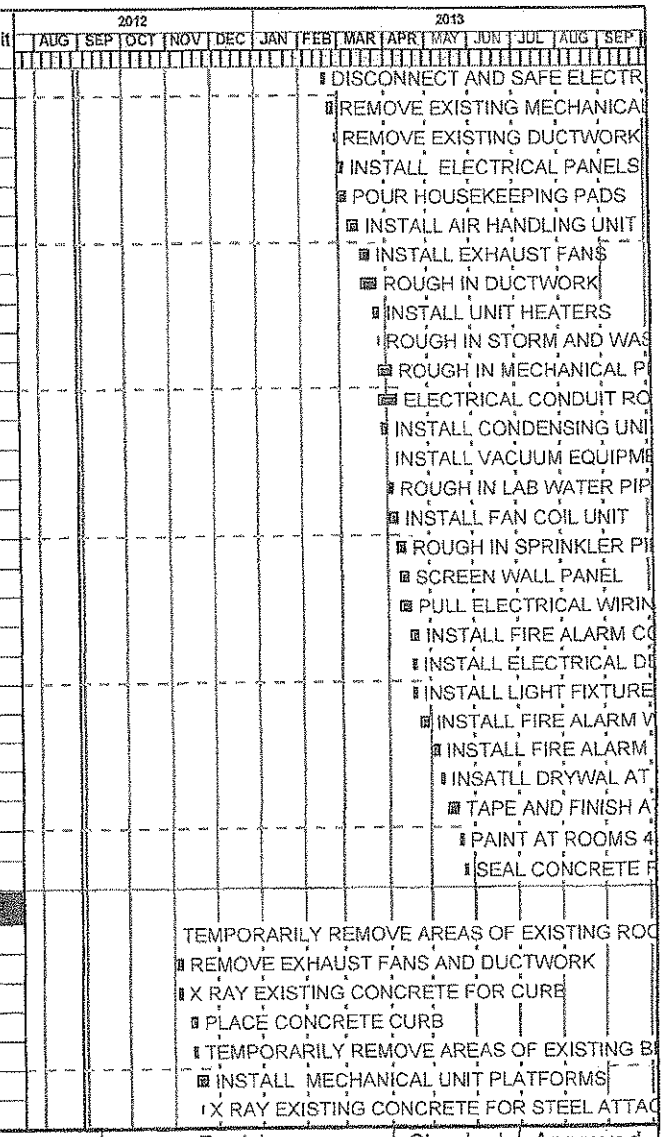

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	16A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
CRB1160	INSTALL ROOF SCREEN SUPPORT	7	7	20NOV12	28NOV12	SSTL
CRB1380	INSTALL ROOF DRAINS	2	2	29NOV12	30NOV12	MECH
CRB1340	INSTALL WINDOW CLEANING ANCHORS	4	4	29NOV12	04DEC12	WIND
CRB1360	INSTALL PEDESTAL BASE FOR WINDOW WASH	4	4	29NOV12	04DEC12	WIND
CRB1120	INSTALL STRUCTURAL STEEL AND METAL DECK	10	10	03DEC12	14DEC12	SSTL
CRB1200	INSTALL METAL STUD FRAMING	10	10	17DEC12	02JAN13	DRYW
CRB1220	INSTALL EXTERIOR HOLLOW METAL DOOR FRAMES	3	3	26DEC12	28DEC12	DOOR
CRB1240	INSTALL EXTERIOR SHEETHIING	5	5	03JAN13	09JAN13	ROOF
CRB1260	INSTALL VAPOR BARRIER	3	3	10JAN13	14JAN13	ROOF
CRB1280	INSTALL MASONRY VENEER	10	10	15JAN13	28JAN13	MASN
CRB1300	INSTALL WOOD BLOCKING AT TOP OF WALLS	2	2	29JAN13	30JAN13	DRYW
CRB1420	INSTALL EXTERIOR DOORS AND HARDWARE	2	2	29JAN13	30JAN13	DOOR
CRB1440	INSTALL WINDOWS	3	3	29JAN13	31JAN13	WIND
CRB1320	INSTALL AIR INTAKE HOOD CURB	1	1	31JAN13	31JAN13	MECH
CRB1400	INSTALL ROOFING	5	5	01FEB13	07FEB13	ROOF
CRB1480	REMOVE EXISTING ROOF DRAINS	2	2	08FEB13	11FEB13	MECH
CRB1500	REMOVE EXISTING WINDOW CLEANING ANCHORS	2	2	08FEB13	11FEB13	WIND
CRB1520	REMOVE EXISTING LIGHTNING PROTECTION	2	2	08FEB13	11FEB13	ELEC
CRB1460	REMOVE EXISTING ROOFING	3	3	08FEB13	12FEB13	ROOF
CRB1540	REMOVE EXISTING MASONRY WALL	4	4	08FEB13	13FEB13	MASN
CRB1620	REMOVE EXISTING LOUVERS	2	2	14FEB13	15FEB13	MECH
CRB1560	DISCONNECT AND SAFE ELECTRICAL	3	3	14FEB13	18FEB13	ELEC
CRB1580	REMOVE EXISTING MECHANICAL EQUIPMENT	3	3	19FEB13	21FEB13	MECH
CRB1600	REMOVE EXISTING DUCTWORK	3	3	22FEB13	26FEB13	MECH
CRB1640	REMOVE EXISTING AIR COMPRESSOR	2	2	27FEB13	28FEB13	MECH
CRB1660	POUR HOUSEKEEPING PADS	5	5	01MAR13	07MAR13	CONC
CRB1680	INSTALL AIR HANDLING UNIT	4	4	08MAR13	13MAR13	MECH
CRB1700	INSTALL EXHAUST FANS	5	5	14MAR13	20MAR13	MECH
CRB1860	ROUGH IN DUCTWORK	8	8	14MAR13	25MAR13	MECH
CRB1720	INSTALL FAN COIL UNIT	3	3	21MAR13	25MAR13	MECH
CRB1740	INSTALL CONDENSING UNITS	4	4	26MAR13	29MAR13	MECH
CRB1900	ROUGH IN STORM AND WASTE PIPING	4	4	26MAR13	29MAR13	MECH
CRB2040	INSTALL FIRE ALARM CONDUIT	5	5	26MAR13	01APR13	FIRE
CRB1880	ROUGH IN MECHANICAL PIPING	15	15	26MAR13	15APR13	MECH
CRB1980	ELECTRICAL CONDUIT ROUGH IN	15	15	26MAR13	15APR13	ELEC
CRB1760	INSTALL BOILERS	5	5	01APR13	05APR13	MECH

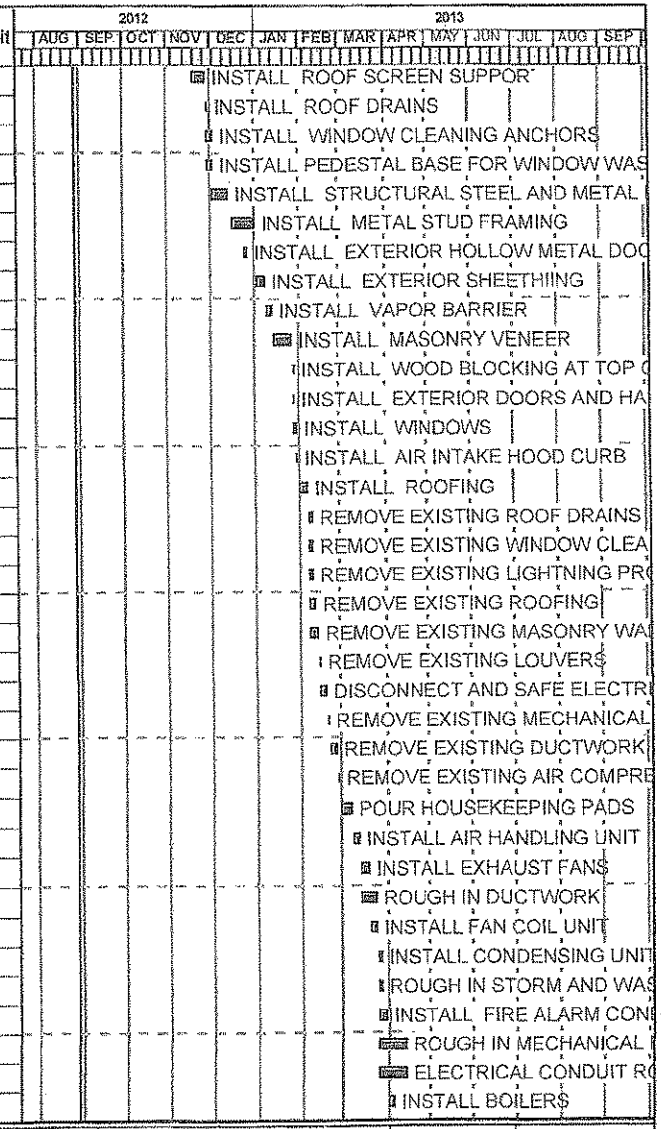

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	17A
© Primavera Systems, Inc.	

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
CRB2060	INSTALL FIRE ALARM WIRING	5	5	02APR13	08APR13	FIRE
CRB1920	INSTALL WATER HEATER	3	3	08APR13	10APR13	MECH
CRB1800	INSTALL PUMPS	4	4	08APR13	11APR13	MECH
CRB1780	INSTALL BOILER FLUES THROUGH ROOF	5	5	08APR13	12APR13	MECH
CRB2080	INSTALL FIRE ALARM DEVICES	4	4	09APR13	12APR13	FIRE
CRB1820	INSTALL TANKS	4	4	12APR13	17APR13	MECH
CRB1960	ROUGH IN SPRINKLER PIPE	6	6	16APR13	23APR13	SPRK
CRB2000	PULL ELECTRICAL WIRING	10	10	16APR13	29APR13	ELEC
CRB1940	ROUGH IN LAB WATER PIPE	5	5	18APR13	24APR13	MECH
CRB1180	INSTALL SCREEN WALL PANEL	7	7	18APR13	26APR13	
CRB2100	INSTALL DRYWALL AT ROOMS 401 AND 402	3	3	25APR13	29APR13	DRYW
CRB2020	INSTALL ELECTRICAL DEVICES	4	4	30APR13	03MAY13	ELEC
CRB2120	TAPE AND FINISH AT ROOMS 401 AND 402	5	5	30APR13	06MAY13	DRYW
CRB2140	PAINT AT ROOOMS 401 AND 402	2	2	07MAY13	08MAY13	PAIN
CRB2160	INSTALL CEILING AT ROOMS 401 AND 402	3	3	09MAY13	13MAY13	CLGT
CRB2180	INSTALL CARPET AND BASE AT ROOMS 401 AND 402	3	3	14MAY13	16MAY13	CARP
CRB2200	INST KICHENETTE & SYSTEMS FURNITURE AT ROOM	4	4	17MAY13	22MAY13	
CRB2220	SEAL CONCRETE FLOORS	2	2	23MAY13	24MAY13	CONC
C3W1000	TEMPORARILY REMOVE EXISTING WINDOWS	2	2	07SEP12	10SEP12	WIND
C3W1020	TEMPORARY PARTITIONS AND DOORS	4	4	11SEP12	14SEP12	DOOR
C3W1040	CAP AND SAFE MECHANICAL	7	7	17SEP12	25SEP12	MECH
C3W1060	CAP AND SAFE ELECTRICAL	7	7	17SEP12	25SEP12	ELEC
C3W1080	CAP AND SAFE PLUMBING	7	7	17SEP12	25SEP12	PLBG
C3W1100	CAP AND SAFE SPRINKLER	7	7	17SEP12	25SEP12	SPRK
C3W1120	DEMO LABORATORY CASEWORK	7	7	26SEP12	04OCT12	DEMO
C3W1140	DEMO ARCHITECTURAL	10	10	01OCT12	12OCT12	DEMO
C3W1160	DEMO MECHANICAL	10	10	15OCT12	26OCT12	DEMO
C3W1180	DEMO ELECTRICAL	10	10	15OCT12	26OCT12	DEMO
C3W1200	DEMO PLUMBING	10	10	15OCT12	26OCT12	DEMO
C3W1220	DEMO SPRINKLER	10	10	15OCT12	26OCT12	DEMO
C3W1240	LAYOUT PARTITIONS	5	5	29OCT12	02NOV12	DRYW
C3W1280	INSTALL DUCTWORK ROUGH IN	10	10	01NOV12	14NOV12	MECH
C3W1260	BELOW SLAB WASTE ROUGH IN	5	5	05NOV12	09NOV12	MECH
C3W1380	INSTALL ABOVE CEILING LAB WATER ROUGH IN	12	12	08NOV12	23NOV12	MECH
C3W1400	INSTALL ABOVE CEILING LAB GAS ROUGH IN	12	12	08NOV12	23NOV12	MECH

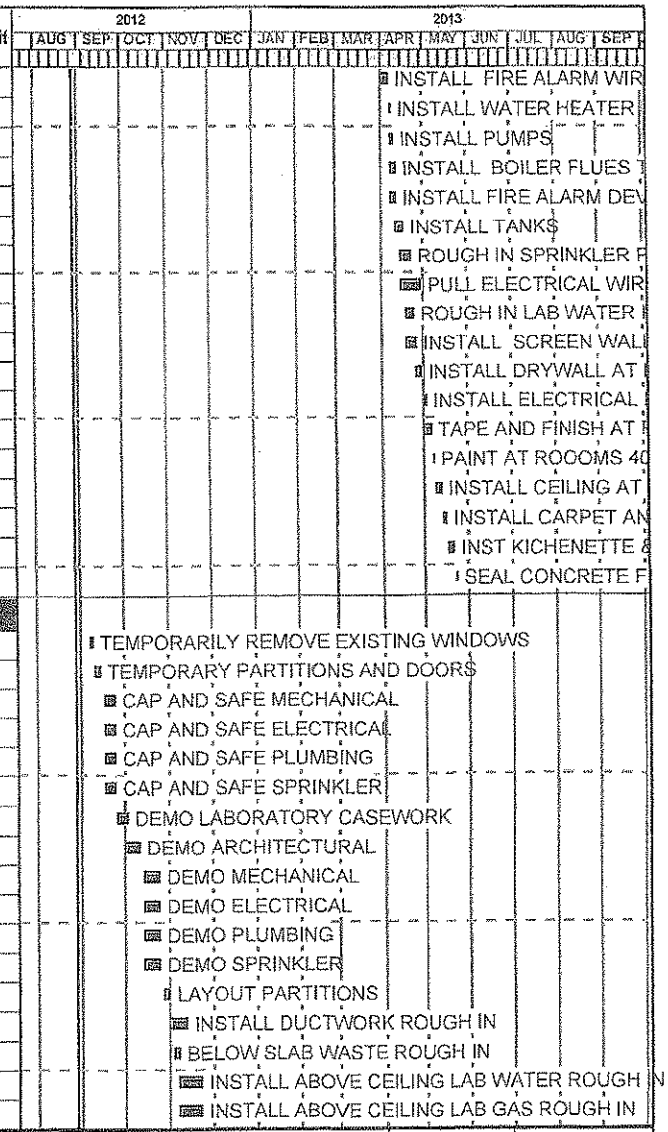

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	18A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
C3W1460	INSTALL ABOVE CEILING SECURITY ROUGH IN	12	12	08NOV12	23NOV12	SECU
C3W1500	INSTALL ABOVE CEILING LAB WASTE VENT ROUGH IN	12	12	08NOV12	23NOV12	MECH
C3W1480	INSTALL ABOVE CEILING SPRINKLER ROUGH IN	5	5	15NOV12	21NOV12	SPRK
C3W1520	FRAME PARTITIONS	7	7	15NOV12	23NOV12	DRYW
C3W1420	INSTALL ABOVE CEILING ELECTRICAL ROUGH IN	12	12	15NOV12	30NOV12	ELEC
C3W1560	INSTALL HOLLOW METAL FRAMES	5	5	19NOV12	23NOV12	DOOR
C3W1320	INSTALL FAN COIL UNITS	4	4	20NOV12	23NOV12	MECH
C3W1300	INSTALL AIR TERMINAL UNITS	10	10	20NOV12	03DEC12	MECH
C3W1580	IN WALL LAB WATER ROUGH IN	5	5	21NOV12	27NOV12	MECH
C3W1600	IN WALL LAB GAS ROUGH IN	5	5	21NOV12	27NOV12	MECH
C3W1620	IN WALL ELECTRICAL ROUGH IN	8	8	21NOV12	30NOV12	ELEC
C3W1640	IN WALL FIRE ALARM ROUGH IN	8	8	21NOV12	30NOV12	FIRE
C3W1660	IN WALL VOICE/DATA ROUGH IN	8	8	21NOV12	30NOV12	ELEC
C3W1680	IN WALL SECURITY ROUGH IN	8	8	21NOV12	30NOV12	SECU
C3W2300	SPRINKLER HYDROSTATIC TEST AND INSPECTION	2	2	22NOV12	23NOV12	OWNR
C3W1440	INSTALL ABOVE CEILING FIRE ALARM ROUGH IN	12	12	22NOV12	07DEC12	FIRE
C3W1360	INSTALL ABOVE CEILING CONDENSATE ROUGH IN	4	4	26NOV12	29NOV12	MECH
C3W1720	IN WALL PLUMBING INSPECTION	2	2	28NOV12	29NOV12	OWNR
C3W1700	IN WALL ELECTRICAL INSPECTION	2	2	03DEC12	04DEC12	OWNR
C3W1540	IN WALL BLOCKING	3	3	03DEC12	05DEC12	DRYW
C3W1980	PULL ELECTRICAL WIRE	6	6	03DEC12	10DEC12	ELEC
C3W2000	PULL VOICE/DATA WIRE	6	6	03DEC12	10DEC12	ELEC
C3W2020	PULL SECURITY WIRE	6	6	03DEC12	10DEC12	SECU
C3W2060	PULL FIRE ALARM WIRE	6	6	03DEC12	10DEC12	FIRE
C3W1340	HYDRONIC PIPE ROUGH IN	8	8	04DEC12	13DEC12	MECH
C3W2040	PULL MECHANICAL CONTROL WIRE	8	8	04DEC12	13DEC12	MECH
C3W1740	FRAMING INSPECTION	2	2	06DEC12	07DEC12	OWNR
C3W1760	INSTALL FIRST SIDE DRYWALL	4	4	10DEC12	13DEC12	DRYW
C3W2080	INSTALL ELECTRICAL DEVICES	5	5	11DEC12	17DEC12	ELEC
C3W2100	INSTALL VOICE/DATA DEVICES	5	5	11DEC12	17DEC12	ELEC
C3W1780	INSTALL INSULATION	4	4	14DEC12	19DEC12	INSU
C3W2420	INSTALL VOICE/DATA COVER PLATES	3	3	18DEC12	20DEC12	ELEC
C3W1800	INSULATION INSPECTION	2	2	20DEC12	21DEC12	OWNR
C3W1820	INSTALL SECOND SIDE DRYWALL	4	4	26DEC12	31DEC12	DRYW
C3W1880	INSTALL ACOUSTICAL SEALANT	2	2	02JAN13	03JAN13	DRYW
C3W1900	INSTALL FIRESTOPPING	2	2	02JAN13	03JAN13	MECH

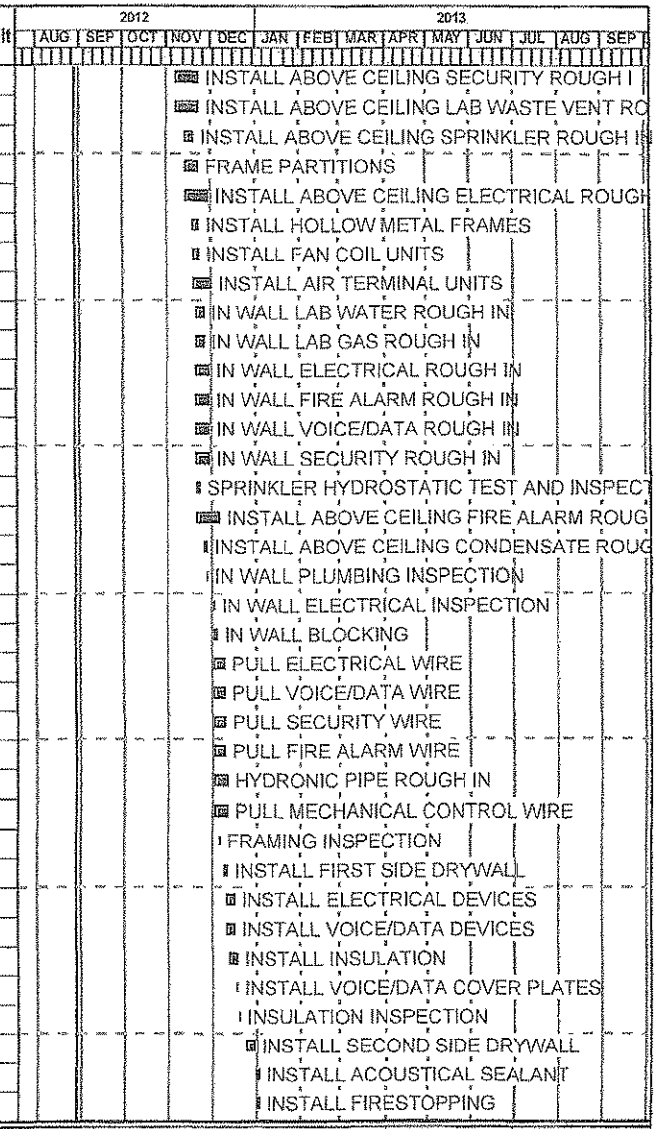

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	19A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
C3W2160	INSTALL FRAMING FOR DRYWALL CEILING	2	2	02JAN13	03JAN13	DRYW
C3W2120	INSTALL OVERHEAD SERVICE CARRIER SUPPORT	3	3	02JAN13	04JAN13	MECH
C3W1840	TAPE AND FINISH	7	7	02JAN13	10JAN13	DRYW
C3W1920	PRIME AND FIRST COAT PAINT	5	5	11JAN13	17JAN13	PAIN
C3W1860	INSTALL COLD BOXES	10	10	11JAN13	24JAN13	MECH
C3W1940	INSTALL ELECTRICAL PANELS	2	2	18JAN13	21JAN13	ELEC
C3W1960	INSTALL FIRE ALARM PANEL	2	2	18JAN13	21JAN13	FIRE
C3W2140	INSTALL CEILING GRID	5	5	18JAN13	24JAN13	CLGT
C3W2180	INSTALL GRILLES, REGISTERS, AND DIFFUSERS	6	6	23JAN13	30JAN13	MECH
C3W2200	INSTALL LIGHTS	9	9	23JAN13	04FEB13	ELEC
C3W2220	INSTALL SPRINKLER HEADS	3	3	25JAN13	29JAN13	SPRK
C3W2240	ABOVE CEILING MECHANICAL INSPECTION	2	2	31JAN13	01FEB13	OWNR
C3W2320	ABOVE CEILING BUILDING INSPECTION	2	2	31JAN13	01FEB13	OWNR
C3W2260	ABOVE CEILING ELECTRICAL INSPECTION	2	2	05FEB13	06FEB13	OWNR
C3W2280	ABOVE CEILING PLUMBING INSPECTION	2	2	05FEB13	06FEB13	OWNR
C3W2340	INSTALL CEILING TILE	5	5	07FEB13	13FEB13	CLGT
C3W2500	INSTALL VINYL COMPOSITION TILE	5	5	11FEB13	15FEB13	FLRG
C3W2360	POINT UP WALLS	4	4	14FEB13	19FEB13	DRYW
C3W2580	INSTALL OVERHEAD SERVICE CARRIERS	4	4	14FEB13	19FEB13	MECH
C3W2680	INSTALL EMERGENCY SHOWERS	5	5	14FEB13	20FEB13	PLBG
C3W2380	FINAL PAINT	5	5	20FEB13	26FEB13	PAIN
C3W2540	INSTALL CARPET	2	2	27FEB13	28FEB13	CARP
C3W2960	INSTALL SIGNAGE	2	2	27FEB13	28FEB13	SIGN
C3W2980	INSTALL FIRE EXTINGUISHER CABINETS	2	2	27FEB13	28FEB13	FIRE
C3W2400	INSTALL ELECTRICAL COVER PLATES	3	3	27FEB13	01MAR13	ELEC
C3W3000	INSTALL WALL/CORNER GUARDS	3	3	27FEB13	01MAR13	DRYW
C3W2520	INSTALL SHEET VINYL	4	4	27FEB13	04MAR13	FLRG
C3W2440	INSTALL FIRE ALARM DEVICES	5	5	27FEB13	05MAR13	FIRE
C3W2460	INSTALL THERMOSTATS	5	5	27FEB13	05MAR13	ELEC
C3W2480	INSTALL CARD READERS	5	5	27FEB13	05MAR13	OWNR
C3W2560	INSTALL VINYL BASE	3	3	01MAR13	05MAR13	FLRG
C3W2600	INSTALL LABORATORY CASEWORK CORES	2	2	05MAR13	06MAR13	CASE
C3W2630	INSTALL LABORATORY CABINETS AND COUNTERS	6	6	07MAR13	14MAR13	CASE
C3W2640	INSTALL LAB GAS ROUGH IN AT CASEWORK	7	7	13MAR13	21MAR13	MECH
C3W2660	INSTALL LAB WASTE ROUGH IN AT CASEWORK	7	7	13MAR13	21MAR13	MECH
C3W2680	INSTALL LAB WASTE ROUGH IN AT CASEWORK	7	7	13MAR13	21MAR13	MECH

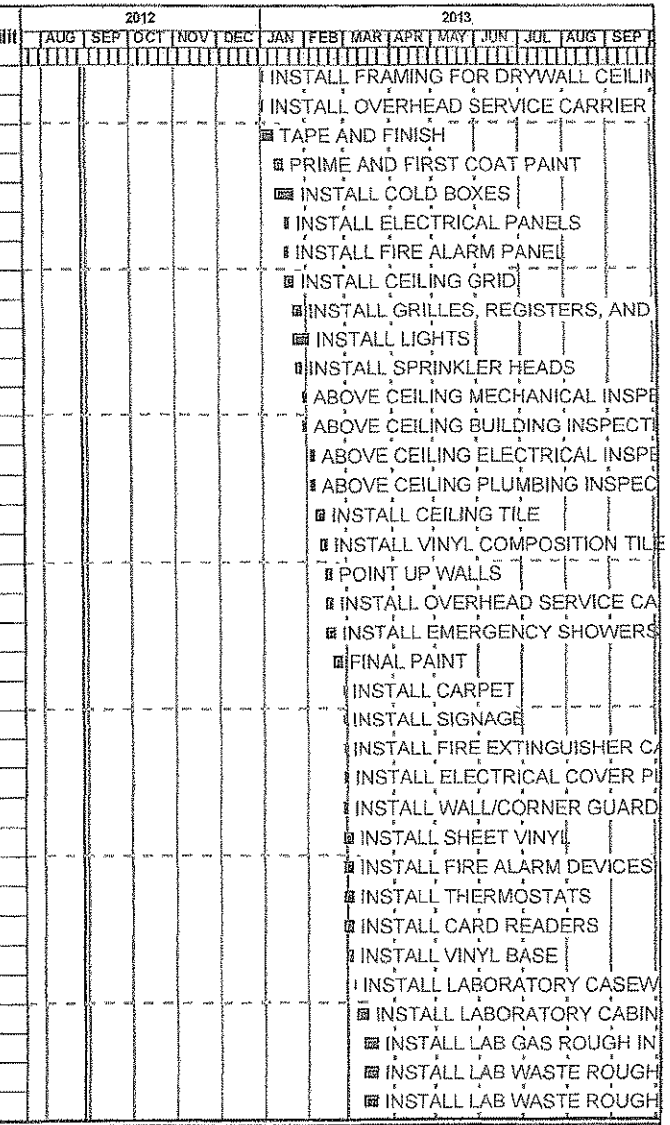

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	20A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
C3W2700	ELECTRICAL ROUGH IN AT CASEWORK	7	7	13MAR13	21MAR13	ELEC
C3W2720	INSTALL VOICE/DATA ROUGH IN AT CASEWORK	7	7	13MAR13	21MAR13	ELEC
C3W2620	INSTALL FUME HOODS	3	3	15MAR13	19MAR13	CASE
C3W2840	INSTALL ELECTRICAL SURFACE METAL RACEWAY	10	10	15MAR13	28MAR13	ELEC
C3W2740	INSTALL LAB GAS TURRETS AT CASEWORK	5	5	22MAR13	28MAR13	MECH
C3W2760	INSTALL PLUMBING FIXTURES AT CASEWORK	5	5	22MAR13	28MAR13	PLBG
C3W2610	INSTALL LABORATORY SHELVING AND TRIM	10	10	29MAR13	11APR13	CASE
C3W2860	INSTALL LAB EQUIPMENT	3	3	12APR13	16APR13	CASE
C3W2780	INSTALL ELECTRICAL DEVICES/COVERS AT	5	5	12APR13	18APR13	ELEC
C3W2800	INSTALL VOICE/DATA DEVICES/COVERS AT	5	5	12APR13	18APR13	ELEC
C3W2820	INSTALL LIGHTS AT CASEWORK	5	5	12APR13	18APR13	ELEC
C3W2900	INSTALL DOORS	5	5	17APR13	23APR13	DOOR
C3W2920	INSTALL HARDWARE	5	5	17APR13	23APR13	DOOR
C3W3120	FINAL ELECTRICAL INSPECTION	2	2	19APR13	22APR13	OWNR
C3W3140	FINAL PLUMBING INSPECTION	2	2	19APR13	22APR13	OWNR
C3W2830	TESTING OF VOICE/DATA PORTS	5	5	19APR13	25APR13	OWNR
C3W2940	INSTALL GLASS AT BORROW LIGHTS	3	3	24APR13	26APR13	ELEC
C3W3040	FINAL CLEAN	5	5	24APR13	30APR13	FORR
C3W2950	REVIEW AND ACCEPTANCE OF SECURITY/ TELE DATA	5	5	26APR13	02MAY13	OWNR
C3W3180	FINAL FIRE MARSHALL INSPECTION	2	2	29APR13	30APR13	OWNR
C3W3060	TEST AND BALANCE	7	7	29APR13	07MAY13	MECH
C3W3160	FINAL BUILDING INSPECTION	2	2	01MAY13	02MAY13	OWNR
C3W3080	COMMISSIONING	15	15	08MAY13	28MAY13	MECH
C3W3100	VALIDATION	7	7	20MAY13	28MAY13	OWNR
C3W3020	PUNCHLIST	15	15	29MAY13	18JUN13	FORR
[illegible]						
C3E1000	INSTALL TEMPORARY PARTITIONS AND DOORS	5	5	17SEP12	21SEP12	DOOR
C3E1020	CAP AND SAFE MECHANICAL	7	7	24SEP12	02OCT12	MECH
C3E1040	CAP AND SAFE ELECTRICAL	7	7	24SEP12	02OCT12	ELEC
C3E1060	CAP AND SAFE PLUMBING	7	7	24SEP12	02OCT12	PLBG
C3E1080	CAP AND SAFE SPRINKLER	7	7	24SEP12	02OCT12	SPRK
C3E1100	DEMO LABORATORY CASEWORK	7	7	03OCT12	11OCT12	DEMO
C3E1120	DEMO ARCHITECTURAL	10	10	10OCT12	23OCT12	DEMO
C3E1140	DEMO MECHANICAL	10	10	16OCT12	29OCT12	DEMO
C3E1160	DEMO ELECTRICAL	10	10	16OCT12	29OCT12	DEMO
C3E1180	DEMO PLUMBING	10	10	16OCT12	29OCT12	DEMO

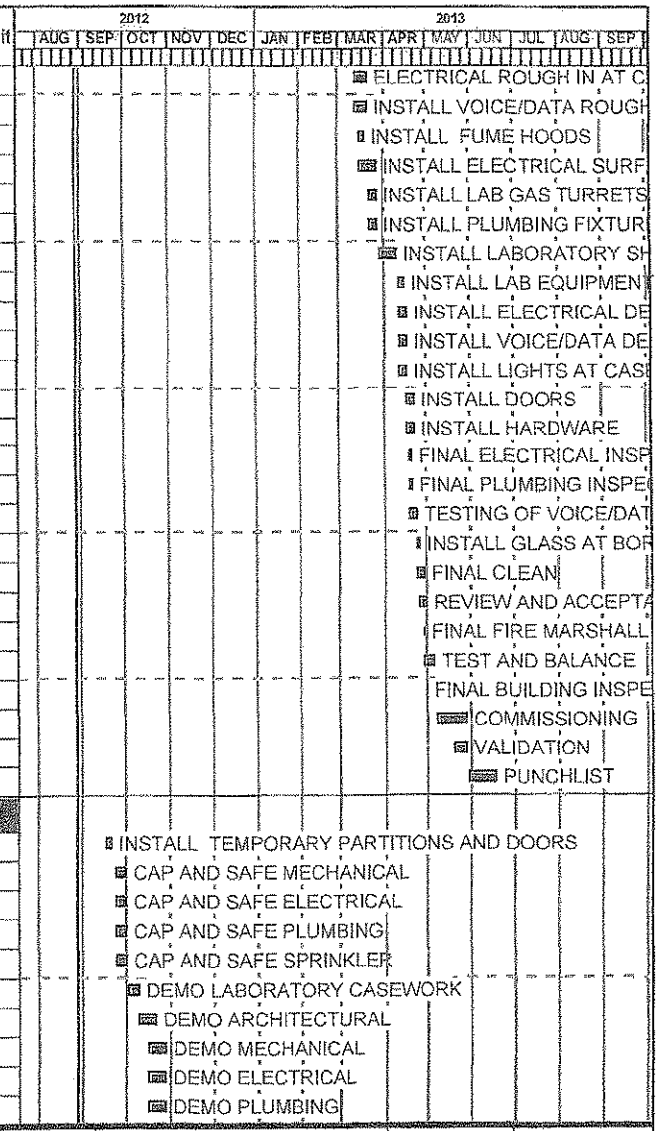

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	21A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
C3E1200	DEMO SPRINKLER	10	10	16OCT12	29OCT12	DEMO
C3E1220	INFILL RECESSED CONCRETE SLAB	2	2	30OCT12	31OCT12	CONC
C3E1240	LAYOUT PARTITIONS	5	5	30OCT12	05NOV12	DRYW
C3E1280	DUCTWORK ROUGH IN	15	15	01NOV12	21NOV12	MECH
C3E1260	BELOW SLAB WASTE ROUGH IN	5	5	06NOV12	12NOV12	MECH
C3E1520	FRAME PARTITIONS	8	8	06NOV12	15NOV12	DRYW
C3E1560	INSTALL HOLLOW METAL FRAMES	6	6	08NOV12	15NOV12	DOOR
C3E1600	IN WALL LAB GAS ROUGH IN	10	10	12NOV12	23NOV12	MECH
C3E1620	IN WALL ELECTRICAL ROUGH IN	10	10	12NOV12	23NOV12	ELEC
C3E1640	IN WALL FIRE ALRAM ROUGH IN	10	10	12NOV12	23NOV12	FIRE
C3E1660	IN WALL VOICE/DATA ROUGH IN	10	10	12NOV12	23NOV12	ELEC
C3E1680	IN WALL SECURITY ROUGH IN	10	10	12NOV12	23NOV12	SECU
C3E1580	IN WALL LAB WATER ROUGH IN	10	10	13NOV12	26NOV12	MECH
C3E1360	ABOVE CEILING CONDENSATE ROUGH IN	6	6	15NOV12	22NOV12	PLBG
C3E1380	ABOVE CEILING LAB WATER ROUGH IN	15	15	15NOV12	05DEC12	MECH
C3E1400	ABOVE CEILING LAB GAS ROUGH IN	15	15	15NOV12	05DEC12	MECH
C3E1420	ABOVE CEILING ELECTRICAL ROUGH IN	15	15	15NOV12	05DEC12	ELEC
C3E1440	ABOVE CEILING FIRE ALARM ROUGH IN	15	15	15NOV12	05DEC12	FIRE
C3E1460	ABOVE CEILING SECURITY ROUGH IN	15	15	15NOV12	05DEC12	OWNR
C3E1500	ABOVE CEILING LAB WASTE VENT ROUGH IN	15	15	15NOV12	05DEC12	MECH
C3E1320	INSTALL FANCOIL UNITS	5	5	20NOV12	26NOV12	PLBG
C3E1300	INSTALL AIR TERMINAL UNITS	15	15	20NOV12	10DEC12	MECH
C3E1700	IN WALL ELECTRICAL INSPECTION	2	2	26NOV12	27NOV12	OWNR
C3E1980	PULL ELECTRICAL WIRE	8	8	26NOV12	05DEC12	ELEC
C3E2000	PULL VOICE/DATA WIRE	8	8	26NOV12	05DEC12	OWNR
C3E2020	PULL SECURITY WIRE	8	8	26NOV12	05DEC12	OWNR
C3E2060	PULL FIRE ALARM WIRE	8	8	26NOV12	05DEC12	FIRE
C3E1720	IN WALL PLUMBING INSPECTION	2	2	27NOV12	28NOV12	OWNR
C3E1540	IN WALL BLOCKING	5	5	27NOV12	03DEC12	DRYW
C3E1740	FRAMING INSPECTION	2	2	04DEC12	05DEC12	OWNR
C3E1760	INSTALL FIRST SIDE DRYWALL	5	5	06DEC12	12DEC12	DRYW
C3E1480	ABOVE CEILING SPRINKLER ROUGH IN	7	7	06DEC12	14DEC12	SPRK
C3E2080	INSTALL ELECTRICAL DEVICES	7	7	06DEC12	14DEC12	ELEC
C3E2100	INSTALL VOICE/DATA DEVICES	7	7	06DEC12	14DEC12	OWNR
C3E1780	INSTALL INSULATION	5	5	10DEC12	14DEC12	INSU
C3E1340	HYDRONIC PIPE ROUGH IN	10	10	11DEC12	26DEC12	MECH

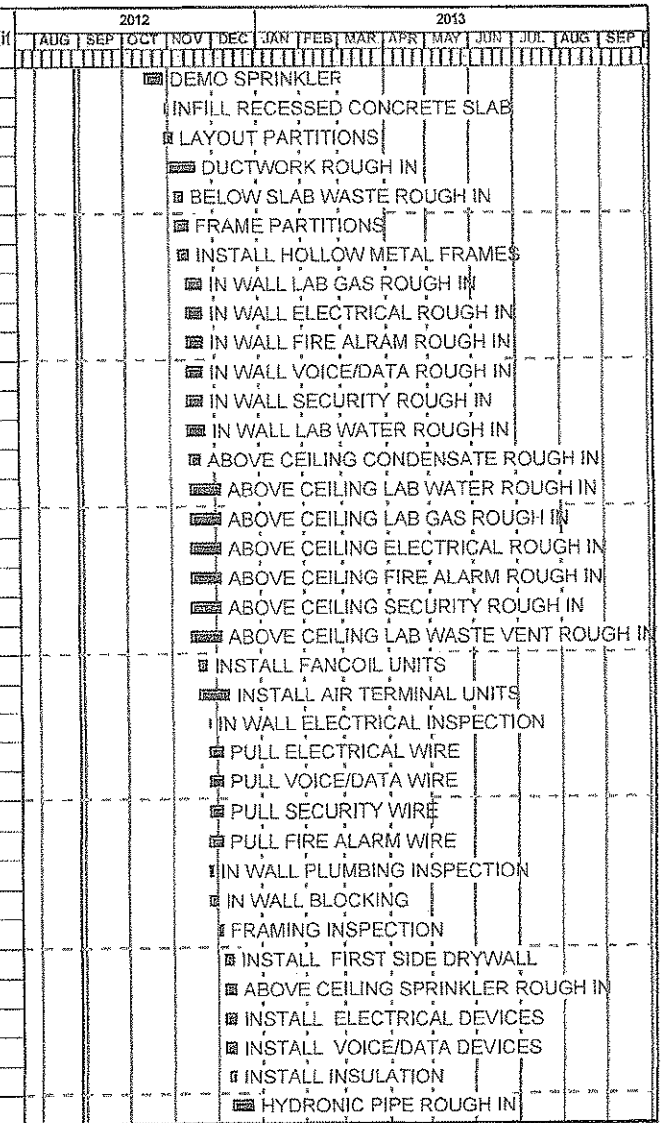

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	22A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
C3E2040	PULL MECHANICAL CONTROL WIRE	10	10	11DEC12	26DEC12	MECH
C3E1800	INSULATION INSPECTION	2	2	17DEC12	18DEC12	OWNR
C3E2300	SPRINKLER HYDROSTATIC TEST AND INSPECTION	2	2	17DEC12	18DEC12	OWNR
C3E1820	INSTALL SECOND SIDE DRYWALL	5	5	19DEC12	27DEC12	DRYW
C3E1840	TAPE AND FINISH	8	8	27DEC12	08JAN13	DRYW
C3E1880	INSTALL ACOUSTICAL SEALANT	3	3	28DEC12	02JAN13	DRYW
C3E1900	INSTALL FIRESTOPPING	3	3	28DEC12	02JAN13	MECH
C3E2120	INSTALL OVERHEAD SERVICE CARRIER SUPPORT	5	5	28DEC12	04JAN13	MECH
C3E1920	PRIME AND FIRST COAT PAINT	5	5	04JAN13	10JAN13	PAIN
C3E2140	INSTALL CEILING GRID	7	7	09JAN13	17JAN13	CLGT
C3E1860	INSTALL COLD BOXES	10	10	09JAN13	22JAN13	COLD
C3E1940	INSTALL ELECTRICAL PANELS	2	2	11JAN13	14JAN13	ELEC
C3E1960	INSTALL FIRE ALARM PANEL	2	2	11JAN13	14JAN13	FIRE
C3E2160	INSTALL FRAMING FOR DRYWALL CEILING	4	4	11JAN13	16JAN13	DRYW
C3E2220	INSTALL SPRINKLER HEADS	4	4	15JAN13	18JAN13	SPRK
C3E2180	INSTALL GRILLES, REGISTERS, AND DIFFUSERS	10	10	15JAN13	28JAN13	MECH
C3E2200	INSTALL LIGHTS	10	10	15JAN13	28JAN13	ELEC
C3E2260	ABOVE CEILING ELECTRICAL INSPECTION	2	2	21JAN13	22JAN13	OWNR
C3E2240	ABOVE CEILING MECHANICAL INSPECTION	2	2	29JAN13	30JAN13	OWNR
C3E2280	ABOVE CEILING PLUMBING INSPECTION	2	2	29JAN13	30JAN13	OWNR
C3E2320	ABOVE CEILING BUILDING INSPECTION	2	2	29JAN13	30JAN13	OWNR
C3E2340	INSTALL CEILING TILE	7	7	31JAN13	08FEB13	CLGT
C3E2580	INSTALL OVERHEAD SERVICE CARRIERS	7	7	31JAN13	08FEB13	MECH
C3E2360	POINT UP WALLS	3	3	01FEB13	05FEB13	DRYW
C3E2380	INSTALL FINAL PAINT	5	5	05FEB13	11FEB13	PAIN
C3E2500	INSTALL VINYL COMPOSITION TILE	7	7	05FEB13	13FEB13	FLRG
C3E2900	INSTALL EMERGENCY SHOWERS	5	5	11FEB13	15FEB13	PLBG
C3E2980	INSTALL SIGNAGE	2	2	12FEB13	13FEB13	SIGN
C3E3000	INSTALL FIRE EXTINGUISHER CABINETS	2	2	12FEB13	13FEB13	FIRE
C3E2400	INSTALL ELECTRICAL COVER PLATES	4	4	12FEB13	15FEB13	ELEC
C3E2420	INSTALL VOICE/DATA COVER PLATES	4	4	12FEB13	15FEB13	ELEC
C3E2520	INSTALL SHEET VINYL	4	4	12FEB13	15FEB13	FLRG
C3E2440	INSTALL FIRE ALARM DEVICES	5	5	12FEB13	18FEB13	FIRE
C3E2460	INSTALL THERMOSTATS	5	5	12FEB13	18FEB13	ELEC
C3E2480	INSTALL CARD READRES	5	5	12FEB13	18FEB13	OWNR
C3E3020	INSTALL WALL/CORNER GUARDS	5	5	12FEB13	18FEB13	DRYW

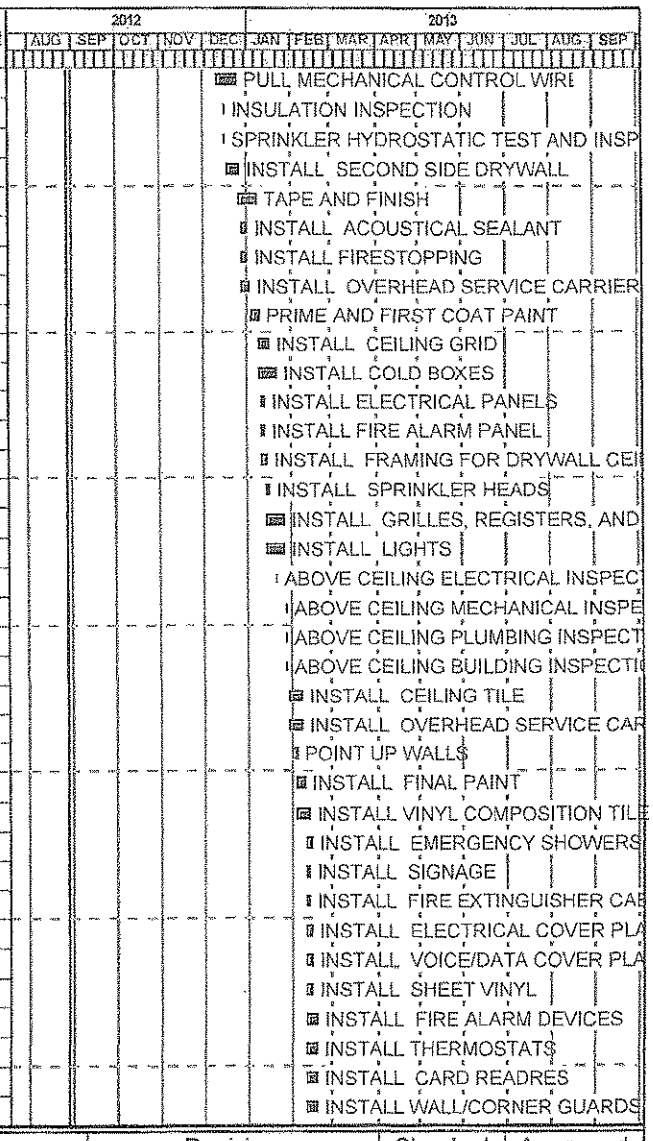

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	23A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
C3E2600	INSTALL LABORATORY CASEWORK CORES	10	10	14FEB13	27FEB13	CASE
C3E2540	INSTALL CARPET	3	3	18FEB13	20FEB13	CARP
C3E2630	INSTALL LABORATORY CABINETS AND COUNTERS	10	10	25FEB13	08MAR13	CASE
C3E2640	INSTALL LAB GAS ROUGH IN AT CASEWORK	10	10	06MAR13	19MAR13	MECH
C3E2660	INSTALL LAB WASTE ROUGH IN AT CASEWORK	10	10	06MAR13	19MAR13	MECH
C3E2680	INSTALL LAB WASTE ROUGH IN AT CASEWORK	10	10	06MAR13	19MAR13	MECH
C3E2700	ELECTRICAL ROUGH IN AT CASEWORK	10	10	06MAR13	19MAR13	ELEC
C3E2720	VOICE/DATA ROUGH IN AT CASEWORK	10	10	06MAR13	19MAR13	OWNR
C3E2620	INSTALL FUME HOODS	2	2	11MAR13	12MAR13	CASE
C3E2560	INSTALL VINYL BASE	4	4	11MAR13	14MAR13	FLRG
C3E2650	INSTALL LABORATORY SHELVING AND TRIM	5	5	11MAR13	15MAR13	CASE
C3E2740	INSTALL LAB GAS TURRETS AT CASEWORK	8	8	11MAR13	20MAR13	MECH
C3E2760	INSTALL PLUMBING FIXTURES AT CASEWORK	8	8	11MAR13	20MAR13	PLBG
C3E2840	INSTALL ELECTRICAL SURFACE METAL RACEWAY	13	13	11MAR13	27MAR13	ELEC
C3E2780	INSTALL ELECTRICAL DEVICES/COVERS AT	8	8	18MAR13	27MAR13	ELEC
C3E2800	INSTALL VOICE/DATA DEVICES/COVERS AT	8	8	18MAR13	27MAR13	OWNR
C3E2820	INSTALL LIGHTS AT CASEWORK	8	8	18MAR13	27MAR13	ELEC
C3E2860	INSTALL LAB EQUIPMENT	2	2	28MAR13	29MAR13	CASE
C3E3140	FINAL ELECTRICAL INSPECTION	2	2	28MAR13	29MAR13	OWNR
C3E3160	FINAL PLUMBING INSPECTION	2	2	28MAR13	29MAR13	OWNR
C3E3130	TESTING VOICE/DATA PORTS	5	5	28MAR13	03APR13	OWNR
C3E2920	INSTALL DOORS	7	7	01APR13	09APR13	DOOR
C3E2940	INSTALL HARDWARE	7	7	01APR13	09APR13	DOOR
C3E2930	REVIEW AND ACCEPTANCE OF SECURITY/ TELE DATA	5	5	04APR13	10APR13	OWNR
C3E2960	INSTALL GLASS AT BORROW LIGHTS	4	4	10APR13	15APR13	ELEC
C3E3200	FINAL FIRE MARSHALL INSPECTION	1	1	16APR13	16APR13	OWNR
C3E3060	FINAL CLEAN	7	7	16APR13	24APR13	FORR
C3E3080	TEST AND BALANCE	10	10	16APR13	29APR13	MECH
C3E3180	FINAL BUILDING INSPECTION	1	1	17APR13	17APR13	OWNR
C3E3100	COMMISSIONING	20	20	30APR13	27MAY13	MECH
C3E3120	VALIDATION	10	10	14MAY13	27MAY13	OWNR
C3E3040	PUNCHLIST	15	15	28MAY13	17JUN13	FORR
BUILDING CLEAN UP						
C21000	TEMPORARILY REMOVE EXISTING WINDOWS	2	2	11SEP12	12SEP12	WIND
C21020	TEMPORARY PARTITIONS AND DOORS	2	2	24SEP12	25SEP12	DOOR
C21040	CAP AND SAFE MECHANICAL	5	5	26SEP12	02OCT12	MECH

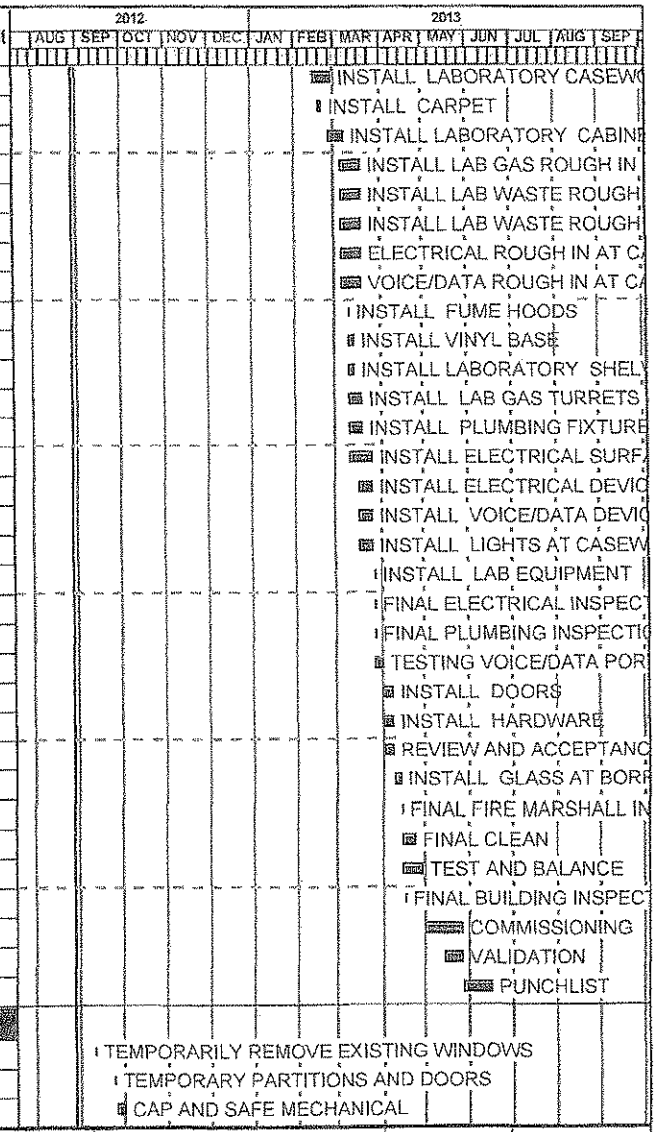

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	24A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
C21060	CAP AND SAFE ELECTRICAL	5	5	26SEP12	02OCT12	ELEC
C21080	CAP AND SAFE PLUMBING	5	5	26SEP12	02OCT12	PLBG
C21100	CAP AND SAFE SPRINKLER	5	5	26SEP12	02OCT12	SPRK
C21120	DEMO LABORATORY CASEWORK	6	6	03OCT12	10OCT12	DEMO
C21140	DEMO ARCHITECTURAL	7	7	08OCT12	16OCT12	DEMO
C21160	DEMO MECHANICAL	10	10	15OCT12	26OCT12	DEMO
C21180	DEMO ELECTRICAL	10	10	15OCT12	26OCT12	DEMO
C21200	DEMO PLUMBING	10	10	15OCT12	26OCT12	DEMO
C21220	DEMO SPRINKLER	10	10	15OCT12	26OCT12	DEMO
C21240	INFILL RECESSED CONCRETE SLAB	2	2	29OCT12	30OCT12	CONC
C21260	LAYOUT PARTITIONS	3	3	29OCT12	31OCT12	DRYW
C21280	BELOW SLAB WASTE ROUGH IN	5	5	01NOV12	07NOV12	MECH
C21300	DUCTWORK ROUGH IN	15	15	01NOV12	21NOV12	MECH
C21540	FRAME PARTITIONS	10	10	09NOV12	22NOV12	DRYW
C21400	ABOVE CEILING LAB WATER ROUGH IN	20	20	15NOV12	12DEC12	MECH
C21420	ABOVE CEILING LAB GAS ROUGH IN	20	20	15NOV12	12DEC12	MECH
C21440	ABOVE CEILING ELECTRICAL ROUGH IN	20	20	15NOV12	12DEC12	ELEC
C21460	ABOVE CEILING FIRE ALARM ROUGH IN	20	20	15NOV12	12DEC12	FIRE
C21480	ABOVE CEILING SECURITY ROUGH IN	20	20	15NOV12	12DEC12	SECU
C21520	ABOVE CEILING LAB WASTE VENT ROUGH IN	20	20	15NOV12	12DEC12	MECH
C21700	IN WALL SECURITY ROUGH IN	10	10	20NOV12	03DEC12	SECU
C21320	INSTALL AIR TERMINAL UNITS	15	15	20NOV12	10DEC12	MECH
C21600	IN WALL LAB WATER ROUGH IN	10	10	21NOV12	04DEC12	MECH
C21620	IN WALL LAB GAS ROUGH IN	10	10	21NOV12	04DEC12	MECH
C21640	IN WALL ELECTRICAL ROUGH IN	10	10	21NOV12	04DEC12	ELEC
C21660	IN WALL FIRE ALRM ROUGH IN	10	10	21NOV12	04DEC12	FIRE
C21680	IN WALL VOICE/DATA ROUGH IN	10	10	21NOV12	04DEC12	ELEC
C21580	INSTALL HOLLOW METAL FRAMES	10	10	23NOV12	06DEC12	DOOR
C21360	HYDRONIC PIPE ROUGH IN	10	10	27NOV12	10DEC12	MECH
C21560	IN WALL BLOCKING	5	5	04DEC12	10DEC12	DRYW
C22020	PULL SECURITY WIRE	8	8	04DEC12	13DEC12	SECU
C21720	IN WALL ELECTRICAL INSPECTION	1	1	05DEC12	05DEC12	OWNR
C21740	IN WALL PLUMBING INSPECTION	1	1	05DEC12	05DEC12	OWNR
C21980	PULL ELECTRICAL WIRE	8	8	05DEC12	14DEC12	ELEC
C22000	PULL VOICE/DATA WIRE	8	8	05DEC12	14DEC12	ELEC
C22060	PULL FIRE ALARM WIRE	10	10	05DEC12	18DEC12	FIRE

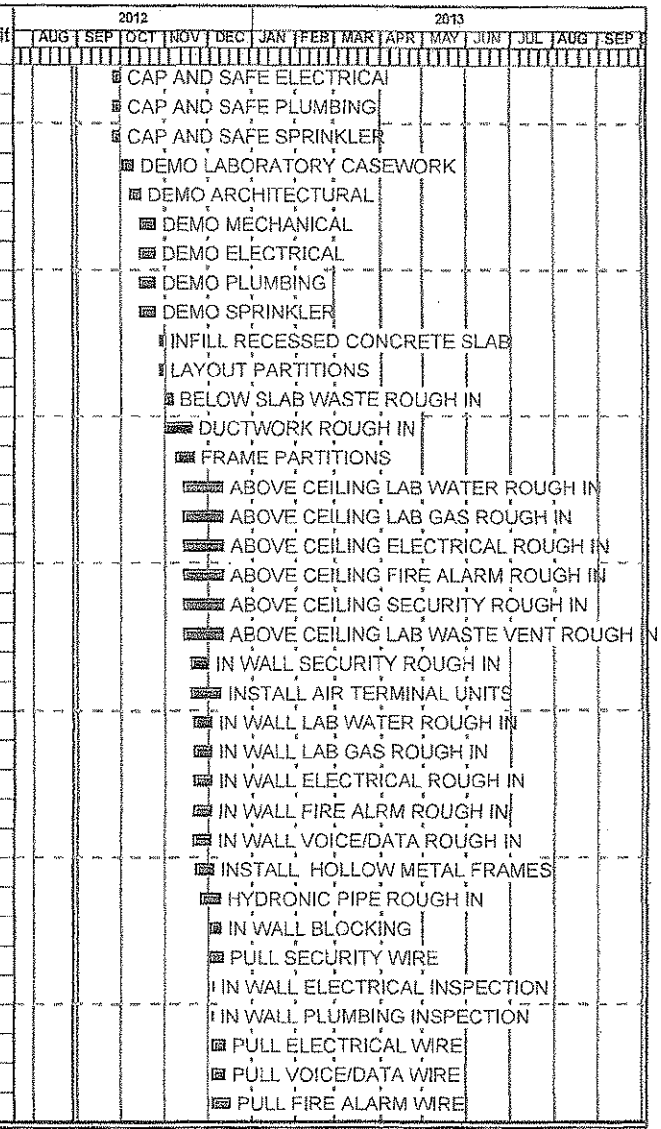

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	25A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
C21340	INSTALL FANCOUL UNITS	3	3	06DEC12	10DEC12	PLBG
C21380	ABOVE CEILING CONDENSATE ROUGH IN	3	3	06DEC12	10DEC12	PLBG
C21500	ABOVE CEILING SPRINKLER ROUGH IN	8	8	06DEC12	17DEC12	SPRK
C21760	FRAMING INSPECTION	1	1	11DEC12	11DEC12	OWNR
C22040	PULL MECHANICAL CONTROL WIRE	10	10	11DEC12	26DEC12	MECH
C21780	INSTALL FIRST SIDE DRYWALL	7	7	12DEC12	20DEC12	DRYW
C22080	INSTALL ELECTRICAL DEVICES	8	8	17DEC12	28DEC12	ELEC
C22100	INSTALL VOICE/DATA DEVICES	8	8	17DEC12	28DEC12	ELEC
C22300	SPRINKLER HYDROSTATIC TEST AND INSPECTION	1	1	18DEC12	18DEC12	OWNR
C21800	INSTALL INSULATION	7	7	19DEC12	31DEC12	INSU
C21820	INSULATION INSPECTION	1	1	02JAN13	02JAN13	OWNR
C21840	INSTALL SECOND SIDE DRYWALL	7	7	03JAN13	11JAN13	DRYW
C21860	TAPE AND FINISH	10	10	10JAN13	23JAN13	DRYW
C21880	INSTALL ACOUSTICAL SEALANT	4	4	14JAN13	17JAN13	DRYW
C21900	INSTALL FIRESTOPPING	4	4	14JAN13	17JAN13	MECH
C22120	INSTALL OVERHEAD SERVICE CARRIER SUPPORT	5	5	14JAN13	18JAN13	MECH
C21920	PRIME AND FIRST COAT PAINT	5	5	21JAN13	25JAN13	PAIN
C22140	INSTALL CEILING GRID	8	8	24JAN13	04FEB13	CLGT
C21940	INSTALL FIRE ALARM PANELS	2	2	28JAN13	29JAN13	FIRE
C21960	INSTALL ELECTRICAL PANELS	2	2	28JAN13	29JAN13	ELEC
C22160	FRAMING FOR DRYWALL CEILING	5	5	28JAN13	01FEB13	DRYW
C22180	INSTALL GRILLES, REGISTERS, AND DIFFUSERS	10	10	30JAN13	12FEB13	MECH
C22200	INSTALL LIGHTS	10	10	30JAN13	12FEB13	ELEC
C22220	INSTALL SPRINKLER HEADS	5	5	05FEB13	11FEB13	SPRK
C22240	ABOVE CEILING MECHANICAL INSPECTION	1	1	13FEB13	13FEB13	OWNR
C22260	ABOVE CEILING ELECTRICAL INSPECTION	1	1	13FEB13	13FEB13	OWNR
C22320	ABOVE CEILING BUILDING INSPECTION	1	1	13FEB13	13FEB13	OWNR
C22280	ABOVE CEILING PLUMBING INSPECTION	1	1	14FEB13	14FEB13	OWNR
C22520	INSTALL SHEET VINYL	2	2	14FEB13	15FEB13	FLRG
C22500	INSTALL VINYL COMPOSITION TILE	7	7	14FEB13	22FEB13	FLRG
C22580	INSTALL OVERHEAD SERVICE CARRIERS	8	8	14FEB13	25FEB13	MECH
C22340	INSTALL CEILING TILE	8	8	15FEB13	26FEB13	CLGT
C22540	INSTALL CARPET	5	5	18FEB13	22FEB13	CARP
C22360	POINT UP WALLS	3	3	22FEB13	26FEB13	DRYW
C22380	FINAL PAINT	5	5	26FEB13	04MAR13	PAIN
C22900	INSTALL EMERGENCY SHOWERS	3	3	27FEB13	01MAR13	PLBG

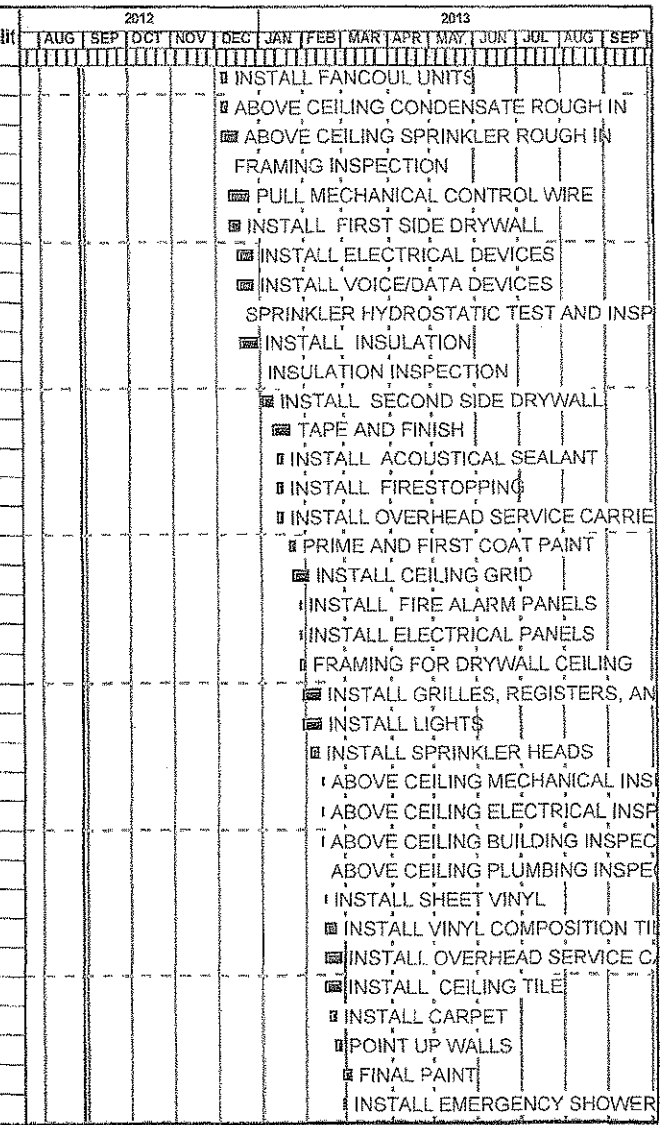

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	26A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
C22600	INSTALL LABORATORY CASEWORK CORES	10	10	28FEB13	13MAR13	CASE
C22980	INSTALL SIGNAGE	2	2	05MAR13	06MAR13	SIGN
C23000	INSTALL FIRE EXTINGUISHER CABINETS	2	2	05MAR13	06MAR13	FIRE
C22400	INSTALL ELECTRICAL COVER PLATES	5	5	05MAR13	11MAR13	ELEC
C22420	INSTALL VOICE/DATA COVER PLATES	5	5	05MAR13	11MAR13	ELEC
C22440	INSTALL FIRE ALARM DEVICES	5	5	05MAR13	11MAR13	FIRE
C22460	INSTALL THERMOSTATS	5	5	05MAR13	11MAR13	ELEC
C22480	INSTALL CARD READERS	5	5	05MAR13	11MAR13	OWNR
C23020	INSTALL WALL/CORNER GUARDS	5	5	05MAR13	11MAR13	DRYW
C22630	INSTALL LABORATORY CABINETS AND COUNTERS	15	15	06MAR13	26MAR13	CASE
C22660	INSTALL LAB GAS ROUGH IN AT CASEWORK	15	15	13MAR13	02APR13	MECH
C22680	INSTALL LAB WATER ROUGH IN AT CASEWORK	15	15	13MAR13	02APR13	MECH
C22700	INSTALL LAB WASTE ROUGH IN AT CASEWORK	15	15	13MAR13	02APR13	MECH
C22720	INSTALL ELECTRICAL ROUGH IN AT CASEWORK	15	15	13MAR13	02APR13	ELEC
C22740	INSTALL VOICE/DATA ROUGH IN AT CASEWORK	15	15	13MAR13	02APR13	ELEC
C22620	INSTALL FUME HOODS	2	2	27MAR13	28MAR13	CASE
C22560	INSTALL VINYL BASE	4	4	27MAR13	01APR13	FLRG
C22650	INSTALL LABORATORY SHELVING AND TRIM	10	10	27MAR13	09APR13	CASE
C22860	INSTALL ELECTRICAL METAL SURFACE RACEWAY	10	10	27MAR13	09APR13	ELEC
C22640	INSTALL LAB GAS CYLINDER RESTARINT	1	1	29MAR13	29MAR13	MECH
C22760	INSTALL LAB GAS TURRETS AT CASEWORK	5	5	03APR13	09APR13	MECH
C22780	INSTALL PLUMBING FIXTURES AT CASEWORK	5	5	03APR13	09APR13	PLBG
C23160	FINAL PLUMBING INSPECTION	1	1	10APR13	10APR13	OWNR
C22880	INSTALL LAB EQUIPMENT	3	3	10APR13	12APR13	CASE
C22800	INSTALL ELECTRICAL DEVICES/COVERS AT	5	5	10APR13	16APR13	ELEC
C22820	INSTALL VOICE/DATA DEVICES/COVERS AT	5	5	10APR13	16APR13	ELEC
C22840	INSTALL LIGHTS AT CASEWORK	5	5	10APR13	16APR13	ELEC
C22920	INSTALL DOORS	5	5	15APR13	19APR13	DOOR
C22940	INSTALL HARDWARE	5	5	15APR13	19APR13	DOOR
C23140	FINAL ELECTRICAL INSPECTION	1	1	17APR13	17APR13	OWNR
C22960	INSTALL GLASS AT BORROW LIGHTS	2	2	22APR13	23APR13	ELEC
C23200	FINAL FIRE MARSHALL INSPECTION	2	2	24APR13	25APR13	OWNR
C23060	FINAL CLEAN	5	5	24APR13	30APR13	FORR
C23080	TEST AND BALANCE	10	10	24APR13	07MAY13	MECH
C23180	FINAL BUILDING INSPECTION	2	2	26APR13	29APR13	OWNR
C23100	COMMISSIONING	20	20	07MAY13	03JUN13	MECH

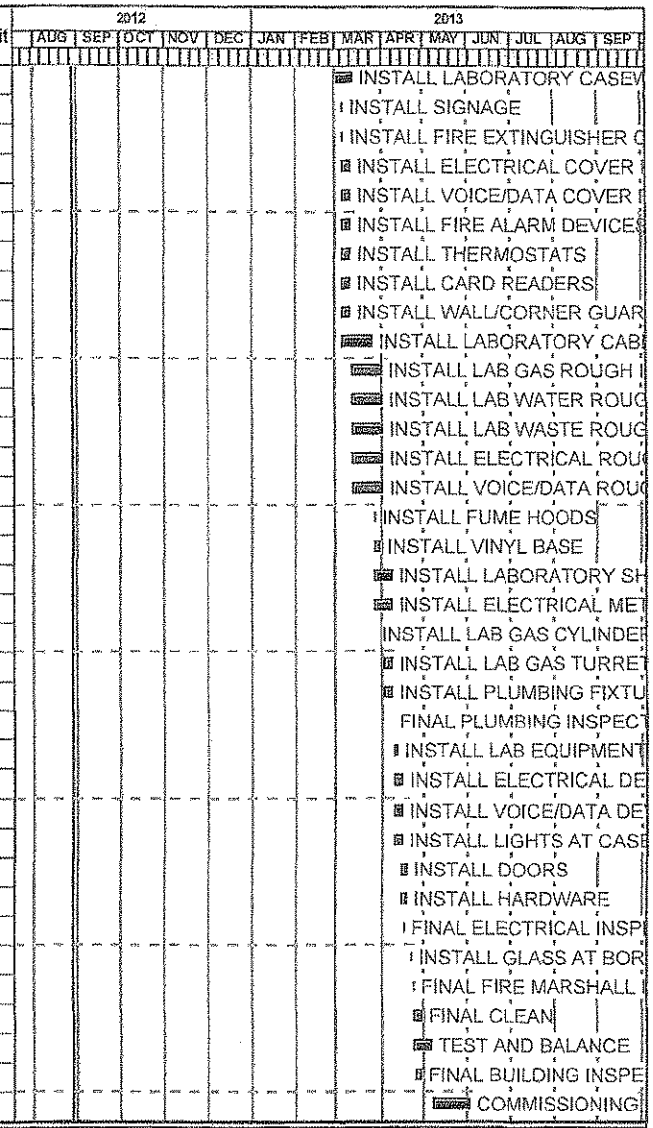

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	27A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
C23120	VALIDATION	10	10	21MAY13	03JUN13	OWNR
C23040	PUNCHLIST	15	15	04JUN13	24JUN13	FORR
BUILDING CLEANER LAWER						
CL1000	INSTALL TEMPORARY PARTITIONS AND DOORS	5	5	26SEP12	02OCT12	DOOR
CL1020	CAP AND SAFE MECHANICAL	5	5	03OCT12	09OCT12	MECH
CL1040	CAP AND SAFE ELECTRICAL	5	5	03OCT12	09OCT12	ELEC
CL1060	CAP AND SAFE PLUMBING	5	5	03OCT12	09OCT12	PLBG
CL1080	CAP AND SAFE SPRINKLER	5	5	03OCT12	09OCT12	SPRK
CL1100	DEMO ARCHITECTURAL	7	7	10OCT12	18OCT12	DEMO
CL1120	DEMO MECHANICAL	7	7	10OCT12	18OCT12	DEMO
CL1140	DEMO ELECTRICAL	7	7	10OCT12	18OCT12	DEMO
CL1160	DEMO PLUMBING	7	7	10OCT12	18OCT12	DEMO
CL1180	DEMO SPRINKLER	7	7	10OCT12	18OCT12	DEMO
CL1200	LAYOUT PARTITIONS	4	4	19OCT12	24OCT12	DRYW
CL1220	BELOW SLAB WASTE ROUGH IN	3	3	25OCT12	29OCT12	MECH
CL1240	DUCTWORK ROUGH IN	10	10	01NOV12	14NOV12	MECH
CL1320	ABOVE CEILING CONDENSATE ROUGH IN	10	10	09NOV12	22NOV12	MECH
CL1340	ABOVE CEILING LAB WATER ROUGH IN	10	10	09NOV12	22NOV12	MECH
CL1360	ABOVE CEILING LAB GAS ROUGH IN	10	10	09NOV12	22NOV12	MECH
CL1380	ABOVE CEILING ELECTRICAL ROUGH IN	10	10	09NOV12	22NOV12	ELEC
CL1420	ABOVE CEILING FIRE ALARM ROUGH IN	10	10	09NOV12	22NOV12	FIRE
CL1440	ABOVE CEILING SECURITY ROUGH IN	10	10	09NOV12	22NOV12	SECU
CL1480	ABOVE CEILING LAB WASTE VENT ROUGH IN	10	10	09NOV12	22NOV12	MECH
CL1400	CABLE TRAY ROUGH IN	3	3	13NOV12	15NOV12	MECH
CL1460	ABOVE CEILING SPRINKLER ROUGH IN	5	5	13NOV12	19NOV12	SPRK
CL1260	INSTALL AIR TERMINAL UNITS	7	7	20NOV12	28NOV12	MECH
CL2100	INSTALL OVERHEAD SERVICE CARRIER SUPPORT	5	5	23NOV12	29NOV12	MECH
CL1500	FRAME PARTITIONS	6	6	23NOV12	30NOV12	DRYW
CL1520	IN WALL BLOCKING	3	3	28NOV12	30NOV12	DRYW
CL1540	INSTALL HOLLOW METAL FRAMES	4	4	28NOV12	03DEC12	DOOR
CL1720	FRAMING INSPECTION	2	2	03DEC12	04DEC12	OWNR
CL1560	IN WALL LAB WATER ROUGH IN	5	5	03DEC12	07DEC12	MECH
CL1580	IN WALL LAB GAS ROUGH IN	5	5	03DEC12	07DEC12	MECH
CL1600	IN WALL ELECTRICAL ROUGH IN	5	5	03DEC12	07DEC12	ELEC
CL1620	IN WALL FIRE ALARM ROUGH IN	5	5	03DEC12	07DEC12	FIRE
CL1640	IN WALL VOICE/DATA ROUGH IN	5	5	03DEC12	07DEC12	ELEC

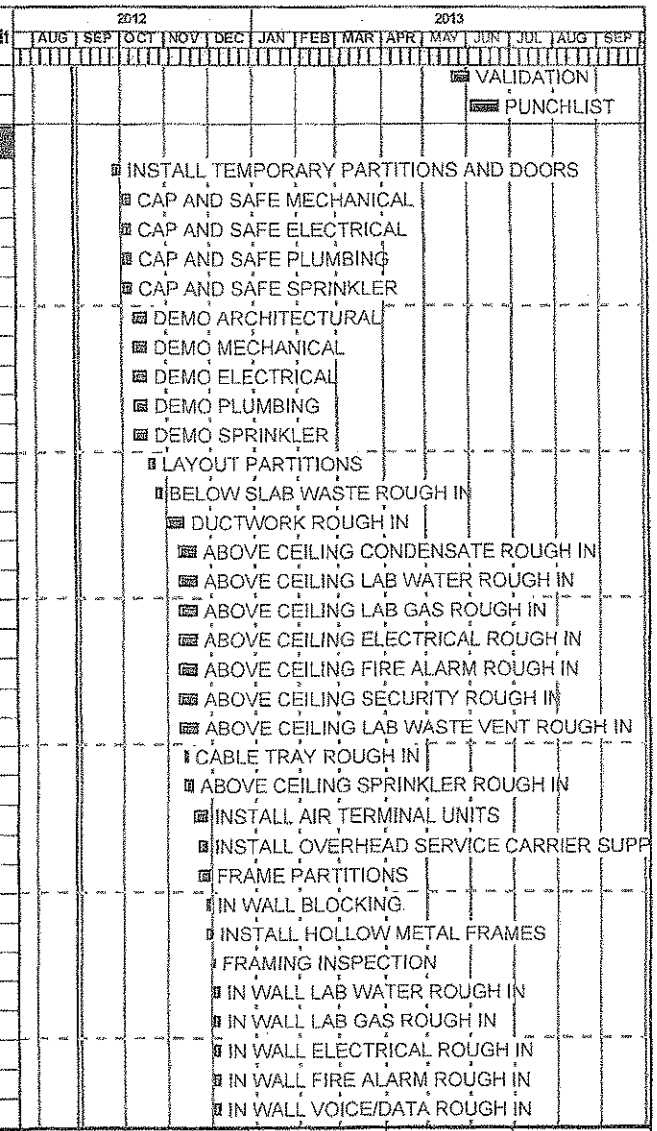

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	28A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
CL1660	IN WALL SECURITY ROUGH IN	5	5	03DEC12	07DEC12	SECU
CL1740	INSTALL FIRST SIDE DRYWALL	6	6	05DEC12	12DEC12	DRYW
CL1760	INSTALL INSULATION	4	4	07DEC12	12DEC12	INSU
CL1680	IN WALL ELECTRICAL INSPECTION	2	2	10DEC12	11DEC12	OWNR
CL1700	IN WALL PLUMBING INSPECTION	2	2	10DEC12	11DEC12	OWNR
CL1960	PULL ELECTRICAL WIRE	7	7	12DEC12	20DEC12	ELEC
CL1980	PULL VOICE DATA WIRE	7	7	12DEC12	20DEC12	ELEC
CL2000	PULL SECURITY WIRE	7	7	12DEC12	20DEC12	SECU
CL2020	PULL MECHANICAL CONROL WIRE	7	7	12DEC12	20DEC12	MECH
CL2040	PULL FIRE ALARM WIRE	7	7	12DEC12	20DEC12	FIRE
CL1780	INSULATION INSPECTION	2	2	13DEC12	14DEC12	OWNR
CL1800	INSTALL SECOND SIDE DRYWALL	6	6	17DEC12	26DEC12	DRYW
CL2060	INSTALL ELECTRCAL DEVICES	7	7	19DEC12	31DEC12	ELEC
CL2080	INSTALL VOICE/DATA DEVICES	7	7	19DEC12	31DEC12	ELEC
CL1280	INSTALL FANCOIL UNITS	3	3	27DEC12	31DEC12	PLBG
CL1300	HYDRONIC PIPE ROUGH IN	3	3	27DEC12	31DEC12	MECH
CL1820	TAPE AND FINISH	7	7	31DEC12	09JAN13	DRYW
CL1840	INSTALL ACOUSTICAL SEALANT	2	2	10JAN13	11JAN13	DRYW
CL1860	FIRESTOPPING	3	3	10JAN13	14JAN13	MECH
CL1880	PRIME AND FIRST COAT PAINT	5	5	10JAN13	16JAN13	PAIN
CL2120	INSTALL CEILING GRID	6	6	14JAN13	21JAN13	CLGT
CL1920	INSTALL FIRE ALARM PANEL	3	3	17JAN13	21JAN13	FIRE
CL1900	INSTALL ELECTRICAL PANELS	5	5	17JAN13	23JAN13	ELEC
CL2140	INSTALL GRILLES, REGISTERS, AND DIFFUSERS	7	7	17JAN13	25JAN13	MECH
CL2160	INSTALL LIGHTS	7	7	22JAN13	30JAN13	ELEC
CL1940	CONVERT EXIST SWITCHGEAR TO FULL	3	3	24JAN13	28JAN13	ELEC
CL2180	INSTALL SPRINKLER HEADS	4	4	31JAN13	05FEB13	SPRK
CL2200	ABOVE CEILING MECHANICAL INSPECTION	2	2	06FEB13	07FEB13	OWNR
CL2220	ABOVE CEILING ELECTRICAL INSPECTION	2	2	06FEB13	07FEB13	OWNR
CL2240	ABOVE CEILING PLUMBING INSPECTION	2	2	06FEB13	07FEB13	OWNR
CL2260	SPRINKLER HYDROSTATIC TEST AND INSPECTION	2	2	06FEB13	07FEB13	OWNR
CL2280	ABOVE CEILING BUILDING INSPECTION	2	2	08FEB13	11FEB13	OWNR
CL2480	INSTALL SHEET VINYL	2	2	11FEB13	12FEB13	FLRG
CL2300	INSTALL CEILING TILE	5	5	12FEB13	18FEB13	CLGT
CL2460	INSTALL VINYL COMPOSITION TILE	5	5	12FEB13	18FEB13	FLRG
CL2320	POINT UP WALLS	3	3	19FEB13	21FEB13	DRYW

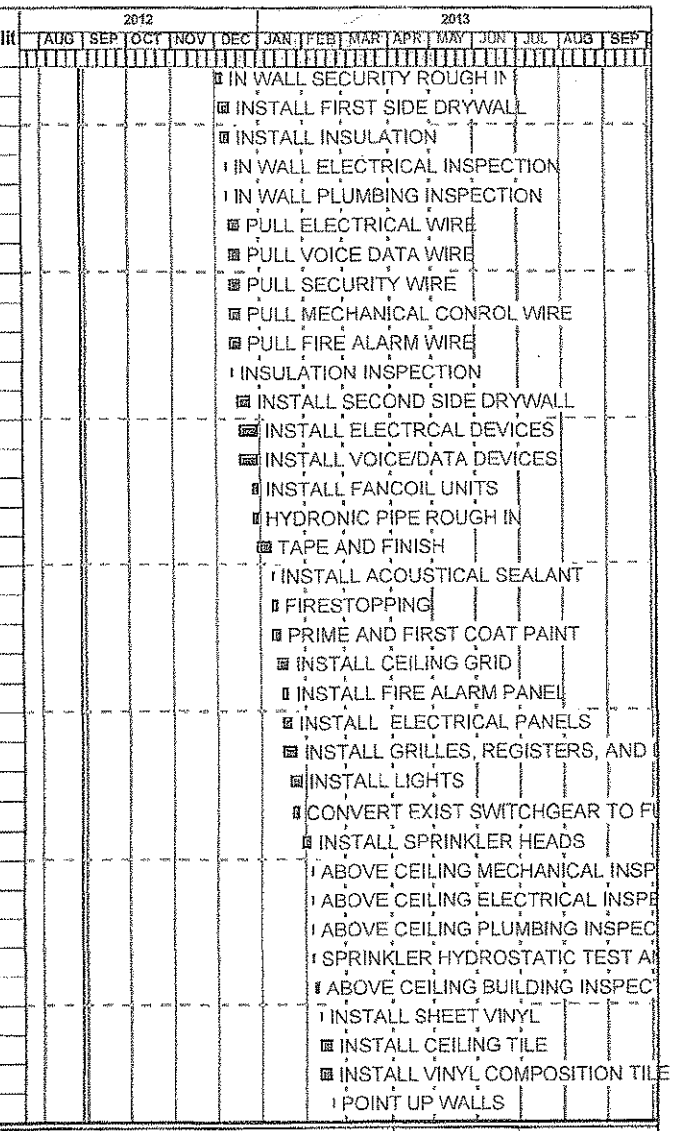

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	29A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
CL2520	INSTALL OVERHEAD SERVICE CARRIERS	3	3	19FEB13	21FEB13	MECH
CL2940	INSTALL FIRE EXTINGUISHER CABINETS	2	2	22FEB13	25FEB13	FIRE
CL2340	FINAL PAINT	4	4	22FEB13	27FEB13	PAIN
CL2540	INSTALL LABORATORY CASEWORK CORES	5	5	22FEB13	28FEB13	CASE
CL2920	INSTALL SIGNAGE	2	2	28FEB13	01MAR13	SIGN
CL2360	INSTALL ELECTRICAL COVER PLATES	3	3	28FEB13	04MAR13	ELEC
CL2380	INSTALL VOICE/DATA COVER PLATES	3	3	28FEB13	04MAR13	ELEC
CL2440	INSTALL CARD READERS	3	3	28FEB13	04MAR13	OWNR
CL2840	INSTALL EMERGENCY SHOWERS	3	3	28FEB13	04MAR13	PLBG
CL2960	INSTALL CORNER GUARD	3	3	28FEB13	04MAR13	DRYW
CL2420	INSTALL THERMOSTATS	4	4	28FEB13	05MAR13	ELEC
CL2400	INSTALL FIRE ALARM DEVICES	5	5	28FEB13	06MAR13	FIRE
CL2570	INSTALL LABORATORY CABINETS AND COUNTERS	5	5	01MAR13	07MAR13	CASE
CL2620	INSTALL LAB WASTE ROUGH IN AT CASEWORK	5	5	07MAR13	13MAR13	MECH
CL2640	INSTALL LAB WASTE ROUGH IN AT CASEWORK	5	5	07MAR13	13MAR13	MECH
CL2660	ELECTRICAL ROUGH IN AT LAB CASEWORK	5	5	07MAR13	13MAR13	ELEC
CL2680	VOICE/DATA ROUGH IN AT CASEWORK	5	5	07MAR13	13MAR13	ELEC
CL2560	INSTALL FUME HOODS	4	4	08MAR13	13MAR13	CASE
CL2600	INSTALL LAB GAS ROUGH IN AT CASEWORK	5	5	08MAR13	14MAR13	MECH
CL2800	INSTALL ELECTRICAL METAL SURFACE RACEWAY	7	7	08MAR13	18MAR13	ELEC
CL2580	INSTALL LAB GAS CYLINDER RESTARINT	1	1	14MAR13	14MAR13	MECH
CL2720	PLUMBING FIXTURES AT CASEWORK	3	3	14MAR13	18MAR13	PLBG
CL2700	INSTALL LAB GAS TURRETS AT CASEWORK	3	3	15MAR13	19MAR13	MECH
CL2590	INSTALL LABORATORY SHELVING AND TRIM	5	5	19MAR13	25MAR13	CASE
CL2820	INSTALL LAB EQUIPMENT	5	5	19MAR13	25MAR13	CASE
CL3100	FINAL PLUMBING INSPECTION	1	1	20MAR13	20MAR13	OWNR
CL2500	INSTALL VINYL BASE	3	3	26MAR13	28MAR13	FLRG
CL2740	INSTALL ELECTRICAL DEVICES/COVERS AT	3	3	26MAR13	28MAR13	ELEC
CL2760	INSTALL VOICE/DATA DEVICES/COVERS AT	3	3	26MAR13	28MAR13	ELEC
CL2860	INSTALL DOORS	4	4	26MAR13	29MAR13	DOOR
CL3020	TEST AND BALANCE	5	5	26MAR13	01APR13	MECH
CL2880	INSTALL HARDWARE	3	3	27MAR13	29MAR13	DOOR
CL2780	INSTALL LIGHTS AT CASEWORK	3	3	29MAR13	02APR13	ELEC
CL2900	INSTALL GLASS AT BORROW LIGHTS	4	4	01APR13	04APR13	ELEC
CL3040	COMMISSIONING	10	10	02APR13	15APR13	MECH
CL3080	FINAL ELECTRICAL INSPECTION	1	1	03APR13	03APR13	OWNR

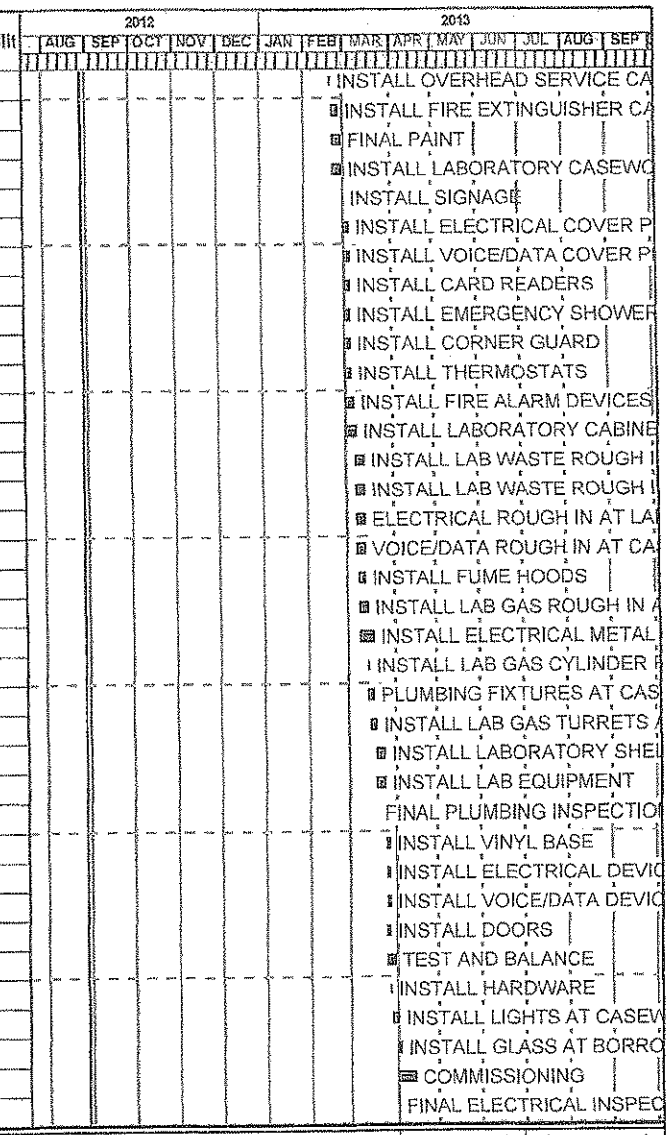

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	30A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved

Act ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	Responsibilit
CL3140	FINAL FIRE MARSHALL INSPECTION	1	1	05APR13	05APR13	OWNR
CL3120	FINAL BUILDING INSPECTION	1	1	08APR13	08APR13	OWNR
CL3060	VALIDATION	5	5	16APR13	22APR13	OWNR
CL2980	PUNCHLIST	15	15	23APR13	13MAY13	FORR
CL3000	FINAL CLEAN	5	5	14MAY13	20MAY13	FORR
CLOSEOUT						
CLSB1000	OPERATION AND MAINTENANCE MANUALS	1	1	25JAN13	25JAN13	FORR
CLSB1020	OWNER TRAINING	2	2	28JAN13	29JAN13	FORR
CLSA1000	OPERATION AND MAINTENANCE MANUALS	1	1	24MAY13	24MAY13	FORR
CLSA1020	OWNER TRAINING	1	1	27MAY13	27MAY13	FORR
CLSC1000	OPERATION AND MAINTENANCE MANUALS	1	1	28MAY13	28MAY13	FORR
CLSC1020	OWNER TRAINING	1	1	29MAY13	29MAY13	FORR

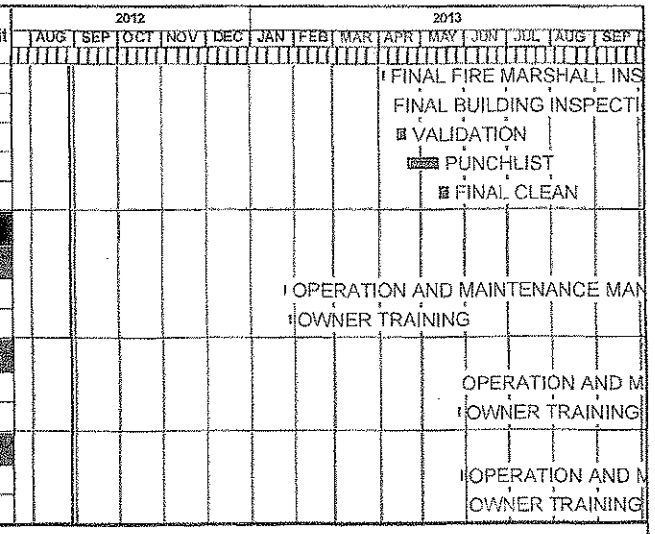

Data date	28AUG12
Start date	08AUG12
Finish date	24JUN13
Project name	9800 08272012
Page number	31A

© Primavera Systems, Inc.

9800 LEASE SPACE FOR MULTI. PROGRAMS

9800 08272012

FORRESTER CONSTRUCTION

Date	Revision	Checked	Approved
