202231

Scope of Work for The Removal of PCB Contaminated Dust for Impacted Homes In the Vicinity of The Cornell Dubilier Site.

Mitigation work to be performed at the site will be implemented using a Phased Approach. Phasing of tasks enables the osc to precisely control the events of the project so that schedules can be developed and provided to ~~the~~ both management and the affected ~~B~~ Public.

~~Three Phase, Phase I and Phase II and Phase III~~

Four Phases will be required for this project. Each Phases and the associated tasks are out lined below:

Phase I: Time Period March 27, 1998 - April 2, 1998

I Pre Mobilization:

a Activation of ERCs (ETI)

b Meet with Response Manager on 3/30/98 to discuss work strategy and support facilities

c. Response Manager: Resources Trailers, Generators, cleaning Equipment (Hepavac/Carpet steam cleaners) ~~initiates~~ obtains permits for Electric drop and trailer placement

d. Field Clerk arrives on ~~Sd~~ 4/1/98 to Assist Rm.

e. RM Prepares Health and Safety Plan for cleaning of homes

f. RM and OSC develop a Work Plan for Site Activities.

G. Bids are solicited for Security/Equipment.

H. Collect 12 background soil samples (PCBs)

Phase II April 3 - April 7

I Mobilization.

a) 1 Foreman & 3 Laborers arrive on Site

b) The Support Area is set up.

1) Vegetation is cleared / area is graded with stone

2) Site Trailers (2) Dumpsters are delivered and set up

3) 50KW Generator connected to trailers (if electric is not available) / Phones connected

4) Dumpsters / Photo Copy / Fax / Copy machine delivered

5) Cleaning Equipment delivered

a) Crew Leaders how to operate Equipment and are assigned specific tasks.

Phase III April 8 - April 22

I. House Cleaning: (Basement & Attic Thur)

a) Objective is to clean one house per day.

1) Clean via vacuum all duct work / Replace Filters

2) Vacuum all Furniture, Carpets, Drapes, Shades

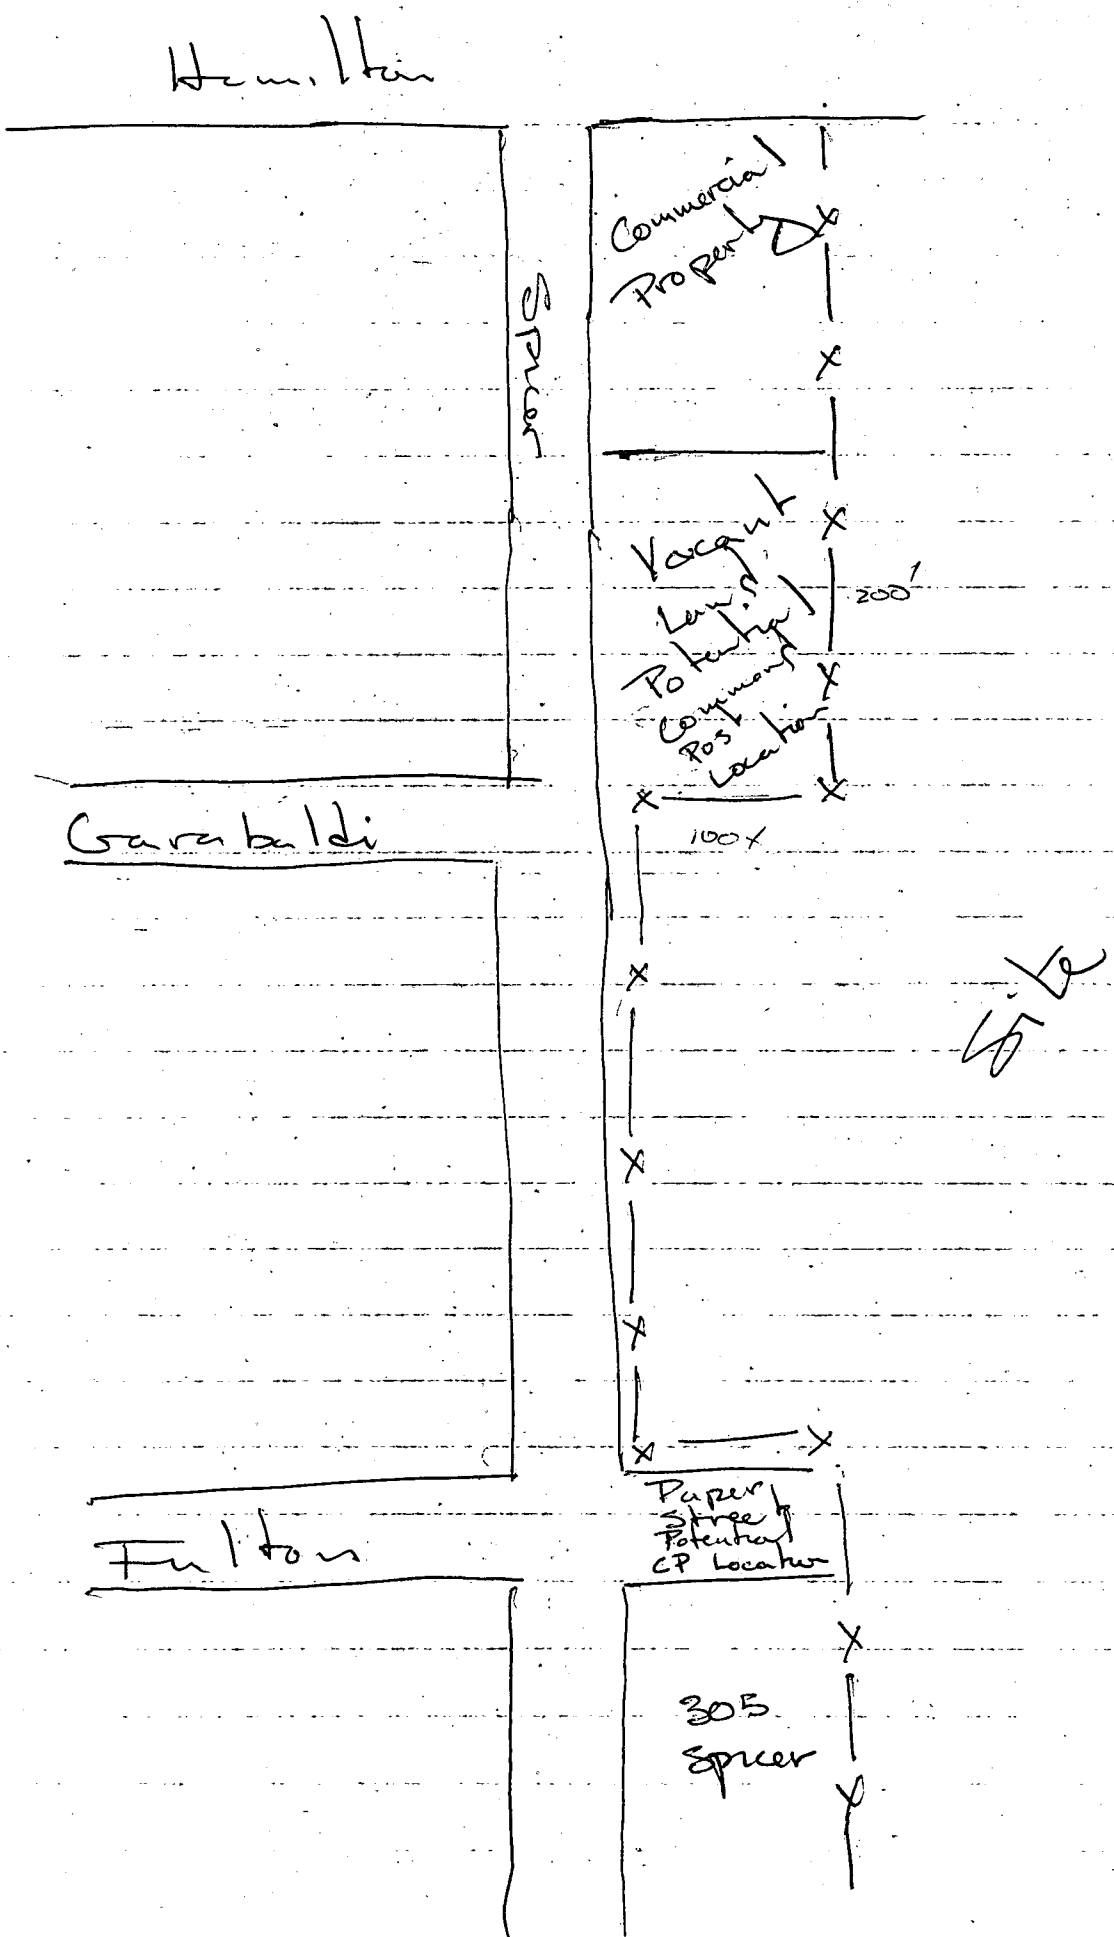
Hamilton
Spencer
Commercial Property
Vacant Land Potential Commercial POS Location
200'
Garibaldi
100'
Site
Paper Street Potential CP Location
Fulton
305 Spencer

3) Wash all Linoleum / Tile Floors - Window and door sills
4) ~~Ale~~ Wash all ~~carpet~~ carpets with Industrial Steam cleaner.
~~5) Move all Furniture~~
5) Move all Appliance, clean floors / coils.
6) Move all Furniture.
7) Vacuum all ~~screens~~ window screens / door screens

b House Cleaning Schedule (To be arranged by the OSC Prior To April 8)

1 500 Garabaldi (3)
2 507 Hamilton (1)
3 204 Spicer (2)
4 501 Garabaldi (4)
5) 108 Spicer
6) 130 Spicer
7) 214 Spicer
8) 305 Spicer
9) 320 Spicer.

c) ~~Effective~~ Verification Sampling.
1) ~~Very~~ Post Clean up Sampling to be Performed by ERT to determine Effectiveness of the Action. Composite dust samples to be analyzed for PCBs.

d Oversite / Security
1) Private Security Service on site after hours
2) Start present to Monitor ETI during Interior

cleaning.

Phase ~~III~~ April 23 - April 27

I Site Demobilization

a) Dispose of all waste generated during the clean up (dust / PPE / filters)

b) Repair ~~any~~ damage to private properties

c) Return rental equipment; trailers generators, ~~vacuums~~ vacuums etc.

d) Await confirmatory sample results.
