WEEKLY STATUS REPORT

Prepared By: Patrick Rubenbauer

BCP Project No.:	C224099	EPA Consent Order No.:	CERCLA-02-2017-2021	Date:	07/08/2019
Project Name:	BRT Powerhouse 153 2nd Street AKA 322 3rd Avenue, Brooklyn, NY 11215				

Remediation Activities (Week of July 1, 2019):

- Continued gauging and product recovery via absorbent sock as necessary.

Redevelopment Activities (Week of July 1, 2019):

- Continued steel repair work in the turbine hall.
- Continued general site maintenance.
- Continued demolition and clean-up in the turbine hall. Assorted demolition debris was removed from the site as it was generated.
- Continued site surveying work as necessary.
- Completed backfill of the asbestos containing materials (ACM) excavation in the east site driveway. ACM abatement work complete.
- Began trenching in the east driveway for support of excavation (SOE) installation for future redevelopment utilities.
- Darcon (Site contractor) completed loading the 100-125% and 125-150% intervals of the turbine hall load test.

Planned Activities for next week:

- Continue gauging and product recovery as necessary.
- Continue steel repair work in the turbine hall.
- Continue loading the turbine hall load test.
- Continue demolition and clean-up in the turbine hall.
- Begin the SOE installation in the east driveway.

594353

Photo Log

Photo 1 – Looking east at the east site driveway. Structure Tech (Site contractor) backfills the ACM excavation with previously excavated and stockpiled soil.	
Photo 2 – Looking west in the turbine hall cellar. Darcon (Site contractor) loads the 125-150% interval of the turbine hall load test.	
Photo 3 – Looking north in the east driveway. Structure Tech (Site contractor) excavates for the water management trench and installs plastic sheeting in preparation for SOE installation.	

Fill Stockpile

Demolition

Geotechnical Test Pit Excavation

Steel Work

SOE Preparation Work
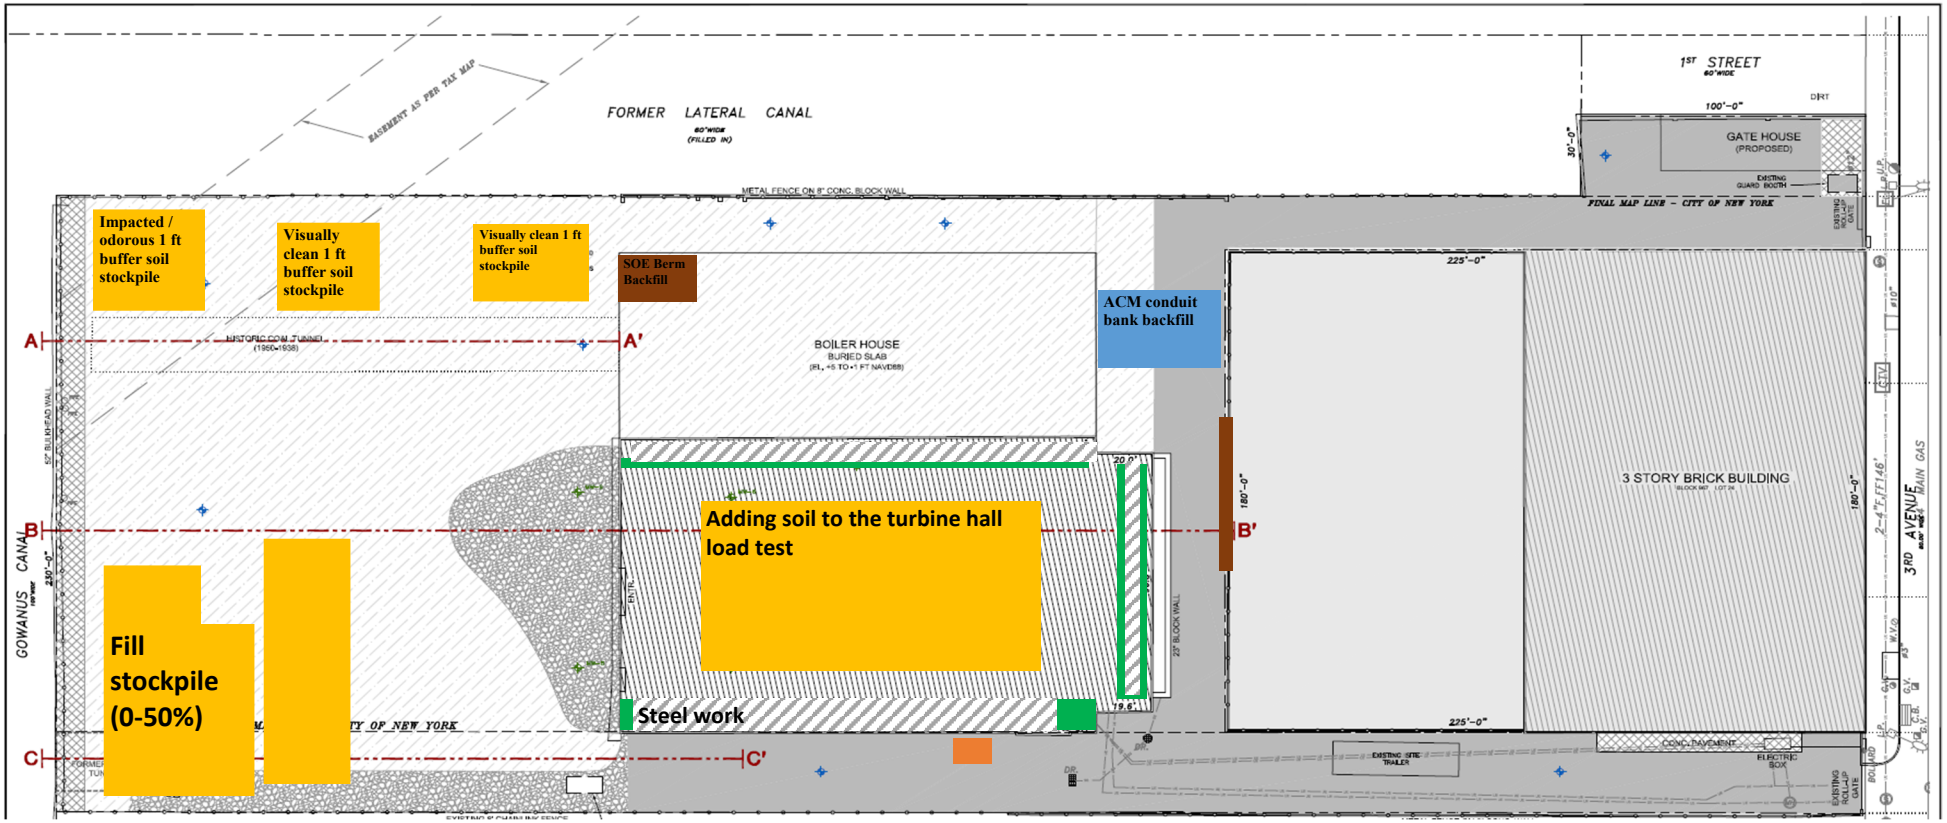
ACM Conduit Bank Backfill
