From:	Bruce Scott Kennington
To:	Granger, Michelle
Cc:	rich.e.gajdek@usace.army.mil; Neal F. Kolb P.E. (Neal.F.Kolb@usace.army.mil); patrick nejand; Hauber, Erin M CIV USARMY CENWK (US); Brink, Bradley J NWK (Bradley.J.Brink@usace.army.mil); Hidalgo, Luis (G&I); Gibson, Bradley (G&I; Stan Popelar; Scott Tarmann; Michael Kevin Eddings
Subject:	Proposed Call - Discuss Results of Soil Boring SB-34 in MPA, Holiday Shutdown Activities, OU3 RA, PVGCS Site
Date:	Sunday, December 29, 2019 8:45:13 PM
Attachments:	Dwg C-102_Holiday SD SB Locs.pdf

Dear Michelle:

We have received the expedited results of the soil samples collected from soil boring SB-34 conducted in the northern portion of the Main Production Area inside the Albéa facility (see the attached figure from our Work Plan. We propose to have a call tomorrow morning (Mon, Dec 30) at 10:30 AM Eastern time to discuss these results. I will also circulate a dial-in number along with a meeting invitation for the call.

We are preparing a summary of these results and will transmit these in advance of tomorrow's call.

Sincerely,
Bruce

Bruce S Kennington
Principal

D +1 (312) 288-3834
M +1 (312) 953-9965
bkennington@ramboll.com

From: Bruce Scott Kennington
Sent: Thursday, December 12, 2019 4:19 PM
To: Michelle A. Granger - USEPA Region 2 (Granger.Michelle@epa.gov) <Granger.michelle@Epa.gov>
Cc: Richard Gajdek P.E. PMP (Rich.E.Gajdek@usace.army.mil) <Rich.E.Gajdek@usace.army.mil>; Neal F. Kolb P.E. (Neal.F.Kolb@usace.army.mil) <Neal.F.Kolb@usace.army.mil>; Patrick C. Nejand (patrick.c.nejand@usace.army.mil) <patrick.c.nejand@usace.army.mil>; Hauber, Erin M CIV USARMY CENWK (US) <Erin.M.Hauber@usace.army.mil>; Brink, Bradley J NWK (Bradley.J.Brink@usace.army.mil) <Bradley.J.Brink@usace.army.mil>; 'Luis Hidalgo (Luis.Hidalgo@riotinto.com)' <Luis.Hidalgo@riotinto.com>; Bruce White (Bruce.White@btlaw.com) <Bruce.White@btlaw.com>; Jeff Armington (jeff.armington@riotinto.com) <jeff.armington@riotinto.com>; Joseph McDonald <joseph.mcdonald@albea-group.com>; Felix E. Miranda <felix.miranda@albea-group.com>; Russell Gladd <russell.gladd@albea-group.com>
Subject: Work Plan for Plant Shutdown Construction Activities, OU3 RA, PVGCS Site

Dear Michelle:

On behalf of Pechiney Plastics Packaging, Inc. (PPPI), the Primary Settling Defendant for the Remedial Design/Remedial Action Consent Decree (CD)[1], and Luis Hidalgo (Project Coordinator for OU3), please see the attached *Work Plan for Year-End Holiday Plant Shutdown, ISTR System Construction, Operable Unit 3*
Pohatcong Valley Groundwater Contamination Superfund Site, also submitted via Aconex.

Please let us know if you or your staff have any questions or comments. We look forward to USEPA acceptance of this plan to implement this work inside the Main Production Areas of the Albéa Americas facility in Washington, NJ during the upcoming scheduled shutdown during the holidays (Dec 21, 2019 to Jan 2, 2020).

[1] In the matter of United States of America v. PPPI (Civil Action No. 09-cv-05692) and United States of America v. Bristol Myers Squibb Company, et. al. (Civil Action No. 13-cv-05798) effective March 11, 2015.

Sincerely,

Bruce S. Kennington

Principal

D +1 312 288 3834
M +1 312 953 9965
bkennington@ramboll.com

Ramboll Environ
333 West Wacker Drive, Suite 2700
Chicago, IL 60606
USA
www.ramboll.com

APPROVED

For Construction

NOTES:

1. SEE SHEET C101 FOR ADDITIONAL NOTES AND LEGEND.
2. EACH HEATER WILL HAVE A CO-LOCATED VAPOR EXTRACTION WELL.

LEGEND:

- H — ISTR HEATERS ((VERTICAL) TOTAL OF 57)
- HA — ISTR HEATERS ((ANGLED) TOTAL OF 14)
- ISTR HEATER FAN (ANGLED) WITH TRENCH AND TOTAL OF 107 ANGLED HEATERS)
- (T) TEMPERATURE MONITORING POINTS (T) (TOTAL OF 7)
- (T) TEMPERATURE MONITORING POINT PREVIOUSLY INSTALLED (T) (TOTAL OF 11)
- THERMAL TREATMENT ZONE (TTZ)
- THERMAL TREATMENT ZONE A (TTZ)
- THERMAL TREATMENT ZONE B (TTZ)
- THERMAL TREATMENT ZONE C (TTZ)

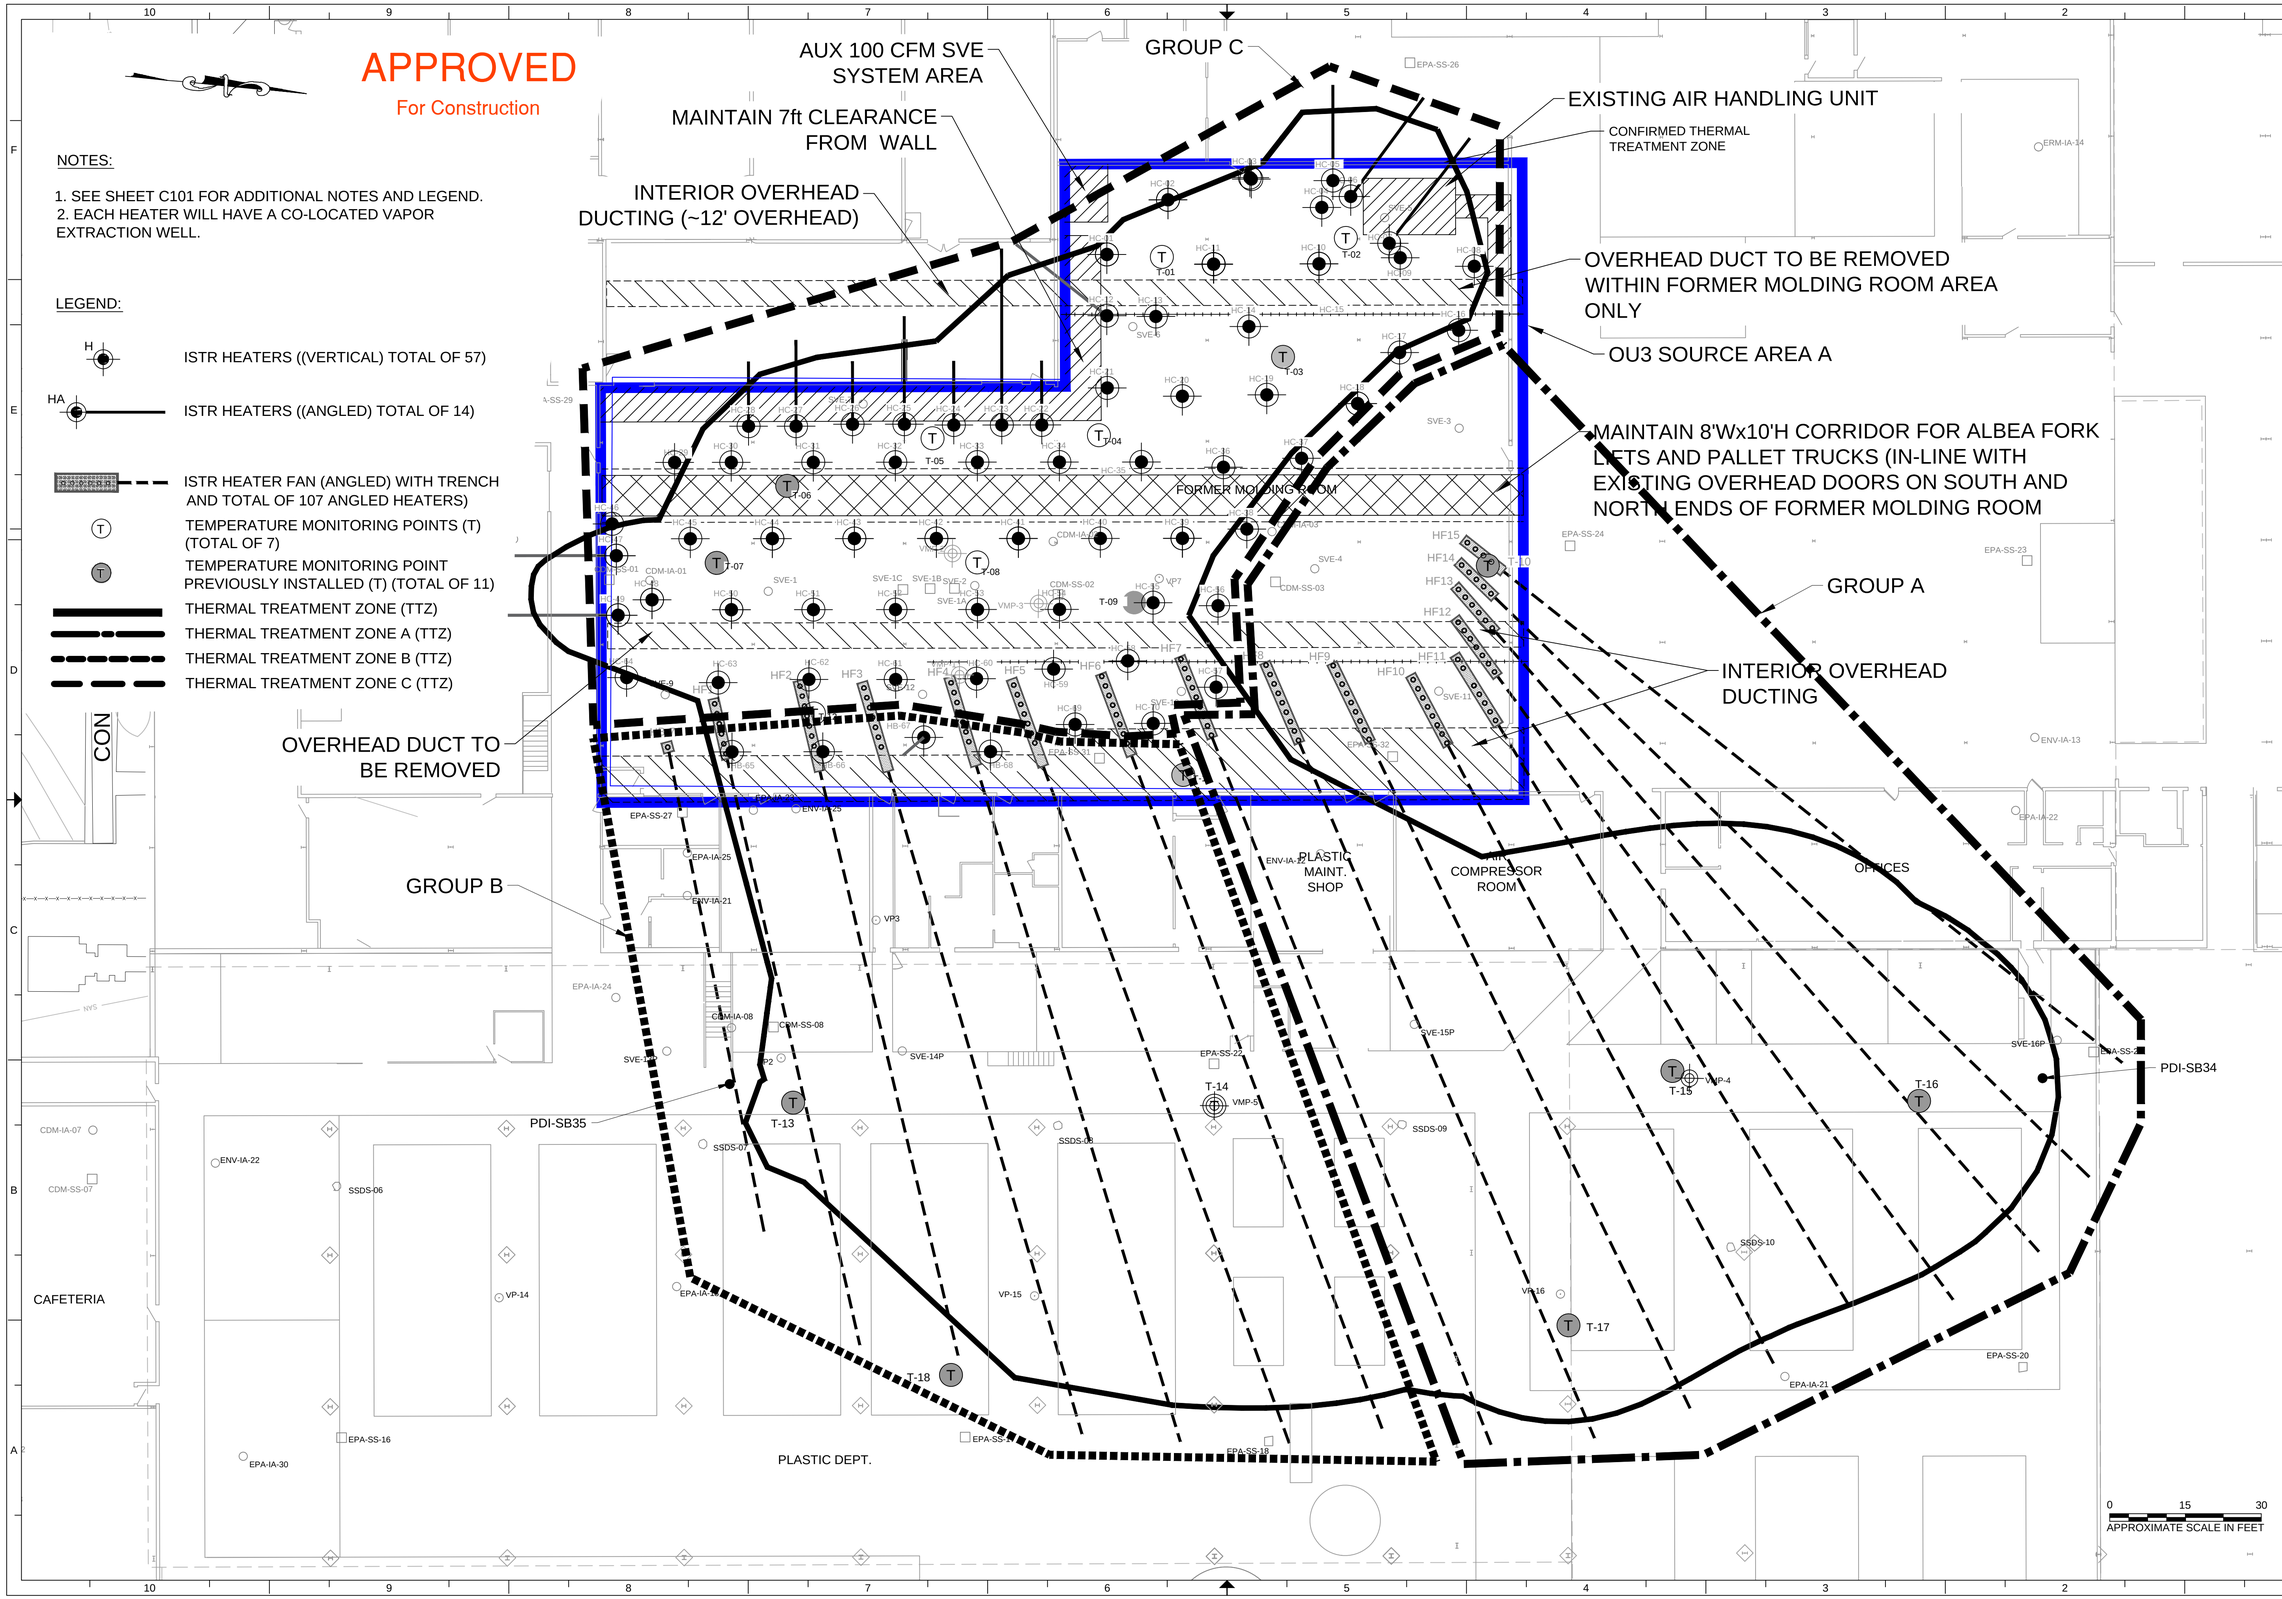

REV	DATE	AP	CAD	ENG	DL	CC	PM	CM	DESCRIPTION
A	10/24/2019								

CONTIDENTIAL: INFORMATION CONTAINED IN THIS DOCUMENT IS CONFIDENTIAL AND THE PROPERTY OF TRS GROUP, INC. NO INFORMATION CONTAINED HEREIN MAY BE REPRODUCED OR DISTRIBUTED WITHOUT THE EXPRESS WRITTEN CONSENT OF TRS GROUP, INC. RENTON, WA.

RAMBOLL US CORPORATION, CHICAGO, IL 60606 (312) 288-3800
WWW.RAMBOLL.COM

TRS Accelerating Value

FINAL (100%) DESIGN, IN SITU THERMAL REMEDIATION SYSTEM, OU3, PVGCS SITE, WARREN COUNTY, NEW JERSEY

WELLFIELD LAYOUT

SCALE:

SHEET SIZE: D

REV: A

REFERENCE NO.: R18-004.01

SHEET: 1 OF 1

DWG NO.: C102
