ID		Task Mode	Task Name	Duration	Start	Finish
1			**Pond D Closure-Outfall Permit DEC-30**	**627 days**	**Mon 11/23/15**	**Tue 4/17/18**
2			Install Dewatering System	60 days	Mon 11/23/15	Fri 2/12/16
3			Decant Pond D into Pond E outfall through Treatment System	60 days	Wed 12/30/15	Tue 3/22/16
4			Dewatering	50 days	Wed 3/23/16	Tue 5/31/16
5			Subgrade Prep	275 days	Wed 4/27/16	Tue 5/16/17
6			Liner Install	100 days	Wed 5/17/17	Tue 10/3/17
7			Cover Material	150 days	Wed 6/14/17	Tue 1/9/18
8			Final Grade/Vegitation	70 days	Wed 1/10/18	Tue 4/17/18

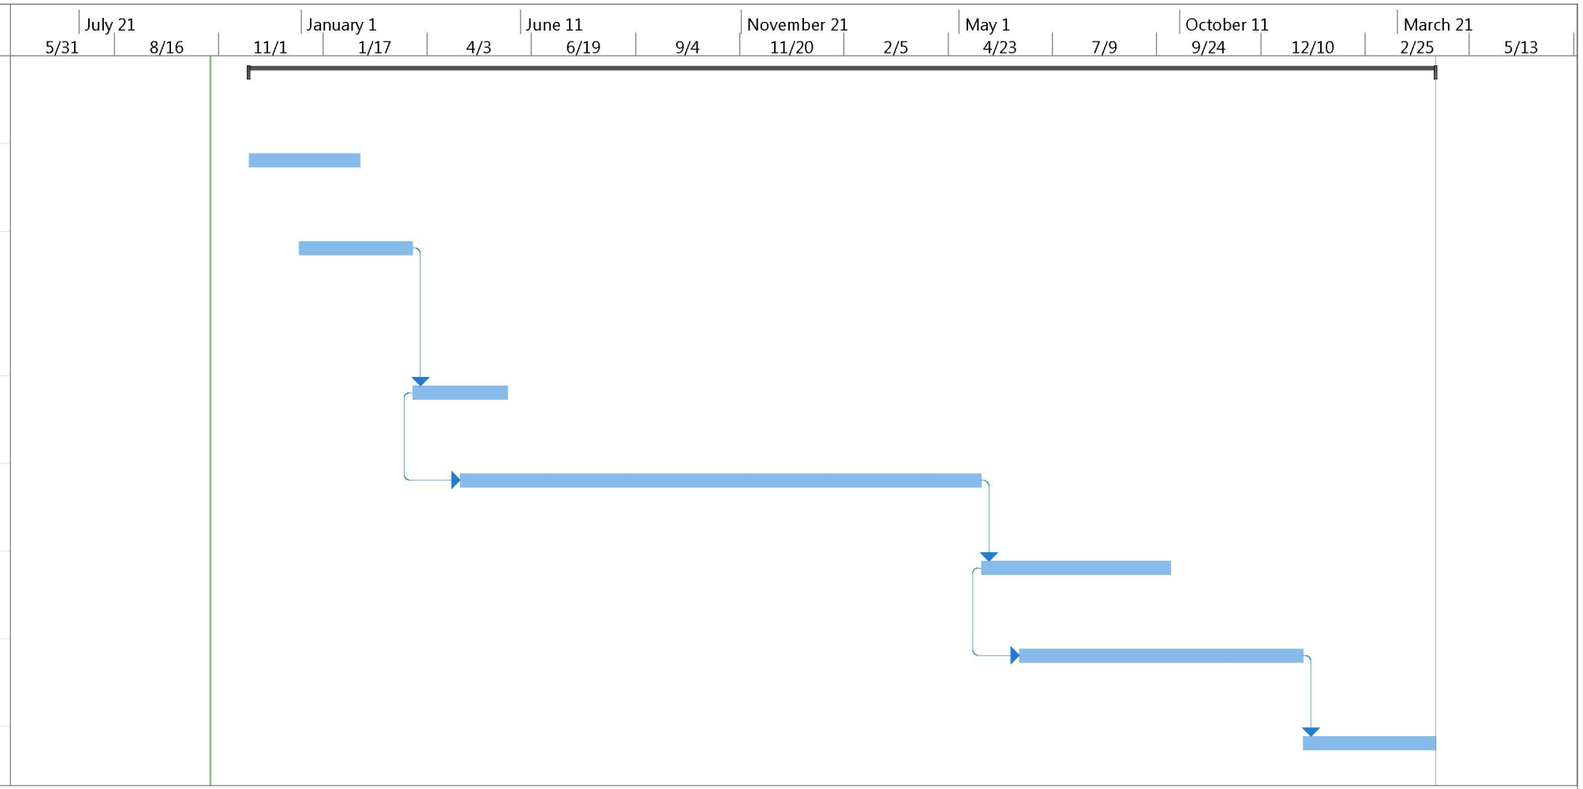

Project: Pond D-Permit-Extra Co
Date: Mon 10/26/15

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

00011639
