2920-20

6/8/89 Satra Sampling

Sample

Only K010 no 91

1 Hi Carbon Slag

2 fines - To be processed in water concentrate

3 fines - Slag - from process - hope to sell

4 baghouse dust from slag pile

5 lime slag from pile

6 rejects from process (same as #5 w/out metal)

7 Pond mud fr. water concentrate process

Note - water from concentrate process goes from pipe on side of bldg. into leach pit. Mud settles out, then is bucketed w. F. end loader to pond for drying. pond made of slag material & almost full. Satra plans to construct another, soon.

EPA Region 5 Records Ctr.

383936

Satralloy - ck. Chrome ore fines Catch - ditch in front of plant for EP tox waste

Slag fines - recovery in progress - 20 workers
ferrochrome mfg - add for speciality steels
Oct 1982 - furnaces shut down
GSA depot - 75,000 tons of chromite ore (1991-or-2)
1958 - built plant

Mixes K090/91 w. lime slag, cant separate,
Magnetic drum separator, tailings contain listed, put back into dump; some on top of slag

Satra Group - trading Co. no Mfg.

19 drums near Maint. Shop - bungs off, lids loose, grease dumped on ground, oil spilled

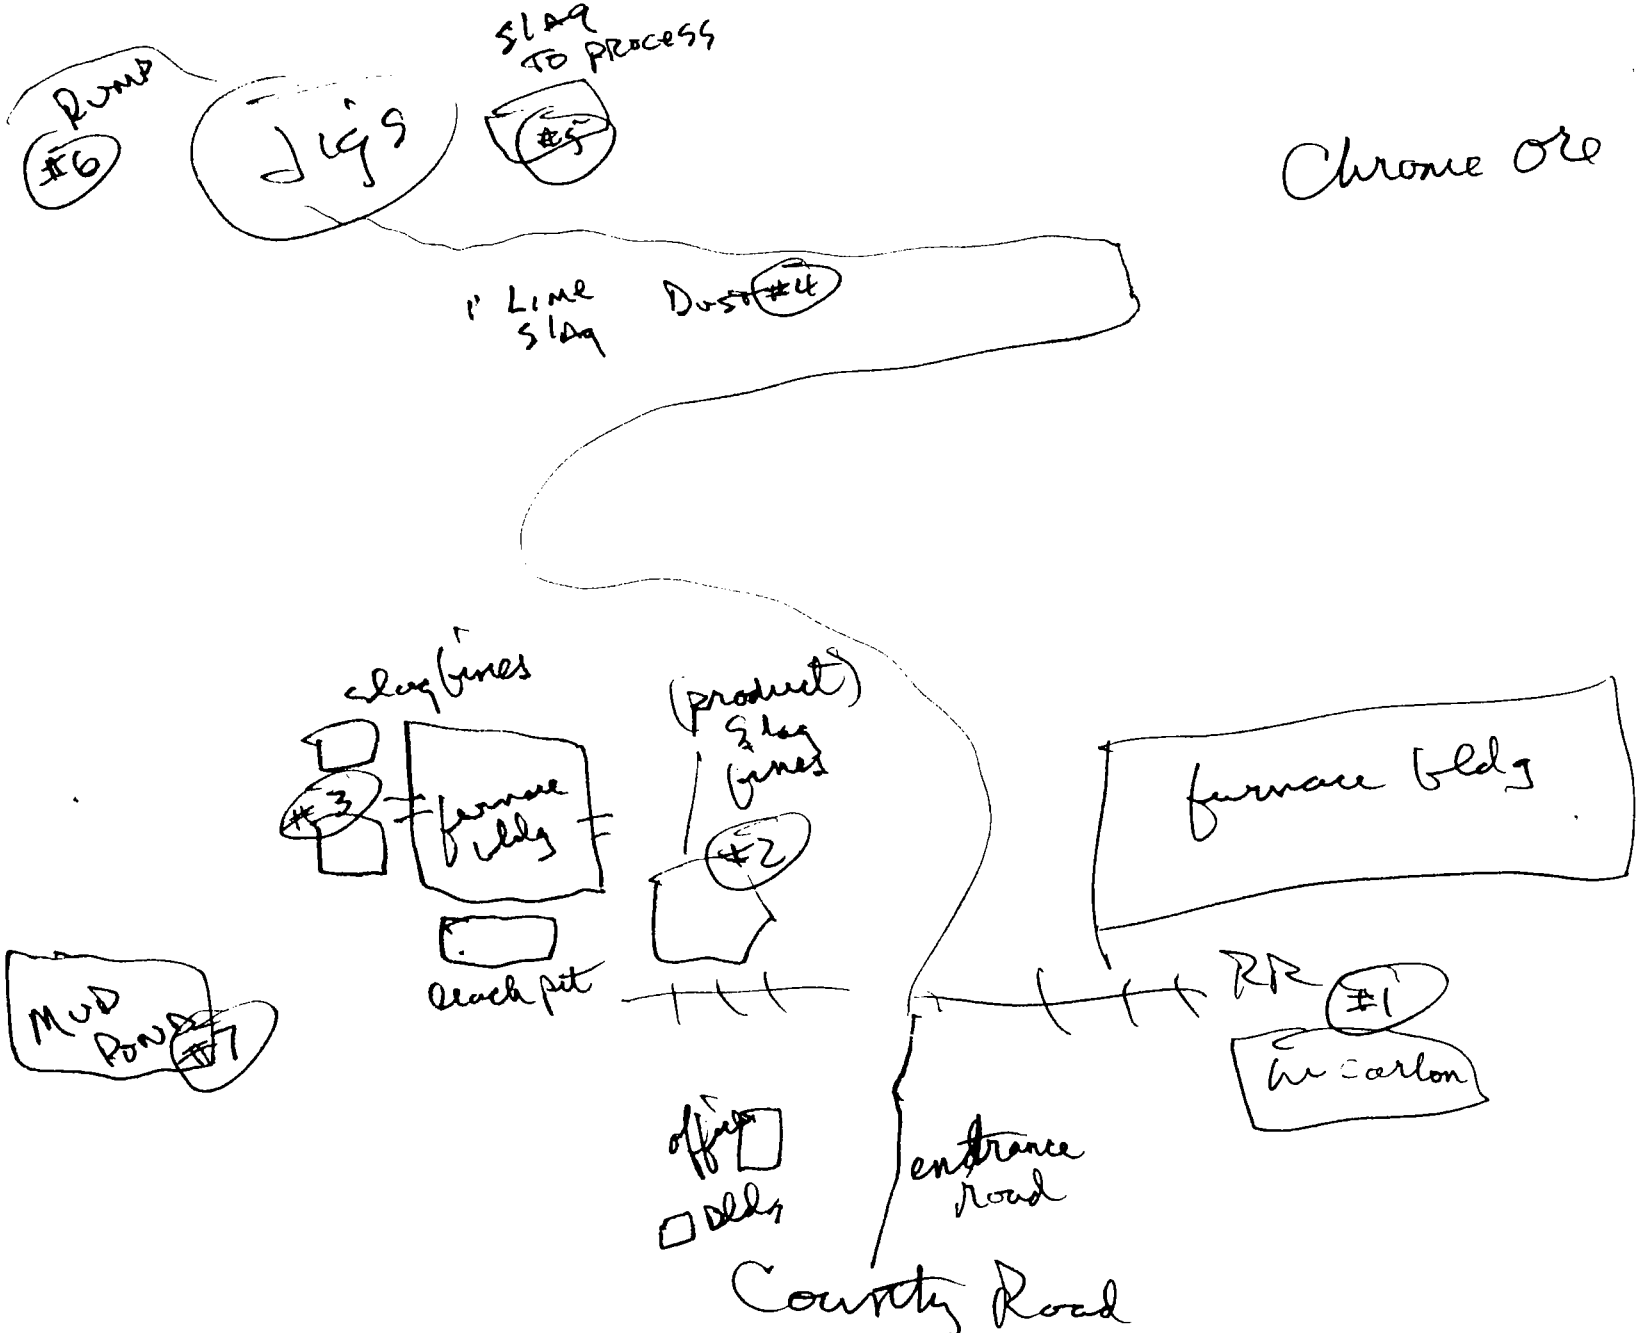
Chrome Ore
Jigs
Pump
#6
Slag to process
#5
1" Lime Slag
Dust #4
slag fines
#3
furnace bldg
(product) Slag fines
#2
furnace bldg
Mud Pond
#7
Leach pit
RR
#1
in carton
office
bldg
entrance road
County Road

CROSS CREEK
