ORBITRON PRP

T05.9408.019 → T05.9410.019
EOH1042RAA → EOH1042RBA

RECORD

US EPA RECORDS CENTER REGION 5
550846

7530-00-222-3525
FEDERAL SUPPLY SERVICE
(GPO)

DANIEL W. BECK
ALLEN COUNTY SHERIFF

Office:
(419) 227-3535 Ext. 267
FAX: (419) 222-3757

TIMOTHY G. GARLOCK
STAFF SERGEANT
9-1-1 COORDINATOR

ALLEN COUNTY SHERIFF'S OFFICE
333 NORTH MAIN STREET
LIMA, OHIO 45801

J. TOM TILSON
DIRECTOR

OFFICE (419) 227-3535
EXT. 265 - 266
HOME (419) 999-2946
FAX (419) 222-~~4675~~ 3757

ALLEN COUNTY
EMERGENCY MANAGEMENT AGENCY
ALLEN COUNTY CRIMINAL JUSTICE CENTER
333 N. MAIN STREET • P.O. BOX 1243
LIMA, OHIO 45802
CHARLES W. HARROD, SHERIFF

Ohio Department of Commerce
Division of State Fire Marshal

BUREAU OF UNDERGROUND STORAGE
TANK REGULATIONS

8895 E. Main Street
P.O. Box 687
Reynoldsburg, Ohio 43068-0687

(419) 227-2454

Larry Horstman
Fire Safety Inspector

ED JOHANSEN
COUSINS - P.M.

DELPHOS FIRE DEPT.
CHIEF WAYNE SUEVER
419 695 - 2911
FAX 419 692 - 1617

EMA
TOM TILSON
419 227 3535
FAX 419 222 3757

OEPA (NWDO)
JIM OTTARSON
419 352 8461

Sept 30, 1994 ORBITRON T059408019/EOH1042RAA

OSC Rennwager spoke w/ Barry Cousins of Cousins Waste Control Corporation (CWC) who assured OSC that a complete and revised Work / Health & Safety Plan would be delivered by Monday, October 3, 1994.

T059410019/EOH1042RBA

October 3, 1994

Revised work/H&S Plan received by OSC & TAT.

October 5, 1994

TAT Dachtler sends S.A. report analytical to John Glockner (Cousins H&S officer) after OSC approval. The results are needed to help in the completion of the H&S Plan.

October 6, 1994

TAT & USEPA each receive copy of complete Work & H&S Plan from Cousins Eng.

10/6/94

4150
80
1,800

October 13, 1994 ORBITRON T059410019/EOH1042RBA

0830 TAT Dachther arrives on-site

0840 Proj. Mgr. Ed Johansen of Cousins & Delphos F.D. chief Wayne Seuver on site

0900 OSC Renninger arrives on-site. Meeting to discuss plans. Johansen scrp @ 150 drums have been sampled already. Johansen scrp numbering system already in progress. Plan is to stage & sample this week (and possibly next) Than look to disposal. Seuver requests that drums be staged outside of building in case of fire. It is decided that all flammables be staged w/in fenced area in back of building.

0930 OSC, TAT, F.D, & Cousins P.M. tour facility and discuss which drums may go where. Cousins has already numbered MANY (almost all noticeable) drums, containers and boxes of polyethylene resin.

1100 OSC & TAT meet to discuss important safety issues:
- line staging area
- cover outdoor drums
- consolidation where?

1300 Tom Tilson & Tim Garlock from County EMA arrive on-site. ~~etc.~~ To be updated on background of site and to be informed of Emergency procedures/conditions.

BACKNOTE: Delphos Herald arrives on-site (1230 hrs), interviews OSC & takes site pictures. OSC requests that TAT get the article from the paper for the files

Yvon CD

October 13, 1994 ORBITRON TO5941001 9/EOH1042RBA

(cont.) EMA is concerned w/ mixing of incompatible wastes and causing a rxn.

OSC informs EMA ~~that~~ about the three privately owned transformers on the west side of the building. Cousins will be getting rid of them since Ohio Power does not own them. However, Ohio Power has visited the site today and informs OSC, F.D Chief., and Cousins P.M. that they are no longer live.

1400 Cousins is currently moving drums from southernmost pole barns and setting them outside of Warehouse 1. These drums will later be loaded into the truck and then moved to the staging area at the back of the building. County EMA is off-site

1410 OSC ~~after~~ requests that TAT stay until tomorrow at lunch to over-see ERCS (Cousins) activities.

1500 Chief Sewver leaves site and will return in the morning at around 0800 HRS. Crew has staged 18 drums (55-g steel) in the back of the facility. Crew is currently taking a break. JCD

1615 Cousins has staged 19 more drums in back of building for a total of 37 flamm. & waste drums. JCD

Pole barn 1 area is almost clear of drums (flammables)

10/13

October 13, 1994 Orbition T059410019/EOH1012RBA

1800 Cousins staged 22 drums of non-hazardous materials in WAREHOUSE on east side of building (WAREHOUSE STAGING AREA). Building is currently being secured by Cousins and will be checked by TAT. Work will resume tomorrow at 0700 HRS

1820 TAT & Cousins off-site

10/13/94

October 14, 1994 Onbitron T059410019/EOH1042RPA

0700 Currently cloudy and 52°F. TAT and Cousins on-site to begin site activities

BACKNOTE: Yesterday, Cousins collected samples from the three transformers on the west side of the building. The samples will be sent to the lab and analyzed for PCB's.

0730 Two ADDITIONAL LABORERS arrive on-site for Cousins (crew total 1 PM, 1 technician, 3 laborers)

0820 Two laborers are searching the building for drums and containers. Unused, empty drums found on-site will be used to consolidate wastes. Cousins' chemist is currently examining uncategorized wastes before consolidation activities commence.

0900 Chief Sewers arrives on-site. Earlier, the tow motor blew a tire, a delay in drum staging, til 0910.

1000 Approximately 10 drums have been moved from the Pole Barn 1 AREA to the front (EAST) dock. They will later be staged in the back of the rest of the drums in the WAREHOUSE. Cousins is using a submersible pump to transfer the non-haz liquids from the open drums in the Pole Barn 1 area into shippable drums

1030 Approximately 100 small containers of paints, thinners, and grease were found in the warehouse "tool area". They are currently sitting outside on the west side of the building. They will later be staged in the back (east side) and consolidated w/ the flammable waste stream.

YCD

October 14, 1994 Orbitron T0594100I9/ EOH1042 RB4

1040 Crew takes a 10-minute break

1100 TAT departs site and calls OSC Renninger to inform him of the progress. TAT has requested ~~that~~ Chief Sawyer to pick-up a copy of today's Delphos Herald for the files (NOTE: today's issue doesn'e come out until 1400 hrs.) Chief Sawyer will be periodically checking up on the ERCS crew. The crew will finish out the day staging and searching for drums and containers. Some consolidation activities may take place. They will return on Monday 10/17/94 at 0700 to continue site activities.

10/14/94

October 17, 1994 Orbitron T059410019/EOH1042RBA

1500 TAT on-site to oversee CWC activities. Chief Sewer of the Delphos F.D. is already on-site.

1600 So far today, two approximately 1500g UST's were identified along the west side of the facility. It has not yet been determined if they contain heating or diesel ~~[illegible]~~. One of the tanks has already been uncovered. Samples will be pulled tomorrow and haz-catted by TAT.

BUSTR has been contacted by Chief Sewer to inspect the tanks to determine if they fall into their jurisdiction. An inspection is scheduled for tomorrow afternoon. City Labor was used to uncover the tank w/ a backhoe. The warehouse staging area now contains 78 drums of non-haz. material, about 60 small drums, containers & boxes of non-haz material for BBC, and 10 drums and containers of both oxidizing & corrosive materials. On the outside staging area, approximately 120-150 small containers of flammable materials have been staged ~~[illegible]~~ w/ the 37 flammable drums. To the northwest of these, 64 55-gallon MT drums and approx. 30 small containers (MT) have been staged. See diagram on next page.

Frank C. Dackett
10/17/94

October 17, 1994 ORDITRON TOS941001G/EOH1Ø42RBA

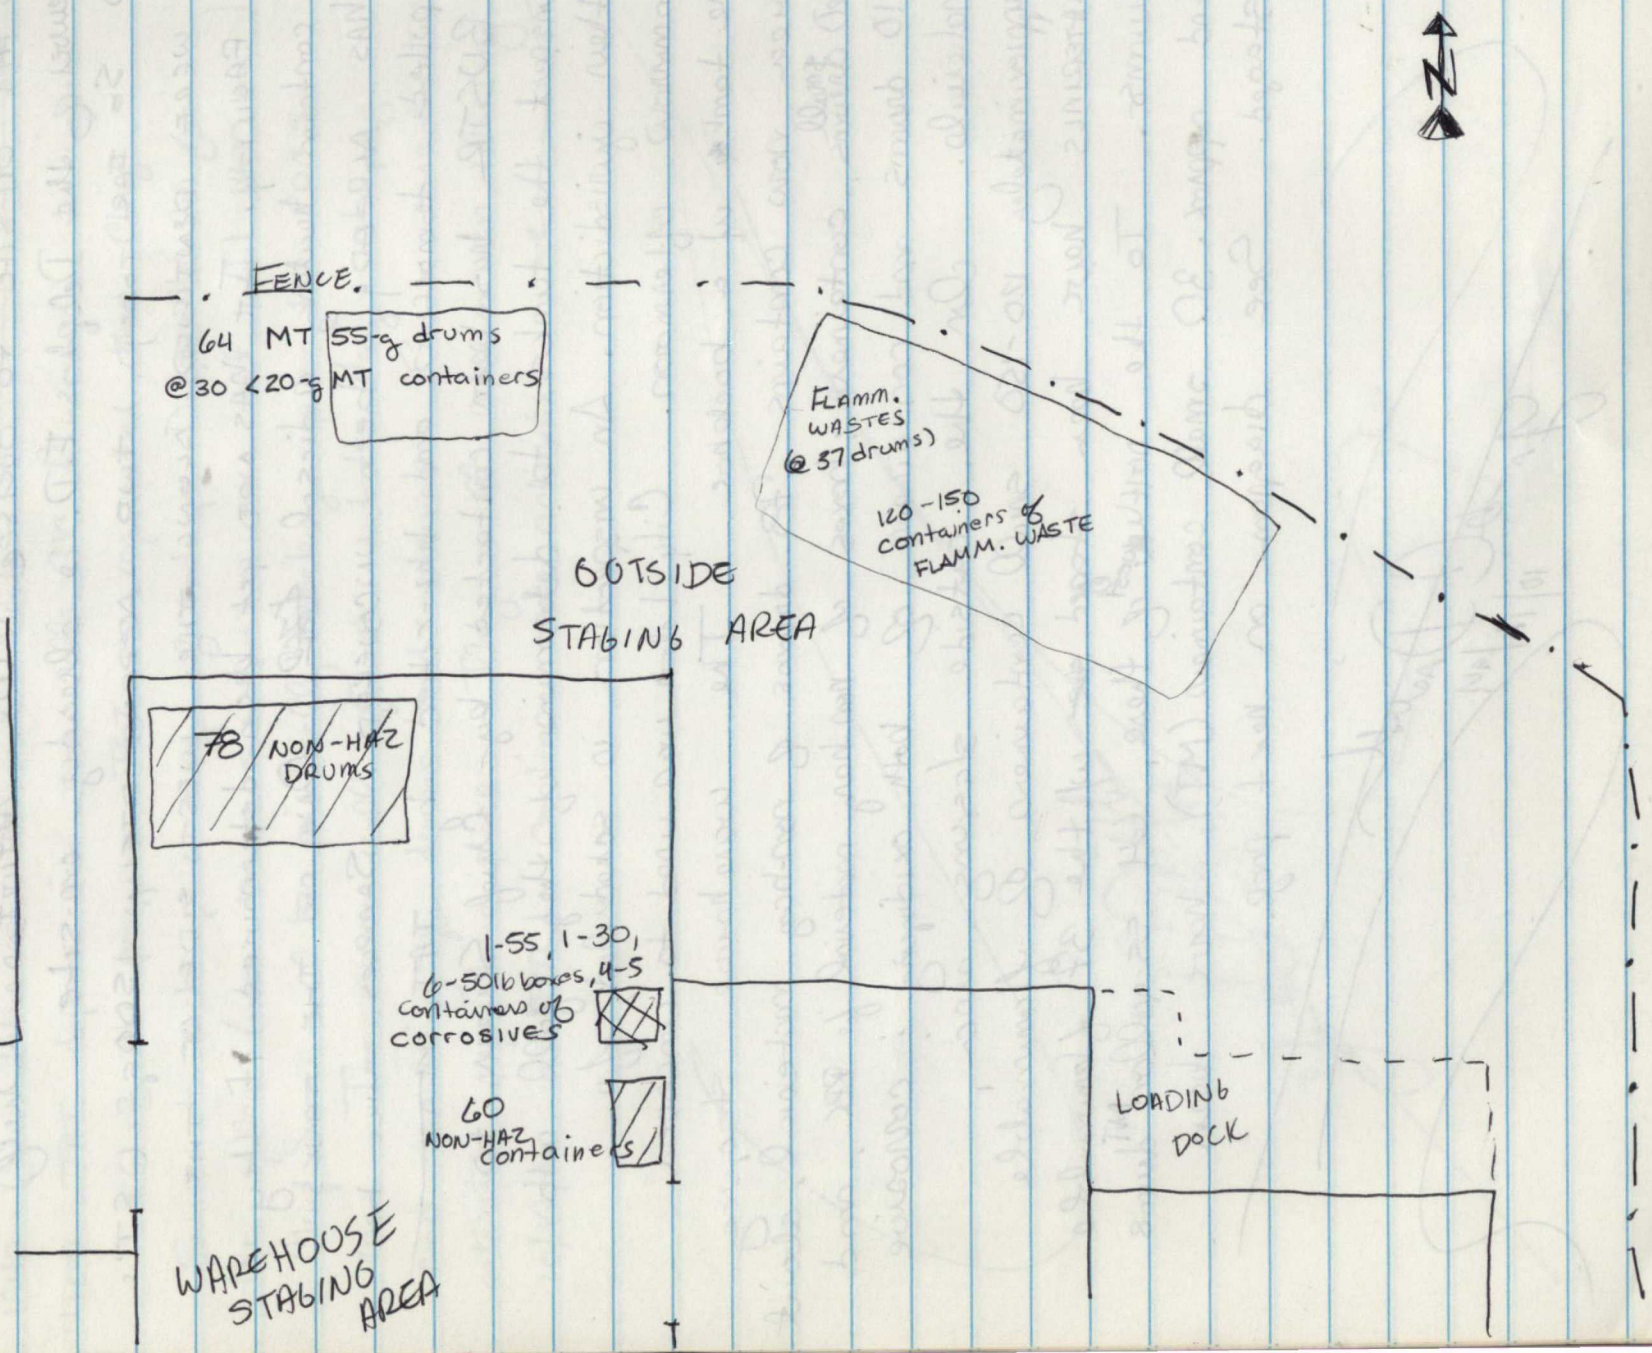

October 17, 1994 ORBITRON T059410019/EOH1042RBA

1630 Cousins is removing the drums from the oil house by truck, & staging them in the rear, outside staging area. Many of the neutral liquids have already been pumped out of their ~~&~~ non-shippable containers and into more suitable containerization. Many of the flammable WASTES have already been consolidated.

1730 BACKNOTE: TAT called OSC Renninger at 1645 to UPDATE ON site activities. OSC WAS NOT IN.

Cousins ~~sec~~ secures site for evening, i.e. locks gates and buildings, nails up boards on oil house, bolt sliding doors from inside, secure machinery in back drum staging area. YCD

1800 Cousins & TAT off-site. Will continue tomorrow at 0730 Hours.

Frank C. Dachtler 10/17/94

October 18, 1994 ORBITRON T059410019/EOH1042RBA

0715 TAT: Cousins arrive on-site & unsecure building. todays weather forecast → 68°F, SUNNY. Currently @ 56°F w/ clear skies. JCD

0840 TAT CALLS CLEVELAND TAT OFFICE. About 4 drums attached to pumping machines were removed from pole barn 4 with about 5 other 55-g drums. These were staged in the back on the loading dock until the machines can be removed. All of these drums will be staged w/ the flammables. Proj Mgr (P.M.) Ed Johansen of Cousins informs TAT of the situation w/ the boxes of solid polyethylene. These are non-haz and Cousins plans to stage these ~~drums~~ boxes in a northwest room w/in the facility. They will remain there until Cousins returns for disposal and will then consolidate the materials into a roll-off box. Cousins is haz-cutting the materials as they are brought in for staging JCD

1025 Cousins has staged the majority of the drums and containers in the facility to the staging areas in the back and outside. The boxes (approx 23 800-lbs) will be left until disposal since they're close together on the back of the building. Cousins plans on completing work today, after labeling the drums, containers, and boxes. NOTE: 4 unused overpack drums were found in a loft storage area in the facility. Cousins will leave them stand due to the large amount of debris around them. NOTE: TAT has called OSC.

10/18/94

October 18, 1994 ORBITRON TØ5941Ø019/EOH1Ø42RBA

1Ø4Ø Additional containers (approx 10, 5g pails) have been ADDED to the 60 NON-HAZ containers in the staging area.

1130 Contacted OSC Renninger to update on site activities. OSC requests that USTs be SAMPLED. —— JCD ——

1200 Cousins is currently labeling the drums in the WAREHOUSE staging area. The ~~OPP~~ P.M. and operator are consolidating the small containers of flammables into the flamm. drums in the staging area. —— JCD ——

1300 Chief Sewer and BUSTR inspector LARRY HORSTMAN arrive on-site to inspect UST's found on the west side of the building. Horstman says that since the tanks are heating oil, they do not fall under BUSTR jurisdiction. Chief Sewer will have to cite Orbitron on other grounds, i.e. tank certifications, fire code violations, location in sensitive area for drinking WATER.

1400 Sewer & Horstman leave site. Cousins is continuing the consolidation, staging & labeling of the drums in the back (east) of the facility. —— JCD ——

1540 The current count for staged drums stands as follows: 80 MT 55-g, and @80 MT <30-g; 47 FLAMM. 55-g, 25 <5-g; 4Ø NON HAZ<2Ø-g; 12 CORROSIVE (OR) OXIDIZER boxes, drums & CONTAINERS; and 93 NON HAZ 55-g drums. Cousins is almost through w/ staging, LABELING & CONSOLIDATION & WASTESTREAMS.

10/18/94

October 18, 1994 ORBITRON T05941ØØ19/EOH1Ø42RBA

1600 TAT: Cousins P.M. Johansen contact OSC Renninger to update him on site activity. Johansen says that crew will demobe tonight and return in about 2-3 weeks for the disposal of the site wastes

1915 off-site (TAT: Cousins) site secured labeling and consolidation of staged drums complete. (Further consolidation of boxes of polyethylene solid.

Mark C. Ladd 10/18/94

NOVEMBER 22, 1994 ORBITRON T05941001 9/EOH1042 RBA

1500 TAT talks to Barry Cousins of Cousins Env. Serv. Mr. Cousins says that his company is awaiting a reply from Jeffe & Tom Cooper of Orbitron to allocate funds for the disposal of site wastes.

Frank C. Dreth
11/22/94

Jan. 9, 1995 EOH1042RBA

0830 TAT Uddin arrived on-site.
0900 Uddin met with Ed Johansen (Cousins) and fire representative Ron M.
0915 Uddin and Ed Johansen conducted a walk through inspection of the site in level 'D'.

TAT Uddin photo/video documented the site.
Approximately fifty drums are staged outside the building along the fence. Approximately 150 empty drums are also staged. Some of the drums are rusted and they are not overpacked. All drums were labeled. These drums will be shipped to a disposal facility without overpacking.

0945 Another Cousin's crew member arrived on site.
10:00 The on-site work is on hold.
Ed J. told Uddin that the PRPs check to the Cousins was bounced and Cousins is trying to get hold of the PRPs. The waste will not

1/9/95

Jan. 9, 1995 EOH1042RBA

be shipped to the disposal facility unless the Cousins are paid.

Approximately hundred (100) non-hazardous waste drums are staged inside the building

TAT Uddin called Barry Cousins to find out more about the site situation He told Uddin they are sending two semi trucks.

1145 The Crew is doing paper work and labeling drums for shipping

1300 The Crew is loading drums into the semi-truck. Another truck is scheduled to be on-site this afternoon.

1330 The Crew is working on paper work and labeling drums for shipping

1415 The second semi-truck is on site and the Crew is loading drums with the loader.

1545 The Crew is loading empty drums into the semi.

All empty drums were loaded on top of the liquid drums and the

HDY 1/9/95

Jan. 9. 1995 EOH1042RBA

truck left site.

1600 The Fire Chief is on-site. Cousins is not shipping PCB Contaminated transformers and polymerized polyethylene because they did not have an OK from the PRPs.

1745 All flammable drums and non-hazardous liquid waste drums were shipped. Only a few empty drums are left on-site. The will be shipped tomorrow. TAT Uddin left site and drove back to Cleveland Office.

Harry Jd
1/9/95

March 7, 1995, EOH1042RBA

weather = Rainy 65°F

0800 Uddin left Office to go to Orbitron Site.

1200 TAT Uddin arrived on-site.
Uddin met with Robert L. (Cousins)
he brought samples that were on hold and dumped them back into the transformers - because their were not analyzed.
Uddin offered split samples to R.L, but he declined.

1230 NO lunch break

1245 TAT Tom Spargo and Jim Ottarson (OEPA) arrived on-site.
Uddin and Spargo preparing for PCB transformer sampling in level 'B' protection.

1300 Uddin collected sample T#1, T#2 and T#3.
Spargo video/photo documented the site and assisted Uddin during sampling.

1330 Uddin & Spargo deconing the sample bottles.

Uddin
3/7/95

March 7, 1995 EOH 1042 RBA

1400 Tom Sparzo left the Site.
1430 Uddin filled out the C.O.C
and loaded the Vehicle.
1500 Uddin left PPE & trash
at the Site.
Uddin left the Site for
Cleveland.

Hdm 3/7/95
