Phase 3   Set-up 37

Location: Building 3 Roof Parapets
                Building 4 North Elevation
                Building 5A North Elevation

Stories: Building 3 - 1
                Building 4 – 2
                Building 7 - 2

Material: Building 3 – Steel Parapet Flashing
                Building 4 – Brick
                Building 5A – Brick

Square Feet: Building 3 Parapets= 540
                Building 4 N. Elevation = 800
                Building 5A N. Elevation = 722

Tenants: Commercial

C/B Zone: Yellow

Roof Drain: Bldg 4&5A - Scupper to downspout, to
                Roof below
                Bldg 3 – Scupper to downspout,
                tightlined to drain
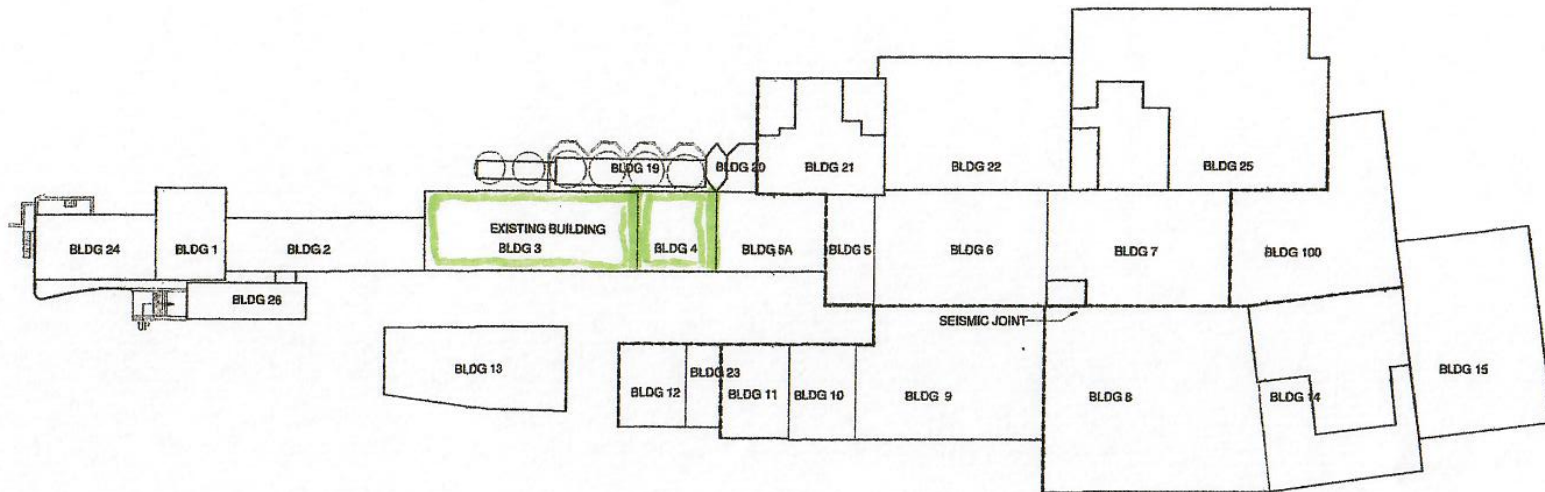
Roof Protection: Bldg 4&5A-Reroute with flex pipe and
                   filters to lower roofs   Bldg 3 – Plug and
                   protect opening through parapet

Additional Protection: Protect parapet walls on the opposite side of the areas being abated by applying a single layer of 6-mil poly, attached to the building utilizing duct tape on all four surfaces, where it is safe to do so.

On parapet walls that cannot be safely sealed, apply one layer of 6-mil poly, attaching to the top of building with duct tape. The bottom edge shall be weighted, to allow the poly to drape at least one foot lower than the height of the parapet wall. During abatement operations, a safety monitor will continuously observe the draped area, immediately notifying the abatement supervisor should any visible dust be detected.

Skylights and Doghouses will have one layer of 6-mil poly applied directly to the interior surfaces adjacent to the abated areas.   A secondary protective layer of 6-mil poly will be applied horizontally, at the interior base

(bottom) of each skylight/doghouse. Protection will be held in place utilizing duct tape and/or spray adhesive.
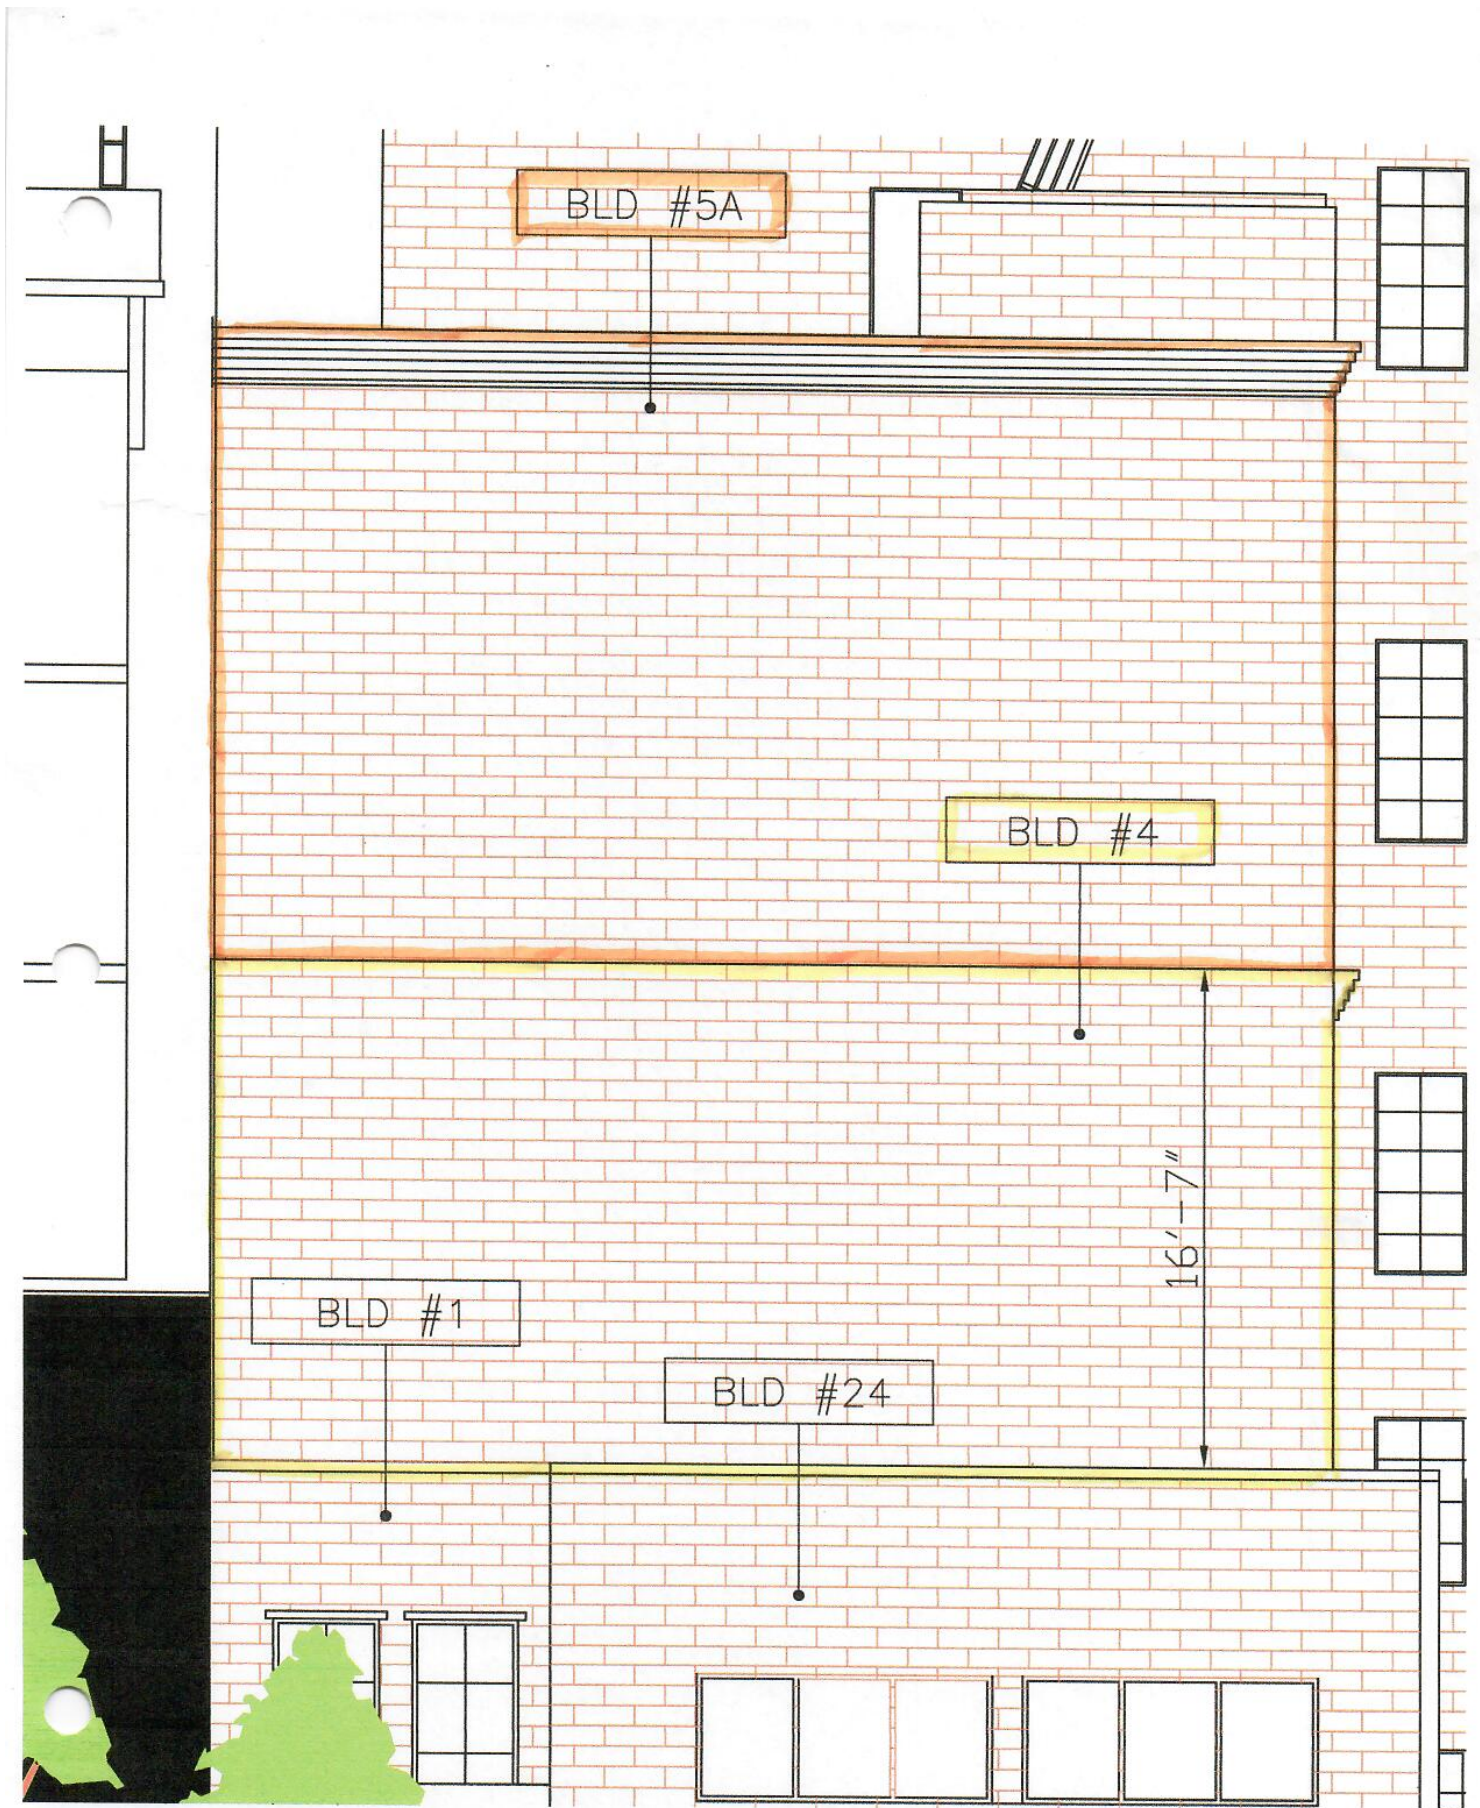
BLDG 24   BLDG 1   BLDG 2   EXISTING BUILDING BLDG 3   BLDG 4   BLDG 5A   BLDG 5   BLDG 6   BLDG 7   BLDG 100

BLDG 19   BLDG 20   BLDG 21   BLDG 22   BLDG 25

BLDG 26

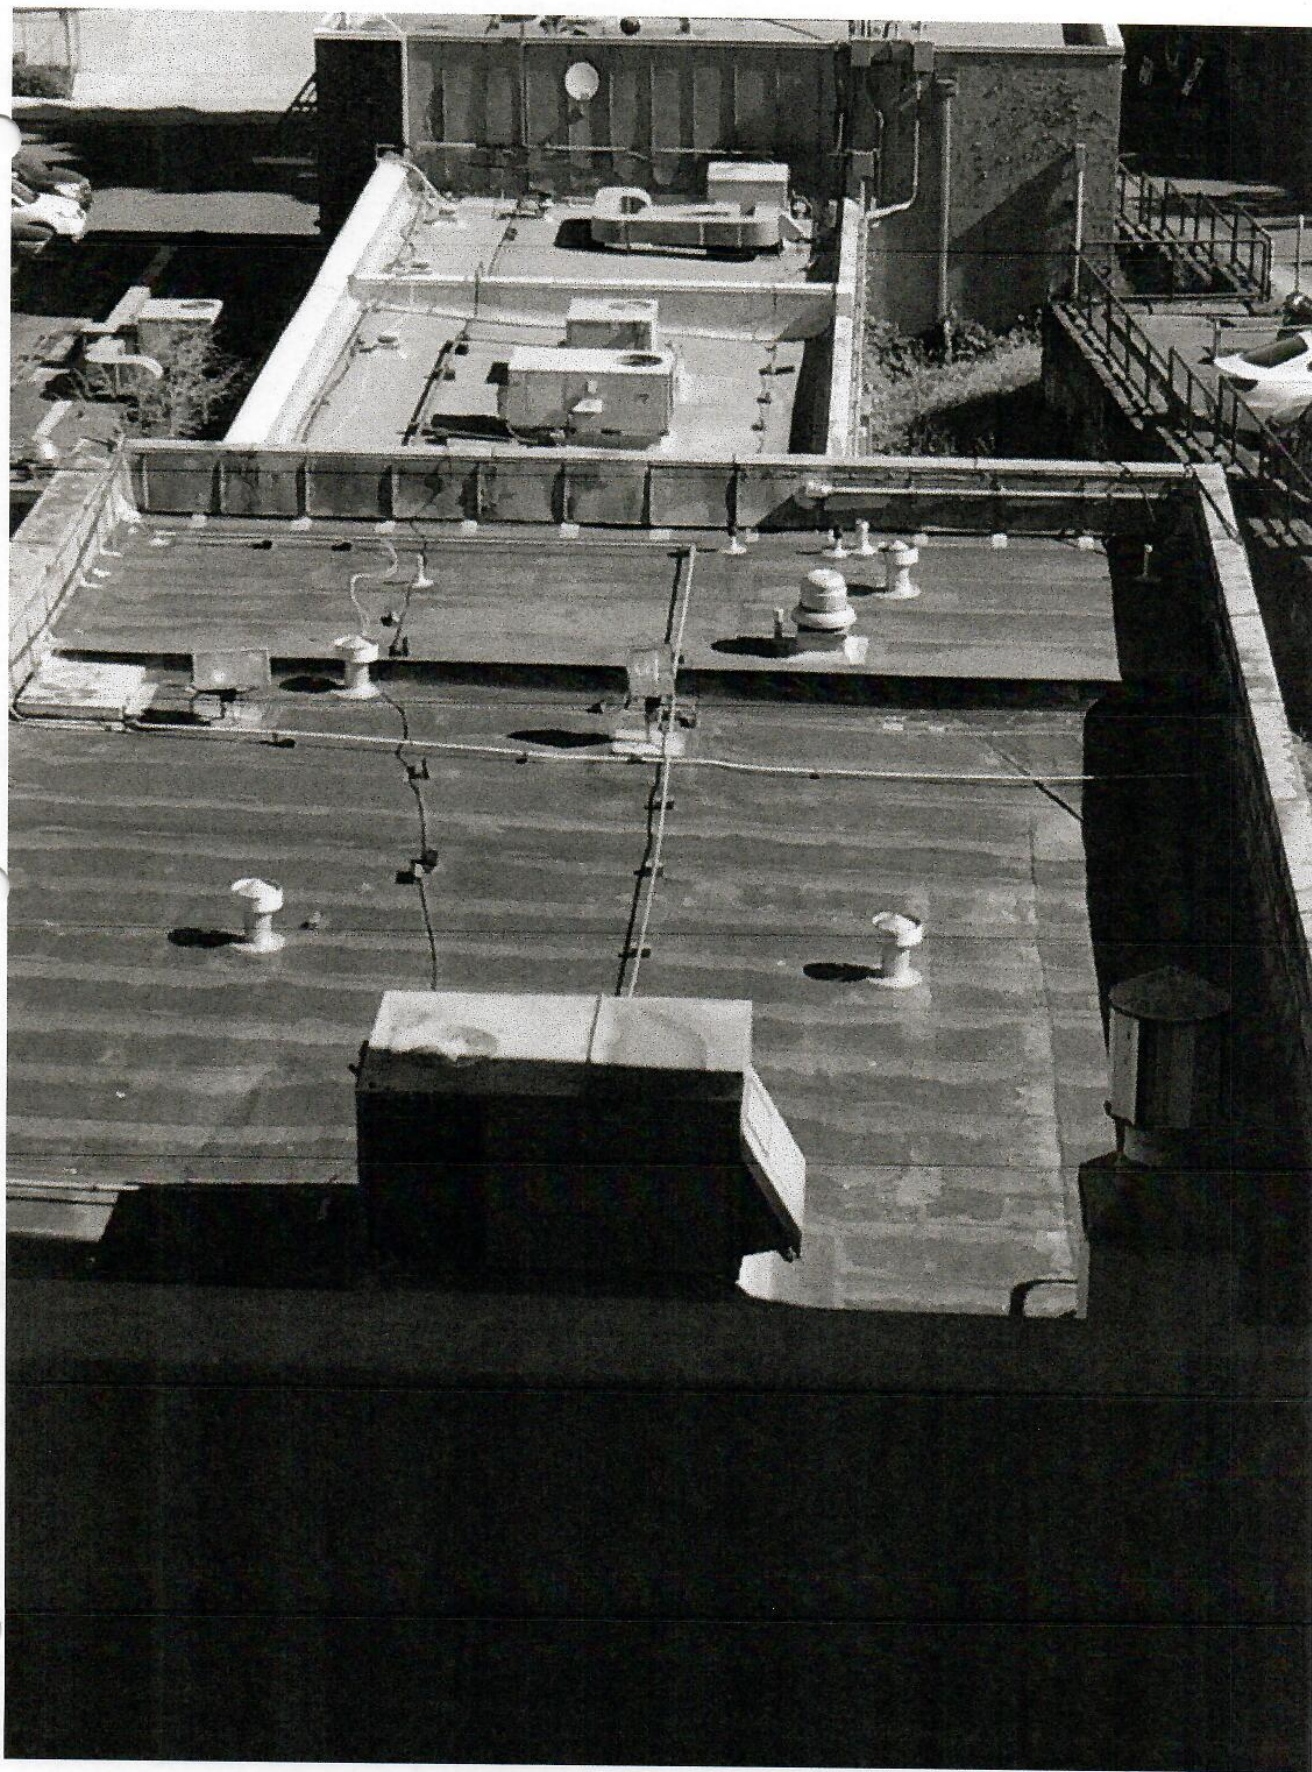BLDG 13   BLDG 12   BLDG 23   BLDG 11   BLDG 10   BLDG 9   BLDG 8   BLDG 14   BLDG 15

SEISMIC JOINT

Building 3, Roof, Parapet

Building 4, Roof, Parapet — COMPLETE

Building 4, North Elevation

Building 5A, North Elevation

BLD #5A

BLD #4

16'-7"

BLD #1

BLD #24

RCLLC 0011234

3 - ROOF - PARAPET

PHASE THREE, SETUP 37
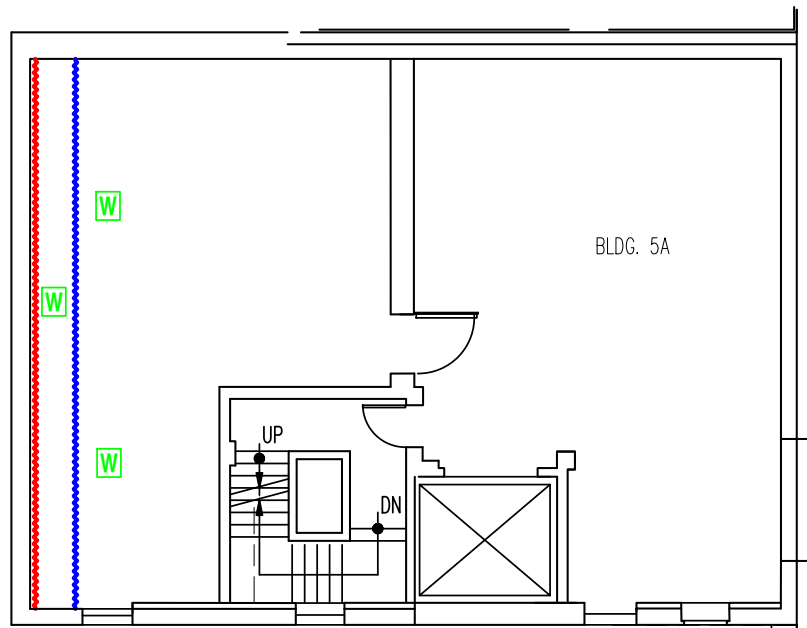## BUILDING 5A, 500 LEVEL

NORTH ELEVATION

INTERIOR CONTAINMENT, WIPE SAMPLING LOCATIONS

OCCUPANCY TYPE: NON-RESIDENTIAL

N

10'-0"
(REF)

BLDG. 5A

W

W

W

UP

DN

RCLLC 0011236

INTERSTATE 5 (WSDOT LAND)

36" DIAM. CONC. PILLAR

S 01°23'38" W 200.41'
S88°31'40"E
L=373.92'
R=5630.58
N07°58'36"E 236.40'

8" PVC   CB13   8" PVC
8" PVC   CB18   8" PVC

RD15   MH9 (CB7)   DS9   RD14
RD47   CB19   D1   D2   D3   D4   D5   6" CI   12" & 4" CI   DS3
RD5   12" CI   42" CI   RD16   RD17
RD4   BLDG 19   RD13   D15   CB17 (SD12)   SD2   RD7   RD8   RD9
RD3   CB20   D10   D9   D8   RD18   DS10   DS4   RD6
RD2   D7   D6   DS11   OLD RD 2" FROM FLOOR
MH124   DS1   DS14   DS13   BLDG 21   TRENCH DRAIN

BLDG 1
BLDG 2
BLDG 26
BLDG 3
BLDG 4
BLDG 5A
BLDG 22
BLDG 25
BLDG OVERHANG

CB14   6" CI   SD1   MH10 (CB8)   DS12   DS6   DS7   D11   D12
MH7 (SD7)   CD15 (SD8)   MH9   CB16 (SD9)   DS15   BLDG 5   DS2   DS3   RD10   RD11
RD40   BLDG 6   DS8   RD12   DS-K   RD31   RD32
RD42   BLDG 13   RD19   BREAKS IN WALL   RD30   RD33
RD41   RD44   RD43   DS16   RD20   BLDG 7   RD29   BLDG 18 (DRAINS ON BLDG 18 GO INTO BUILDING)   RD34   D13   D14
RD46   ELEC.   RD28   RD35
BLDG 23   BLDG 12   BLDG s   ASSUMPTION- THIS IS ALL COMBINED SANITARY SEWER   BLDG 8 (LOWER)   RD27
HOLE IN WALL   8" CI   DS17   RD21   RD25   RD26
RD45   BLDG 11   BLDG 10   RD23   DS18
CB5   BLDG 9   RD22   RD24   DS19   BLDG 14 (DRAINS ON BLDG 14 GO INTO BUILDING)

CB2   4" PVC
S 15°54'39" W 347.29'
CB3 (BNSF CB2)   RAIL ROAD RIGHT-OF-WAY   4" PVC
S 01°10'06" W 240.32'   6" CI   MH1 (CB17)   4" PVC   ?   8" CI
CB4   12"   MH2 (CB14)   12" C
S 14°53'15" W 56.16'   MH3 (CB15)   4" CI   MH5 (BNSF CB2)   RD36
S 12°52'24" W 58.82'   2 8" TC   12" CI   MH4   12" C   12" CI   RD39   RD38
6x1200o 4160v Private Vault   City Light Transformer   12" CI   MH6 (BNSF CB4)   12" & 8" CI   CB16   8" CI   RD37
N 18°15'18" E 83.55'   N 08°29'20" E 92.71'   4" & 6" PVC
S 01°10'06" W 641.94'   N 88°10'52" W 15.62   FND. M.I.C. VISITED: 9-11-03

AIRPORT WAY S.

BLDG 15

N   1" = 30'   15   0   30

RCLLC 0011237

RAINIER COMMONS SURFACE WATER DRAINAGE FLOW MAP
ING 6" DIA. DRAIN LOCATED SOUTH OF BLDG. 25 (D11-D14)
ING 6" DRAIN LOCATED NORTH OF BLDG 25 (D15)

REMARKS

DESIGNED BY: AEM
DRAWN BY: PJR
SHEET CHK'D BY: PJM
CROSS CHK'D BY:
APPROVED BY:
DATE: JANUARY 2009

CDM
Camp Dresser & McKee Inc.
11811 N.E. 1st. Street, Suite 201, P.O. Box 3885
Bellevue, Washington 98005
Tel: (425) 453-8383
consulting · engineering · construction · operations

VERIFY SCALE
THIS BAR IS ONE INCH LONG AT FULL SCALE

RAINIER COMMONS LLC
3100 AIRPORT WAY S
SEATTLE, WASHINGTON

CATCH BASIN STUDY
