Monthly Progress Report #33
March 2007

Falcon Refinery Superfund Site
Ingleside
San Patricio County, Texas
TXD 086 278 058

Prepared for

National Oil and Recovery Corporation
3717 Bowne Street
Flushing, NY 11354

April 10, 2007

Prepared by

KLEINFELDER
3601 Manor Road
Austin, Texas 78723

9568683

TABLE OF CONTENTS

1.0 INTRODUCTION.....2

2.0 COMPLETED ACTIVITIES 2

2.1 Removal Action Activities 2
2.2 Remedial Investigation / Feasibility Study (RI/FS) 2

3.0 CHANGES MADE IN THE PLANS DURING THE REPORTING PERIOD 3

4.0 COMMUNITY RELATIONS.....3

5.0 CHANGES IN PERSONNEL DURING THE REPORTING PERIOD 3

6.0 LIST OF PROJECTED WORK FOR THE NEXT TWO MONTHS 3

6.1 Removal Action Work Projected for the Next Two Months……3
6.2 RI/FS Work Projected for the Next Two Months…….3

7.0 LABORATORY / MONITORING DATA.....3

LIST OF FIGURES

None this reporting period

LIST OF TABLES

Table 1 Hazardous Liquid Waste Disposal……..4

Table 2 Metal Disposal……...5

Table 3 Contaminated Soil and Oily Debris Disposal……5

Table 4 Oil and Filter Disposal……..6

LIST OF APPENDICES

Appendix A Wendel Pipeline Location Report……7

1.0 INTRODUCTION

This thirty-third Monthly Progress Report is submitted in accordance with the Falcon Refinery Site Administrative Orders on Consent for Removal Action and Remedial Investigation / Feasibility Study between the U.S. Environmental Protection Agency (U.S. EPA) and National Oil and Recovery Corporation (NORCO).

This Monthly Progress Report and subsequent reports will address activities associated with both of the orders.

The next monthly progress report, covering March 2007 will be submitted on or before May 10, 2007.

2.0 COMPLETED ACTIVITIES

2.1 Removal Action Activities

During the month of February approximately 152,493 gallons of liquid waste were removed and properly disposed from Tank 27. To date a total of approximately 5,900,115 gallons of hazardous waste have been removed from all of the above ground tanks and disposed of at the Texas Molecular deep well injection well.

Prior to the beginning of liquid waste disposal in October 2004, the volume of waste in the above ground storage tanks was measured at 6,844,094 gallons. Subtracting the current disposal volume indicates that there may be 1,043,984 gallons remaining in the tanks. However, due to holes in the tops of the tanks the volume of waste may have increased due to rainfall or may have decreased due to evaporation.

Original waste manifests are available at the Kleinfelder office in Austin. A compilation of hazardous liquid waste disposal is included as Table 1.

Wendel and Associates was contracted to trace the pipelines from Sunray Road to the former barge dock facility. A copy of the report showing the pipeline route with photographs is included as Appendix A.

NORCO is in the process of obtaining bids to uncover the pipelines at the former barge dock site and to remove the contents of the pipelines, if any.

2.2 Remedial Investigation / Feasibility Study (RI/FS)

The RI/FS Work Plan, Quality Assurance Project Plan, and Field Sampling Plan were conditionally approved by the EPA pending the completion of modifications to the plans. NORCO will provide final copies of all work plans to the EPA and trustees by May 11, 2007.

3.0 CHANGES MADE IN THE PLANS DURING THE REPORTING PERIOD

None this reporting period.

4.0 COMMUNITY RELATIONS

The EPA has developed a web site to display information about the Removal Action and RI/FS activities. The can be found by going to www.epaosc.net and selecting web sites, then Region 6 and then the Falcon Refinery Site.

A sign showing contact information and the website has been posted in front of the refinery.

5.0 CHANGES IN PERSONNEL DURING THE REPORTING PERIOD

None this reporting period.

6.0 LIST OF PROJECTED WORK FOR THE NEXT TWO MONTHS

6.1 Removal Action Work projected for the next two months includes:

- Continuing the removal and disposal of liquids from the storage tanks and pipelines at the anticipated rate of approximately 150,000 gallons a month;
- Continued site maintenance; and
- Further investigation of the pipelines from Sunray Road to the former docking facility.

6.2 RI/FS Work projected for the next two months includes:

- Preparing modifications to the RI/FS Work Plan and submitting the final RI/FS Work Plan; and
- Preparing modifications to and submitting the Field Sampling Plan and the Quality Assurance Project Plan.

7.0 LABORATORY / MONITORING DATA

None this reporting period.

TABLES

Table 1
Hazardous Liquid Waste Disposal

DISPOSAL FACILITY	ADDRESS	PHONE NO.	EPA ID NO.	CONTACT
Texas Molecular Corpus Christi Services, LP	6901 Greenwood Dr. Corpus Christi, TX	361-852-8284	TXR000001016	Robert Rodriguez

RQ, HAZARDOUS WASTE LIQUID N.O.S., 9 , UN3082, III (D007, D008, D018)

Month	Volume (gal)
October-04	53,832
November-04	734,763
December-04	879,158
January-05	783,881
February-05	551,444
March-05	565,489
April-05	445,107
May-05	471,311
December-05	42,550
January-06	58,740
February-06	59,140
March-06	0
April-06	29,371
May-06	59,018
June-06	97,151
July-06	118,743
August-06	148,509
September-06	109,908
October-06	86,665
November-06	140,498
December-06	85,813
January-07	118,541
February-07	107,985
March-07	152,493
Total	**5,900,115**

Table 2
Metal Disposal

DISPOSAL FACILITY	ADDRESS	PHONE NO.	EPA ID NO.	CONTACT
Commercial Metal Company	**4614 Agnes St Corpus Christi, TX**	**361-884-4071**	**None**	**David**

RECYCLED METAL

Month	Volume (lbs)
October-04	0
November-04	16,820
December-04	19,640
January-05	31,380
February-05	0
Total	**67,840**

FIRE EXTINGUISHERS

Month	Quantity
December-04	10
Total	**10**

Industrial Fire & Safety Co. removed 10 fire extinguishers from the job site.
The powder was disposed of properly and the metal went to salvage.

Table 3
Contaminated Soil and Oily Debris Disposal

DISPOSAL FACILITY	ADDRESS	PHONE NO.	EPA ID NO.	CONTACT
U.S. Ecology Texas L.P.	**P.O. Box 307 Robstown, TX**	**361-387-3518**	**TXD069452340**	**Glenda Felkner**

PETROLEUM CONTAMINATED SOIL AND OILY DEBRIS

Month	Volume (cy)
October-04	0
November-04	0
December-04	40
January-05	0
February-05	0
Total	**40**

RQ, HAZARDOUS WASTE SOLID, N.O.S., LEAD, 9 NA3077, PGIII (OILY SLUDGE AND SOIL)

Month	Volume (cy)
February-05	15
Total	**15**

Table 4
Oil and Filter Disposal

DISPOSAL FACILITY	ADDRESS	PHONE NO.	EPA ID NO.	CONTACT
Texas Molecular Corpus Christi Services, LP	**6901 Greenwood Dr Corpus Christi, TX**	**361-852-8284**	**TXR000001016**	**Robert Rodriguez**

RECYLCED OIL AND FILTERS

Month	Volume (gal)
January-05	403
February-05	0
Total	**403**

DISPOSAL FACILITY	ADDRESS	PHONE NO.	EPA ID NO.	CONTACT
Midstate Environmental Services, LLC	**2203 Tower Road Robstown, TX**	**361-387-2171**	**TXR000051227**	**Lloyd Cooke**

RECYLCED OIL AND FILTERS

Month	Volume (gal)
January-05	16,651
February-05	0
Total	**16,651**

Appendix A

Wendel and Associates Pipeline Report

FALCON REFINERY
LOCATE PL'S @ SUNRAY RD
TO WATERS EDGE
3.21.2007

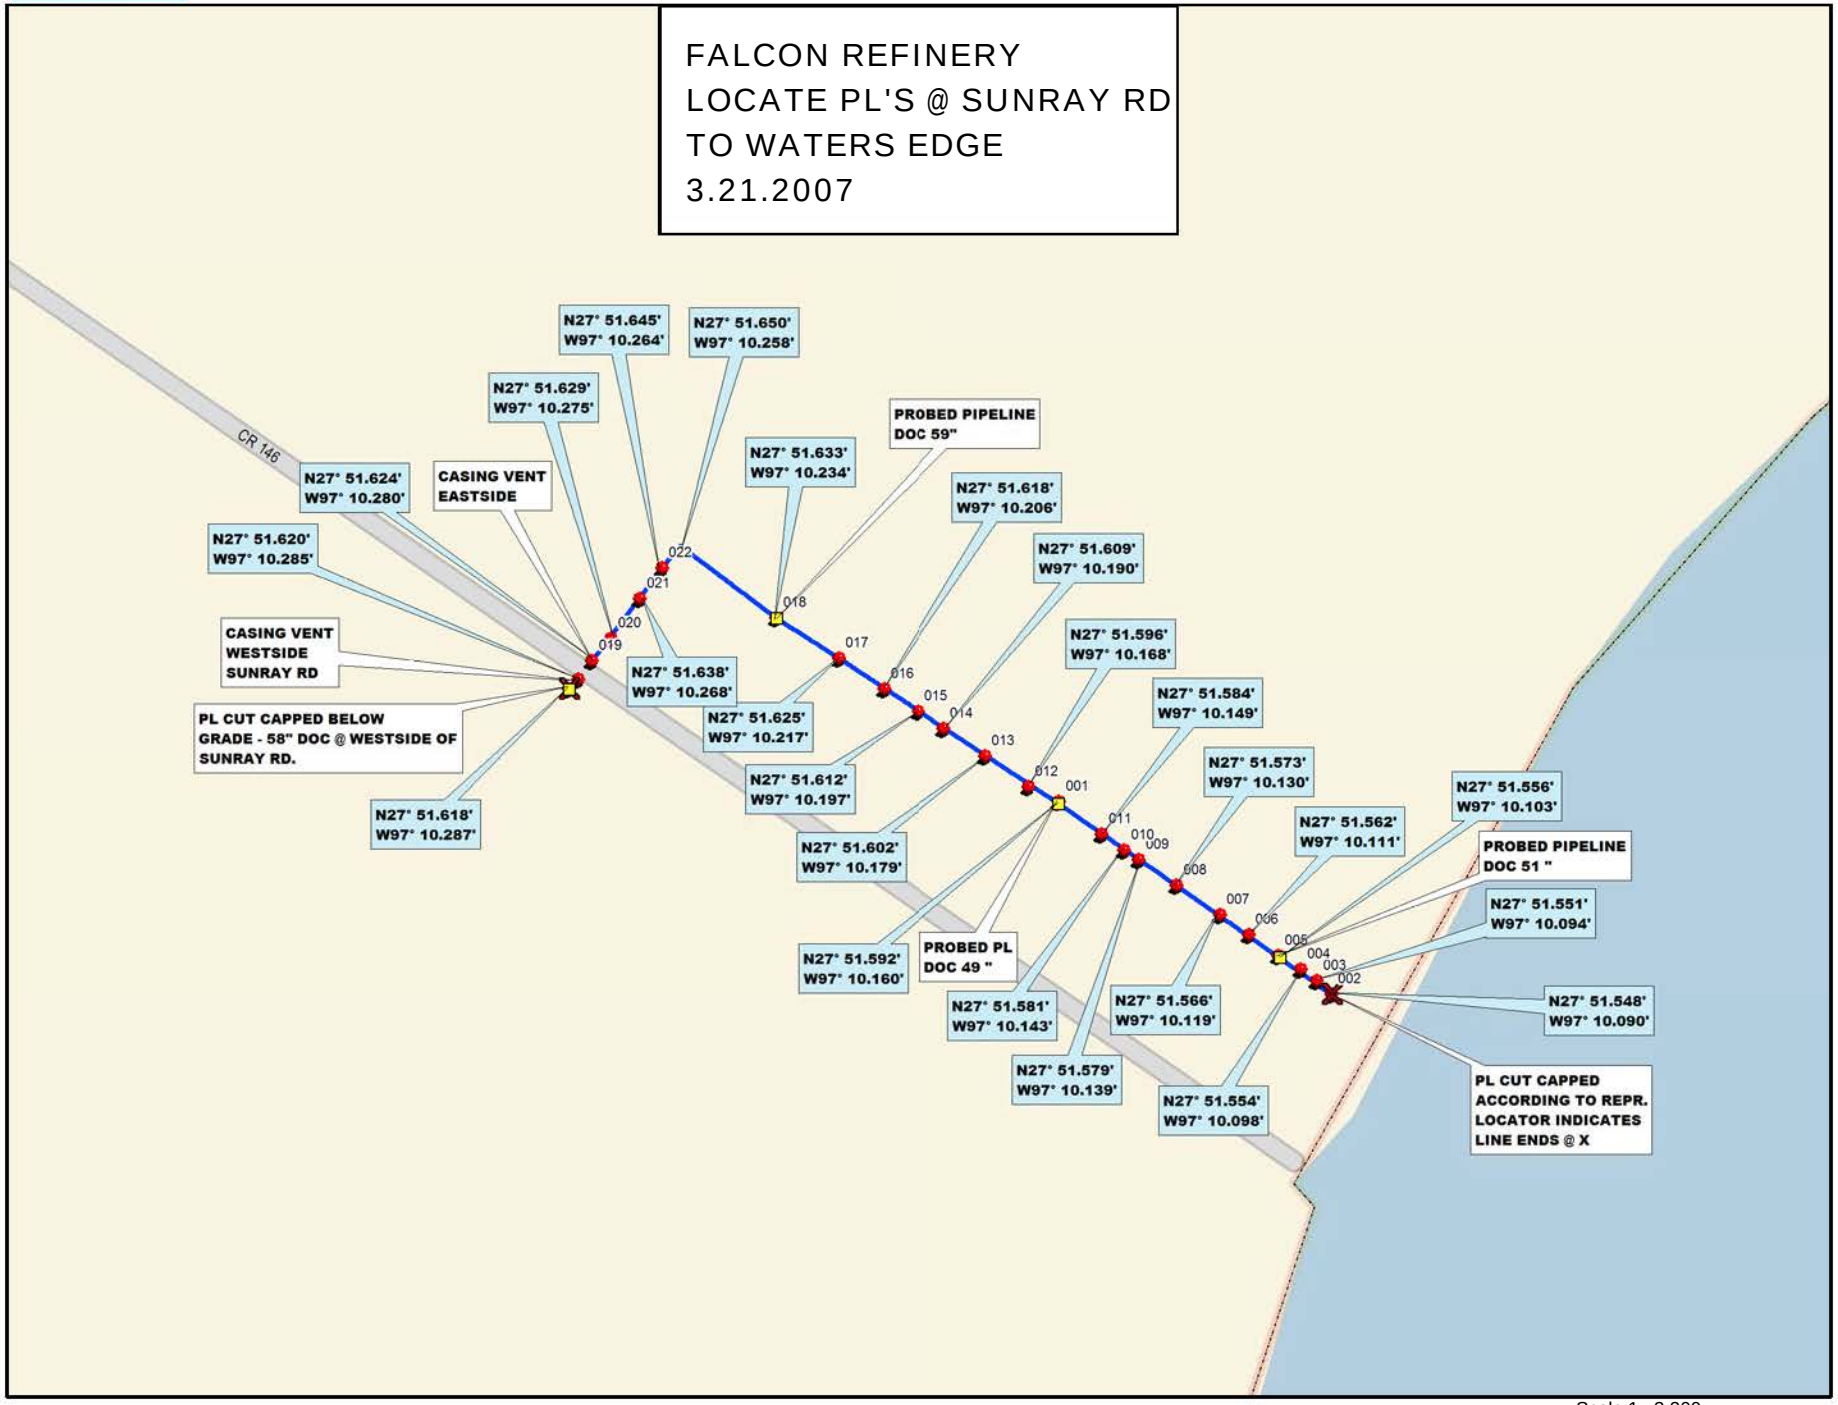

Data use subject to license.
© 2004 DeLorme. Street Atlas USA® 2005.
www.delorme.com

TN
MN (4.8°E)

Scale 1 : 3,200
0 80 160 240 320 400 ft
0 20 40 60 80 100 m
1" = 266.7 ft
Data Zoom 16-0

WENDEL & ASSOCIATES INC.
CORROSION SERVICES
SINCE 1980

FALCON REFINERY
SUNRAY RD AREA
3.21.2007

Office (361) 883-6930 :: Fax (361) 883-6958 :: P.O. Box 1596 :: Corpus Christi, Texas 78403

WENDEL & ASSOCIATES INC.
CORROSION SERVICES
SINCE 1980

FALCON REFINERY
PROBED PL @ STORAGE YARD
DOC 49"
3.21.2007

Office (361) 883-6930 :: Fax (361) 883-6958 :: P.O. Box 1596 :: Corpus Christi, Texas 78403

WENDEL & ASSOCIATES INC.
CORROSION SERVICES
SINCE 1980

FALCON REFINERY
PROBED PL @ STORAGE YARD
LOOKING NORTH WEST
DOC 49"
3.21.2007

Office (361) 883-6930 :: Fax (361) 883-6958 :: P.O. Box 1596 :: Corpus Christi, Texas 78403

WENDEL & ASSOCIATES INC.
CORROSION SERVICES
SINCE 1980

FALCON REFINERY
PROBED PL @ STORAGE YARD
LOOKING NORTH WEST
DOC 55 "
3.21.2007

Office (361) 883-6930 :: Fax (361) 883-6958 :: P.O. Box 1596 :: Corpus Christi, Texas 78403

WENDEL & ASSOCIATES INC.
CORROSION SERVICES
SINCE 1980

FALCON REFINERY
PROBED PL @ STORAGE YARD
LOOKIING @ WATERS EDGE
DOC 55 "
3.21.2007

Office (361) 883-6930 :: Fax (361) 883-6958 :: P.O. Box 1596 :: Corpus Christi, Texas 78403

WENDEL & ASSOCIATES INC.
CORROSION SERVICES
SINCE 1980

FALCON REFINERY
PROBED PL @ STORAGE YARD
LOOKIING @ NORTHWEST
DOC 55 "
3.21.2007

Office (361) 883-6930 :: Fax (361) 883-6958 :: P.O. Box 1596 :: Corpus Christi, Texas 78403
