Contractor: DAVIS | Coordinates: Loc 46 | Project: GILT EDGE | Hole No.: R88-401

Drill Type: Drilltech DH-1 | Casing Depth: | State: SD | Sheet 1 of 6

Hole Size: 5 3/4 | Bearing: | Inclination: -90° | Date Started: 7/22/88 | Property: GILT EDGE

Collar Elev.: | Final Depth: 1040' | Date Completed: 7/26/88 | Hole Surveyed:

Distance (feet)	Alteration (1 Weak, 2 Moderate, 3 Strong)	Total Sulfides (vol %)	Rock Code	Ore Code	Down Hole Location: Distance Down Hole (feet)	Down Hole Location: Elevation	Rock Type	Description: Mineralogy, Alteration, Textures, Grain Size, Fragment Size	Mineralization: Distribution (Massive, Disseminated, Veinlet, Replacement) / Type	Assay: Au	Assay: Ag
			30	1			Edh	0-80 CAMBRIAN DEADWOOD HORNFEL (0-80) green, brown, buff silty hornfel w/ minor qtz veining	0-1040 SULFIDE (0-10) trace FeS_2		
									(10-20) 1% FeS_2 fracture filling		
					20-25						
									(20-30) 4% FeS_2 same		
									(30-65) 2% FeS_2		
					45-50						
									(65-80) 1/2% FeS_2		
					70-75						
			60				Ttp	80-105 TRACHYTE PORPHYRY poorly developed phenos, gray to lt gray matrix.	(80-105) 4% FeS_2		
					95-100						
			30				Edh	105-150 CAMBRIAN DEADWOOD HORNFEL dk brown to dk gray hornfel	(105-115) 1% FeS_2		
									(115-145) 6% FeS_2		
					120-125						
					145-150				(145-150) 15% FeS_2		
							Edq	150-155 DEADWOOD QUARTZITE	(150-155) 6% FeS_2		
							Ttp	155-165 TRACHYTE PORPHYRY	(155-170) 3% FeS_2		
					170-175				(170-175) 4% FeS_2		

DRILL CUTTING LOG

Logged by:

Contractor: DAVIS | Coordinates: Loc #46 | Project: GILT EDGE | Hole No.: R88-401

Drill Type: DRILTECH DH-1 | Casing Depth: | State: SD | Sheet 2 of 6

Hole Size: 5 3/4 | Bearing: | Inclination: -90° | Date Started: 7/22/88 | Property: GILT EDGE

Collar Elev.: | Final Depth: | Date Completed: | Hole Surveyed:

DISTANCE (feet)	GRAPHIC LOGS: ALTERATION (1 Weak, 2 Moderate, 3 Strong)	TOTAL SULFIDES (vol %)	ROCK CODE	ORE CODE	DOWN HOLE LOCATION: DISTANCE DOWN HOLE (feet)	ELEVATION	ROCK TYPE	GEOLOGIC NOTES: DESCRIPTION (MINERALOGY, ALTERATION, TEXTURES, GRAIN SIZE, FRAGMENT SIZE)	MINERALIZATION: DISTRIBUTION (Massive, Disseminated, Veinfill, Replacement) / TYPE	ASSAY Au	ASSAY Ag
			60	1			Ttp	TRACHYTE (cont.)	SULFIDE (cont)		
									(175-245) 1% FeS2		
			40				Edq	185-195 DEADWOOD QUARTZITE			
			60				Ttp	195-205 TRACHYTE			
					195-200			lt gray med. grain			
			40				Edq	205-225 DEADWOOD QUARTZITE			
								lt gray, fine grain qtz			
					220-225						
			10				pE	225-480 PRECAMBRIAN			
								(225-245) banded chert/schist			
					245-250			(245-280) dk brown to black, fine grain siliceous	(245-260) 3% FeS2		
									(260-295) trace		
					270-275						
								(280-) dk green to black			
					295-300				(295-300) 1%		
									(300-340) trace		
					320-325						
									(340-365) ½%		
					345-350			345 @ H_2O HT.			

DRILL CUTTING LOG

Logged by:

Contractor: DAVIS | Coordinates: Loc 46 | Project: GILT EDGE | Hole No.: R88-401

Drill Type: DRILTECH DH-1 | Casing Depth: | State: SD | Sheet 3 of 6

Hole Size: 5 3/4 | Bearing: – | Inclination: -90° | Date Started: 7/22/88 | Property: GILTEDGE

Collar Elev.: | Final Depth: | Date Completed: | Hole Surveyed:

DISTANCE (feet)	GRAPHIC LOGS: ALTERATION (1 Weak, 2 Moderate, 3 Strong)	TOTAL SULFIDES (vol %)	ROCK CODE	ORE CODE	DOWN HOLE LOCATION: DISTANCE DOWN HOLE (feet)	ELEVATION	ROCK TYPE	GEOLOGIC NOTES: DESCRIPTION (MINERALOGY, ALTERATION, TEXTURES, GRAIN SIZE, FRAGMENT SIZE)	MINERALIZATION: DISTRIBUTION (Massive, Disseminated, Veinlill, Replacement) / TYPE	ASSAY Au	ASSAY Ag
			10	1			pE	PRECAMBRIAN (cont.)	SULFIDE (cont.)		
								same	1/2% (cont.) in fractures		
								(355-360) No Return	(365-400) 1% FeS_2		
					370-375						
					395-400						
									(400-480) 2% in fractures		
					420-425						
					445-450						
					470-475						
			20				pEc	480-490 CHERT / white	(480-500) 4% FeS_2		
			10				pEu	490-605 PRECAMBRIAN			
									(500-560) 1% FeS_2		
					495-500						
					520-525						

DRILL CUTTING LOG

Logged by:

Contractor: DAVIS | Coordinates: Loc 96 | Project: GILT EDGE | Hole No.: R88-401

Drill Type: DRILTECH DH-1 | Casing Depth: | State: SD | Sheet 4 of 6

Hole Size: | Bearing: | Inclination: -90 | Date Started: 7/22/88 | Property: GILT EDGE

Collar Elev.: | Final Depth: | Date Completed: | Hole Surveyed:

DISTANCE (feet)	GRAPHIC LOGS: ALTERATION (1 Weak, 2 Moderate, 3 Strong)	TOTAL SULFIDES (vol %)	ROCK CODE	ORE CODE	DOWN HOLE LOCATION: DISTANCE DOWN HOLE (feet)	ELEVATION	ROCK TYPE	GEOLOGIC NOTES: DESCRIPTION (MINERALOGY, ALTERATION, TEXTURES, GRAIN SIZE, FRAGMENT SIZE)	MINERALIZATION: DISTRIBUTION (Massive, Disseminated, Veinfill, Replacement) / TYPE	ASSAY Au	ASSAY Ag
			10	1			pE	PreCambrian (cont.)	Sulfide (cont.)		
								same	same		
					545-550						
								<560-570> abundant qtz veining, possibly	(560-570) 3% FeS_2		
								some Ttp			
					570-575				(570-615) trace		
								(580-605) biotite, mica schist			
								vein qtz present			
					585-600						
			60				Ttp	605-607 TRACHYTE			
			10				pE	607-815 PRECAMBRIAN	(615-635) 1% FeS_2		
								mica schist			
					620-625			<620-650> 10% vein qtz			
									(635-655) 3% FeS_2		
					645-650						
									<660> silver grey sulfide		
									(655-680) 1% FeS_2		
					670-675						
									(680-745) trace		
					695-700						

DRILL CUTTING LOG

Logged by:

Contractor DAVIS | Coordinates LOC #46 | Project GILT EDGE | Hole No. R88-401

Drill Type DRILTECH DH-1 | Casing Depth | State SD | Sheet 5 of 6

Hole Size | Bearing | Inclination -90° | Date Started 7/22/88 | Property GILT EDGE

Collar Elev. | Final Depth | Date Completed | Hole Surveyed

DISTANCE (feet)	GRAPHIC LOGS: ALTERATION (1 Weak, 2 Moderate, 3 Strong)	TOTAL SULFIDES (vol %)	ROCK CODE	ORE CODE	DOWN HOLE LOCATION: DISTANCE DOWN HOLE (feet)	ELEVATION	ROCK TYPE	GEOLOGIC NOTES: DESCRIPTION (MINERALOGY, ALTERATION, TEXTURES, GRAIN SIZE, FRAGMENT SIZE)	MINERALIZATION: DISTRIBUTION (Massive, Disseminated, Veinfill, Replacement) / TYPE	ASSAY Au	ASSAY Ag
			10	1			pE	PRECAMBRIAN (cont.)	SULFIDE (cont.)		
								same			
					720-725						
					745-750				(745-790) 3% FeS_2		
					770-775						
									(790-800) 5% FeS_2		
					795-800						
									(800-815) trace		
			60								
			10				Ttp	815-825 TRACHYTE	(815-845) ½% FeS_2		
			60		820-825		pE	825-830 PRECAMBRIAN			
							Ttp	830-845 TRACHYTE			
								gray fine grain trachyte, very minor pink alt.			
			10		845-850		pE	845-898 PRECAMBRIAN	(845-870) 2-2½% FeS_2 w/ irridescent tarnish		
					870-875				(870-890) trace		

DRILL CUTTING LOG

Logged by:

Contractor DAVIS | Coordinates Loc #46 | Project GILT EDGE | Hole No. R88-401

Drill Type DH-1 DRILTECH | Casing Depth | State SD | Sheet 6 of 6

Hole Size | Bearing | Inclination 90° | Date Started 7/22/88 | Property GILT EDGE

Collar Elev. | Final Depth | Date Completed | Hole Surveyed

DISTANCE (feet)	GRAPHIC LOGS: ALTERATION (1 Weak, 2 Moderate, 3 Strong)	TOTAL SULFIDES (vol %)	ROCK CODE	ORE CODE	DOWN HOLE LOCATION: DISTANCE DOWN HOLE (feet)	ELEVATION	ROCK TYPE	GEOLOGIC NOTES: DESCRIPTION (MINERALOGY, ALTERATION, TEXTURES, GRAIN SIZE, FRAGMENT SIZE)	MINERALIZATION: DISTRIBUTION (Massive, Disseminated, Veinfill, Replacement) / TYPE	ASSAY Au	ASSAY Ag
			10	1			pE	PRE CAMBRIAN (cont.)	SULFIDE (cont.)		
								same			
									(850 - 910) 1½ % FeS_2		
			60		895-900		Ttp	898-975 TRACHYTE			
								(898-910) fine grain greenish gray			
								(910-960) med to dk brownish-gray	(910-960) ½ % FeS_2, ½-1%		
								minor apple grn alt.	dk gray to black mineral		
					920-925						
								(935-940) small inclusions of pE			
					945-950						
								(960-965) greenish gray, coarse Ttp	(960-965) 1 % FeS_2		
								(965-970) med to dk brownish-gray Ttp	(965-970) trace		
								(970-975) greenish gray, coarse	(970-1025) 1 % FeS_2		
					970-975						
			10				pE	975-980 PRE CAMBRIAN			
			60				Ttp	980-992 TRACHYTE			
								(980-985) 30% pE			
								(985-992) greenish gray Ttp			
			10		995-1000		pE	992-1040 PRE CAMBRIAN			
			20					(992-1000) 20% qtz			
								(1000-1013) PC chert			
								(1013-1020) PC schist			
			10								
			20		1020-1025			(1020-1027) PC chert			
			10					(1027-1040) PC schist	(1025-1030) 2-3% FeS_2		
									(1030-1040) tr FeS_2		
					1035-1040						
						HOLE	TD @ 1040'				

DRILL CUTTING LOG

Logged by: [illegible]

Bondar-Clegg, Inc.
12980 West Cedar Dr.
Lakewood, Colorado 80228
(303) 989-1404

BONDAR-CLEGG

Geochemical Lab Report

BROHM MINING CORP.
MR. JIM BARRON
P.O. BOX 485
DEADWOOD, SD
57732

+ + + + +

Bondar-Clegg, Inc.
12980 West Cedar Dr.
Lakewood, Colorado 80228
(303) 989-1404

BONDAR-CLEGG

Geochemical Lab Report

REPORT: 098-0637 (COMPLETE)

REFERENCE INFO: NONE LISTED

CLIENT: BROHM MINING CORP.
PROJECT: GILT EDGE

SUBMITTED BY: J. BARRON
DATE PRINTED: 23-AUG-88

ORDER	ELEMENT		NUMBER OF ANALYSES	LOWER DETECTION LIMIT	EXTRACTION	METHOD
1	Au	Gold	60	0.002 OPT		Fire Assay

SAMPLE TYPES	NUMBER	SIZE FRACTIONS	NUMBER	SAMPLE PREPARATIONS	NUMBER
D DRILL CORE	60	2 -150	60	Assay Prep	60
				Sample Pickup	1

REMARKS: FINAL RESULTS ARE REPORTED. SOME RESULTS HAVE CHANGED SLIGHTLY FROM PRELIMINARY RESULTS.

REPORT COPIES TO: MR. JIM BARRON
MR. JIM BARRON

INVOICE TO: MR. JIM BARRON

Bondar-Clegg, Inc.
12980 West Cedar Dr.
Lakewood, Colorado 80228
(303) 989-1404

BONDAR-CLEGG

Geochemical Lab Report

REPORT: 098-0637

PROJECT: GILT EDGE

SAMPLE NUMBER	ELEMENT UNITS	Au OPT	SAMPLE NUMBER	ELEMENT UNITS	Au OPT
D2 R88-401-0-5		0.006	D2 R88-401-200-205		0.008
D2 R88-401-5-10		0.005	D2 R88-401-205-210		0.015
D2 R88-401-10-15		0.005	D2 R88-401-210-215		0.008
D2 R88-401-15-20		0.009	D2 R88-401-215-220		0.009
D2 R88-401-20-25		0.006	D2 R88-401-220-225		0.009
D2 R88-401-25-30		0.004	D2 R88-401-225-230		0.007
D2 R88-401-30-35		0.007	D2 R88-401-230-235		0.003
D2 R88-401-35-40		0.003	D2 R88-401-235-240		<0.002
D2 R88-401-40-45		0.005	D2 R88-401-240-245		<0.002
D2 R88-401-45-50		0.006	D2 R88-401-245-250		0.032
D2 R88-401-50-55		0.004	D2 R88-401-250-255		0.002
D2 R88-401-55-60		0.002	D2 R88-401-255-260		0.003
D2 R88-401-60-65		0.006	D2 R88-401-260-265		<0.002
D2 R88-401-65-70		0.047	D2 R88-401-265-270		<0.002
D2 R88-401-70-75		0.008	D2 R88-401-270-275		<0.002
D2 R88-401-75-80		0.006	D2 R88-401-275-280		<0.002
D2 R88-401-80-85		0.005	D2 R88-401-280-285		<0.002
D2 R88-401-85-90		0.004	D2 R88-401-285-290		0.006
D2 R88-401-90-95		0.008	D2 R88-401-290-295		<0.002
D2 R88-401-95-100		0.007	D2 R88-401-295-300		0.004
D2 R88-401-100-105		0.005			
D2 R88-401-105-110		0.007			
D2 R88-401-110-115		0.003			
D2 R88-401-115-120		0.020			
D2 R88-401-120-125		0.018			
D2 R88-401-125-130		0.009			
D2 R88-401-130-135		0.106			
D2 R88-401-135-140		0.021			
D2 R88-401-140-145		0.029			
D2 R88-401-145-150		0.055			
D2 R88-401-150-155		0.011			
D2 R88-401-155-160		0.005			
D2 R88-401-160-165		0.006			
D2 R88-401-165-170		0.011			
D2 R88-401-170-175		0.009			
D2 R88-401-175-180		0.004			
D2 R88-401-180-185		0.008			
D2 R88-401-185-190		0.006			
D2 R88-401-190-195		0.005			
D2 R88-401-195-200		0.007			

Bondar-Clegg, Inc.
12980 West Cedar Dr.
Lakewood, Colorado
U.S.A. 80228
Phone: (303) 989-1404
Telex: 45-693

BONDAR-CLEGG

Invoice : 12596, Page 1

BROHM MINING CORP.
MR. JIM BARRON
P.O. BOX 485
DEADWOOD, SD
57732

Date : 31-AUG-88

Report No: 098-0637
Project : GILT EDGE
Reference: NONE LISTED

60 Analyses of Gold	at $ 6.50	$ 390.00	
Subtotal		$ 390.00	$ 390.00
Sample Preparation			
60 Samples of Assay Prep	at $ 3.00	$ 180.00	
1 Sample of Sample Pickup	at $12.00	$ 12.00	
Subtotal		$ 192.00	$ 192.00
Miscellaneous Charges			
4% S.D. STATE SALES TAX		$ 5.28	
2% DEADWOOD CITY SALES TAX		$ 2.64	
Subtotal		$ 7.92	$ 7.92
Invoice Total:			$ 589.92 U.S.

BBE-401
(C-300)

THIS IS A PROFESSIONAL SERVICE
ACCOUNTS DUE WHEN RENDERED

Bondar-Clegg, Inc.
12980 West Cedar Dr.
Lakewood, Colorado 80228
(303) 989-1404

BONDAR-CLEGG

Geochemical Lab Report

REPORT: 098-0638 (COMPLETE)

REFERENCE INFO: NONE LISTED

CLIENT: BROHM MINING CORP.
PROJECT: GILT EDGE

SUBMITTED BY: J. BARRON
DATE PRINTED: 16-AUG-88

ORDER	ELEMENT		NUMBER OF ANALYSES	LOWER DETECTION LIMIT	EXTRACTION	METHOD
1	Au	Gold	9	0.002 OPT		Fire Assay

SAMPLE TYPES	NUMBER	SIZE FRACTIONS	NUMBER	SAMPLE PREPARATIONS	NUMBER
D DRILL CORE	9	2 -150	9	Assay Prep	9
				Sample Pickup	1

REMARKS: FINAL RESULTS ARE REPORTED.

REPORT COPIES TO: MR. JIM BARRON
MR. JIM BARRON

INVOICE TO: MR. JIM BARRON

Bondar-Clegg, Inc.
12980 West Cedar Dr.
Lakewood, Colorado 80228
(303) 989-1404

BONDAR-CLEGG

Geochemical Lab Report

REPORT: 098-0638

PROJECT: GILT EDGE

SAMPLE NUMBER	ELEMENT UNITS	Au OPT
D2 R88-401-300-305		0.004
D2 R88-401-305-310		0.005
D2 R88-401-310-315		0.003
D2 R88-401-315-320		0.017
D2 R88-401-320-325		<0.002
D2 R88-401-325-330		0.004
D2 R88-401-330-335		<0.002
D2 R88-401-335-340		<0.002
D2 R88-401-340-345		<0.002

Bondar-Clegg, Inc.
12980 West Cedar Dr.
Lakewood, Colorado
U.S.A. 80228
Phone: (303) 989-1404
Telex: 45-693

BONDAR-CLEGG

Invoice : 12513, Page 1

BROHM MINING CORP.
MR. JIM BARRON
P.O. BOX 485
DEADWOOD, SD
57732

Date : 22-AUG-88

Report No: 098-0638
Project : GILT EDGE
Reference: NONE LISTED

9 Analyses of Gold .	at $ 6.50	$ 58.50	
Subtotal		$ 58.50	$ 58.50
Sample Preparation			
9 Samples of Assay Prep	at $ 3.00	$ 27.00	
1 Sample of Sample Pickup	at $12.00	$ 12.00	
Subtotal		$ 39.00	$ 39.00
Miscellaneous Charges			
4% S.D. STATE SALES TAX		$ 1.20	
2% DEADWOOD CITY SALES TAX		$ 0.60	
Subtotal		$ 1.80	$ 1.80
Invoice Total:			$ 99.30 U.S.

THIS IS A PROFESSIONAL SERVICE
ACCOUNTS DUE WHEN RENDERED

Bondar-Clegg, Inc.
12980 West Cedar Dr.
Lakewood, Colorado 80228
(303) 989-1404

BONDAR-CLEGG

Geochemical Lab Report

BROHM MINING CORP.
MR. JIM BARRON
P.O. BOX 485
DEADWOOD, SD
57732

Bondar-Clegg, Inc.
12980 West Cedar Dr.
Lakewood, Colorado 80228
(303) 989-1404

BONDAR-CLEGG

Geochemical Lab Report

REPORT: 098-0669 (COMPLETE)

REFERENCE INFO: NONE LISTED

CLIENT: BROHM MINING CORP.
PROJECT: GILT EDGE

SUBMITTED BY: J. BARRON
DATE PRINTED: 24-AUG-88

ORDER	ELEMENT		NUMBER OF ANALYSES	LOWER DETECTION LIMIT	EXTRACTION	METHOD
1	Au	Gold	60	0.002 OPT		Fire Assay

SAMPLE TYPES	NUMBER	SIZE FRACTIONS	NUMBER	SAMPLE PREPARATIONS	NUMBER
D DRILL CORE	60	2 -150	60	Assay Prep	60
				Excessive Wetness	648
				Sample Pickup	1

REMARKS: SAMPLE 401-355-360, SAMPLE BAG WAS RECEIVED WITH NO SAMPLE IN IT.

FINAL RESULTS ARE NOW REPORTED. SOME RESULTS HAVE CHANGED FROM PRELIMINARY REPORT.

REPORT COPIES TO: MR. JIM BARRON
MR. JIM BARRON

INVOICE TO: MR. JIM BARRON

Bondar-Clegg, Inc.
12980 West Cedar Dr.
Lakewood, Colorado 80228
(303) 989-1404

BONDAR-CLEGG

Geochemical Lab Report

REPORT: 098-0669

PROJECT: GILT EDGE

SAMPLE NUMBER	ELEMENT UNITS	Au OPT
D2 R88-401-345-350		<0.002
D2 R88-401-350-355		<0.002
D2 R88-401-360-365		<0.002
D2 R88-401-365-370		<0.002
D2 R88-401-370-375		0.004
D2 R88-401-375-380		<0.002
D2 R88-401-380-385		<0.002
D2 R88-401-385-390		0.006
D2 R88-401-390-395		<0.002
D2 R88-401-395-400		<0.002
D2 R88-401-400-405		0.003
D2 R88-401-405-410		0.008
D2 R88-401-410-415		<0.002
D2 R88-401-415-420		0.006
D2 R88-401-420-425		0.006
D2 R88-401-425-430		0.004
D2 R88-401-430-435		0.006
D2 R88-401-435-440		0.007
D2 R88-401-440-445		<0.002
D2 R88-401-445-450		0.004
D2 R88-401-450-455		0.004
D2 R88-401-455-460		0.005
D2 R88-401-460-465		0.007
D2 R88-401-465-470		<0.002
D2 R88-401-470-475		0.002
D2 R88-401-475-480		<0.002
D2 R88-401-480-485		0.017
D2 R88-401-485-490		0.004
D2 R88-401-490-495		<0.002
D2 R88-401-495-500		<0.002
D2 R88-401-500-505		<0.002
D2 R88-401-505-510		<0.002
D2 R88-401-510-515		<0.002
D2 R88-401-515-520		<0.002
D2 R88-401-520-525		<0.002
D2 R88-401-525-530		<0.002
D2 R88-401-530-535		<0.002
D2 R88-401-535-540		<0.002
D2 R88-401-540-545		<0.002
D2 R88-401-545-550		<0.002
D2 R88-401-550-555		<0.002
D2 R88-401-555-560		<0.002
D2 R88-401-560-565		<0.002
D2 R88-401-565-570		<0.002
D2 R88-401-570-575		<0.002
D2 R88-401-575-580		<0.002
D2 R88-401-580-585		<0.002
D2 R88-401-585-590		<0.002
D2 R88-401-590-595		<0.002
D2 R88-401-595-600		0.004
D2 R88-401-600-605		<0.002
D2 R88-401-605-610		<0.002
D2 R88-401-610-615		0.002
D2 R88-401-615-620		<0.002
D2 R88-401-620-625		0.003
D2 R88-401-625-630		<0.002
D2 R88-401-630-635		0.004
D2 R88-401-635-640		0.003
D2 R88-401-640-645		<0.002
D2 R88-401-645-650		0.004

RECEIVED
SEP - 8 1988
BROHM MINING CO.

Bondar-Clegg, Inc.
12980 West Cedar Dr.
Lakewood, Colorado
U.S.A. 80228
Phone: (303) 989-1404
Telex: 45-693

BONDAR-CLEGG

Invoice : 12603, Page 1

BROHM MINING CORP.
MR. JIM BARRON
P.O. BOX 485
DEADWOOD, SD
57732

Date : 31-AUG-88

Report No: 098-0669
Project : GILT EDGE
Reference: NONE LISTED

60 Analyses of Gold	at $ 6.50	$ 390.00	
Subtotal		$ 390.00	$ 390.00
Sample Preparation			
60 Samples of Assay Prep	at $ 3.00	$ 180.00	
648 Samples of Excessive Wetness	at $ 0.15	$ 97.20	
1 Sample of Sample Pickup	at $12.00	$ 12.00	
Subtotal		$ 289.20	$ 289.20
Miscellaneous Charges			
4% S.D. STATE SALES TAX		$ 0.48	
2% DEADWOOD CITY SALES TAX		$ 0.24	
Subtotal		$ 0.72	$ 0.72
Invoice Total:			$ 679.92 U.S.

BBE-401
(345-450)

THIS IS A PROFESSIONAL SERVICE
ACCOUNTS DUE WHEN RENDERED

Bondar-Clegg, Inc.
12980 West Cedar Dr.
Lakewood, Colorado 80228
(303) 989-1404

BONDAR-CLEGG

Geochemical Lab Report

REPORT: 098-0683 (COMPLETE)

REFERENCE INFO: NONE LISTED

CLIENT: BROHM MINING CORP.
PROJECT: GILT EDGE

SUBMITTED BY: J. BARRON
DATE PRINTED: 18-AUG-88

ORDER		ELEMENT	NUMBER OF ANALYSES	LOWER DETECTION LIMIT	EXTRACTION	METHOD
1	Au	Gold	33	0.002 OPT		Fire Assay

SAMPLE TYPES	NUMBER	SIZE FRACTIONS	NUMBER	SAMPLE PREPARATIONS	NUMBER
D DRILL CORE	33	2 -150	33	Assay Prep	33
				Excessive Wetness	501
				Sample Pickup	1

REMARKS: FINAL RESULTS ARE REPORTED.

REPORT COPIES TO: MR. JIM BARRON
MR. JIM BARRON

INVOICE TO: MR. JIM BARRON

Bondar-Clegg, Inc.
12980 West Cedar Dr.
Lakewood, Colorado 80228
(303) 989-1404

BONDAR-CLEGG

Geochemical Lab Report

REPORT: 098-0683

PROJECT: GILT EDGE

SAMPLE NUMBER	ELEMENT UNITS	Au OPT
D2 R88-401-650-655		<0.002
D2 R88-401-655-660		<0.002
D2 R88-401-660-665		0.002
D2 R88-401-665-670		<0.002
D2 R88-401-670-675		<0.002
D2 R88-401-675-680		0.002
D2 R88-401-680-685		0.005
D2 R88-401-685-690		<0.002
D2 R88-401-690-695		<0.002
D2 R88-401-695-700		0.005
D2 R88-401-700-705		<0.002
D2 R88-401-705-710		<0.002
D2 R88-401-710-715		0.003
D2 R88-401-715-720		<0.002
D2 R88-401-720-725		0.002
D2 R88-401-725-730		<0.002
D2 R88-401-730-735		<0.002
D2 R88-401-735-740		<0.002
D2 R88-401-740-745		<0.002
D2 R88-401-745-750		<0.002
D2 R88-401-750-755		<0.002
D2 R88-401-755-760		0.002
D2 R88-401-760-765		0.005
D2 R88-401-765-770		0.004
D2 R88-401-770-775		0.003
D2 R88-401-775-780		0.014
D2 R88-401-780-785		0.003
D2 R88-401-785-790		<0.002
D2 R88-401-790-795		<0.002
D2 R88-401-795-800		<0.002
D2 R88-401-800-805		<0.002
D2 R88-401-805-810		<0.002
D2 R88-401-810-815		0.002

Bondar-Clegg, Inc.
12980 West Cedar Dr.
Lakewood, Colorado
U.S.A. 80228
Phone: (303) 989-1404
Telex: 45-693

BONDAR-CLEGG

Invoice : 12528, Page 1

BROHM MINING CORP.
MR. JIM BARRON
P.O. BOX 485
DEADWOOD, SD
57732

Date : 22-AUG-88

Report No: 098-0683
Project : GILT EDGE
Reference: NONE LISTED

33 Analyses of Gold	at $ 6.50	$ 214.50	
Subtotal		$ 214.50	$ 214.50
Sample Preparation			
33 Samples of Assay Prep	at $ 3.00	$ 99.00	
501 Samples of Excessive Wetness	at $ 0.15	$ 75.15	
1 Sample of Sample Pickup	at $12.00	$ 12.00	
Subtotal		$ 186.15	$ 186.15
Miscellaneous Charges			
4% S.D. STATE SALES TAX		$ 0.48	
2% DEADWOOD CITY SALES TAX		$ 0.24	
Subtotal		$ 0.72	$ 0.72
Invoice Total:			$ 401.37 U.S.

THIS IS A PROFESSIONAL SERVICE
ACCOUNTS DUE WHEN RENDERED

Bondar-Clegg, Inc.
12980 West Cedar Dr.
Lakewood, Colorado 80228
(303) 989-1404

BONDAR-CLEGG

Geochemical Lab Report

BROHM MINING CORP.
MR. JIM BARRON
P.O. BOX 485
DEADWOOD, SD
57732

Bondar-Clegg, Inc.
12980 West Cedar Dr.
Lakewood, Colorado 80228
(303) 989-1404

BONDAR-CLEGG

Geochemical Lab Report

REPORT: 098-0684 (COMPLETE)

REFERENCE INFO: NONE LISTED

CLIENT: BROHM MINING CORP.
PROJECT: GILT EDGE

SUBMITTED BY: J. BARRON
DATE PRINTED: 23-AUG-88

ORDER	ELEMENT		NUMBER OF ANALYSES	LOWER DETECTION LIMIT	EXTRACTION	METHOD
1	Au	Gold	45	0.002 OPT		Fire Assay

SAMPLE TYPES	NUMBER	SIZE FRACTIONS	NUMBER	SAMPLE PREPARATIONS	NUMBER
D DRILL CORE	45	2 -150	45	Assay Prep	45
				Excessive Wetness	924
				Sample Pickup	1

REMARKS: FINAL RESULTS ARE REPORTED. RESULT HAS CHANGED SLIGHTLY FOR SAMPLE 401-855-860.

REPORT COPIES TO: MR. JIM BARRON
MR. JIM BARRON

INVOICE TO: MR. JIM BARRON

Bondar-Clegg, Inc.
12980 West Cedar Dr.
Lakewood, Colorado 80228
(303) 989-1404

BONDAR-CLEGG

Geochemical Lab Report

REPORT: 098-0684

PROJECT: GILT EDGE

SAMPLE NUMBER	ELEMENT UNITS	Au OPT
D2 R88-401-815-820		<0.002
D2 R88-401-820-825		0.003
D2 R88-401-825-830		<0.002
D2 R88-401-830-835		<0.002
D2 R88-401-835-840		<0.002
D2 R88-401-840-845		<0.002
D2 R88-401-845-850		0.004
D2 R88-401-850-855		<0.002
D2 R88-401-855-860		0.032
D2 R88-401-860-865		0.005
D2 R88-401-865-870		<0.002
D2 R88-401-870-875		<0.002
D2 R88-401-875-880		0.002
D2 R88-401-880-885		<0.002
D2 R88-401-885-890		0.002
D2 R88-401-890-895		0.004
D2 R88-401-895-900		0.009
D2 R88-401-900-905		0.002
D2 R88-401-905-910		<0.002
D2 R88-401-910-915		0.002
D2 R88-401-915-920		<0.002
D2 R88-401-920-925		<0.002
D2 R88-401-925-930		<0.002
D2 R88-401-930-935		<0.002
D2 R88-401-935-940		<0.002
D2 R88-401-940-945		<0.002
D2 R88-401-945-950		<0.002
D2 R88-401-950-955		<0.002
D2 R88-401-955-960		0.002
D2 R88-401-960-965		0.003
D2 R88-401-965-970		0.008
D2 R88-401-970-975		<0.002
D2 R88-401-975-980		<0.002
D2 R88-401-980-985		0.008
D2 R88-401-985-990		<0.002
D2 R88-401-990-995		0.003
D2 R88-401-995-1000		<0.002
D2 R88-401-1000-1005		<0.002
D2 R88-401-1005-1010		<0.002
D2 R88-401-1010-1015		<0.002
D2 R88-401-1015-1020		<0.002
D2 R88-401-1020-1025		<0.002
D2 R88-401-1025-1030		<0.002
D2 R88-401-1030-1035		<0.002
D2 R88-401-1035-1040		0.002

BROHAN MINING CO.

RECEIVED
SEP - 8 1988
BROHM MINING CO.

Bondar-Clegg, Inc.
12980 West Cedar Dr.
Lakewood, Colorado
U.S.A. 80228
Phone: (303) 989-1404
Telex: 45-693

BONDAR-CLEGG

Invoice : 12599, Page 1

BROHM MINING CORP.
MR. JIM BARRON
P.O. BOX 485
DEADWOOD, SD
57732

Date : 31-AUG-88

Report No: 098-0684
Project : GILT EDGE
Reference: NONE LISTED

45 Analyses of Gold	at $ 6.50	$ 292.50	
Subtotal		$ 292.50	$ 292.50
Sample Preparation			
45 Samples of Assay Prep	at $ 3.00	$ 135.00	
924 Samples of Excessive Wetness	at $ 0.15	$ 138.60	
1 Sample of Sample Pickup	at $12.00	$ 12.00	
Subtotal		$ 285.60	$ 285.60
Miscellaneous Charges			
4% S.D. STATE SALES TAX		$ 0.48	
2% DEADWOOD CITY SALES TAX		$ 0.24	
Subtotal		$ 0.72	$ 0.72
Invoice Total:			$ 578.82 U.S.

KEF-401
(815-1090)

THIS IS A PROFESSIONAL SERVICE
ACCOUNTS DUE WHEN RENDERED

```
"TITLE 23-08-88 14:34:20 098-0637   J. BARRON              29/07/88"
"CLIENT BROHM MINING CORP.                                  "
"PROJECT GILT EDGE        #SAMPLES:   60 REFERENCE: NONE LISTED                    "
"SPECIAL VALUES"
"  IS Insufficient Sample"
"  -9 No Value Recorded"
" Values above the upper limit are shown as  +uplimt"
" Values below the lower limit are shown as  -lolmt   (ie not detected)"
"DETERMINATIONS"
"     ELNAME METHO ECO UNI #SAM LOLMT UPLIMT COMMENTS"
"  01 Au     FA        OPT   60 0.002 99.999 Results Reported     "
"SAMPLE PREPS"
"  40 SAMPLE TYPE=D      DRILL CORE          "
"  41 P17=  60           Assay Prep          "
"  42 P23=   1           Sample Pickup       "
"REMARKS"
"  50 FINAL RESULTS ARE REPORTED.  SOME RESULTS HAVE "
"  51 CHANGED SLIGHTLY FROM PRELIMINARY RESULTS.     "
"*****"
"FORMAT (A8,1X,A1,A1,1X,A20,1(1X,A7,A1))"
"BEGIN " "Type" "Frac" "Sample ID"          "    Au"
"06370001" "D" "2" "R88-401-0-5          "    0.006
"06370002" "D" "2" "R88-401-5-10         "    0.005
"06370003" "D" "2" "R88-401-10-15        "    0.005
"06370004" "D" "2" "R88-401-15-20        "    0.009
"06370005" "D" "2" "R88-401-20-25        "    0.006
"06370006" "D" "2" "R88-401-25-30        "    0.004
"06370007" "D" "2" "R88-401-30-35        "    0.007
"06370008" "D" "2" "R88-401-35-40        "    0.003
"06370011" "D" "2" "R88-401-40-45        "    0.005
"06370012" "D" "2" "R88-401-45-50        "    0.006
"06370013" "D" "2" "R88-401-50-55        "    0.004
"06370014" "D" "2" "R88-401-55-60        "    0.002
"06370015" "D" "2" "R88-401-60-65        "    0.006
"06370016" "D" "2" "R88-401-65-70        "    0.047
"06370017" "D" "2" "R88-401-70-75        "    0.008
"06370018" "D" "2" "R88-401-75-80        "    0.006
"06370019" "D" "2" "R88-401-80-85        "    0.005
"06370020" "D" "2" "R88-401-85-90        "    0.004
"06370021" "D" "2" "R88-401-90-95        "    0.008
"06370022" "D" "2" "R88-401-95-100       "    0.007
"06370023" "D" "2" "R88-401-100-105      "    0.005
"06370024" "D" "2" "R88-401-105-110      "    0.007
"06370025" "D" "2" "R88-401-110-115      "    0.003
"06370026" "D" "2" "R88-401-115-120      "    0.020
"06370027" "D" "2" "R88-401-120-125      "    0.018
"06370028" "D" "2" "R88-401-125-130      "    0.009
"06370029" "D" "2" "R88-401-130-135      "    0.106
"06370030" "D" "2" "R88-401-135-140      "    0.021
"06370031" "D" "2" "R88-401-140-145      "    0.029
"06370032" "D" "2" "R88-401-145-150      "    0.055
"06370033" "D" "2" "R88-401-150-155      "    0.011
"06370036" "D" "2" "R88-401-155-160      "    0.005
"06370037" "D" "2" "R88-401-160-165      "    0.006
"06370038" "D" "2" "R88-401-165-170      "    0.011
"06370039" "D" "2" "R88-401-170-175      "    0.009
"06370040" "D" "2" "R88-401-175-180      "    0.004
"06370041" "D" "2" "R88-401-180-185      "    0.008
"06370042" "D" "2" "R88-401-185-190      "    0.006
"06370043" "D" "2" "R88-401-190-195      "    0.005
"06370044" "D" "2" "R88-401-195-200      "    0.007
"06370045" "D" "2" "R88-401-200-205      "    0.008
"06370046" "D" "2" "R88-401-205-210      "    0.015
"06370047" "D" "2" "R88-401-210-215      "    0.008
```

115-150

35' @ .037

"06370048"	"D"	"2"	"R88-401-215-220 "	0.009
"06370049"	"D"	"2"	"R88-401-220-225 "	0.009
"06370050"	"D"	"2"	"R88-401-225-230 "	0.007
"06370051"	"D"	"2"	"R88-401-230-235 "	0.003
"06370052"	"D"	"2"	"R88-401-235-240 "	-0.002
"06370053"	"D"	"2"	"R88-401-240-245 "	-0.002
"06370054"	"D"	"2"	"R88-401-245-250 "	0.032
"06370055"	"D"	"2"	"R88-401-250-255 "	0.002
"06370056"	"D"	"2"	"R88-401-255-260 "	0.003
"06370057"	"D"	"2"	"R88-401-260-265 "	-0.002
"06370058"	"D"	"2"	"R88-401-265-270 "	-0.002
"06370061"	"D"	"2"	"R88-401-270-275 "	-0.002
"06370062"	"D"	"2"	"R88-401-275-280 "	-0.002
"06370063"	"D"	"2"	"R88-401-280-285 "	-0.002
"06370064"	"D"	"2"	"R88-401-285-290 "	0.006
"06370065"	"D"	"2"	"R88-401-290-295 "	-0.002
"06370066"	"D"	"2"	"R88-401-295-300 "	0.004

"END"

BONDAR-CLEGG

Geochemical Lab Report

REPORT: 098-0638

PROJECT: GILT EDGE PAGE 1

SAMPLE NUMBER	ELEMENT UNITS	Au OPT
D2 R88-401-300-305		0.004
D2 R88-401-305-310		0.005
D2 R88-401-310-315		0.003
D2 R88-401-315-320		0.017
D2 R88-401-320-325		<0.002
D2 R88-401-325-330		0.004
D2 R88-401-330-335		<0.002
D2 R88-401-335-340		<0.002
D2 R88-401-340-345		<0.002

```
"TITLE 24-08-88 15:37:49 098-0669   J. BARRON            27/07/88"
"CLIENT BROHM MINING CORP.                                  "
"PROJECT GILT EDGE       #SAMPLES:   60 REFERENCE: NONE LISTED                    "
"SPECIAL VALUES"
"  IS Insufficient Sample"
"  -9 No Value Recorded"
" Values above the upper limit are shown as  +uplimt"
" Values below the lower limit are shown as  -lolmt   (ie not detected)"
"DETERMINATIONS"
"     ELNAME METHO ECO UNI #SAM LOLMT UPLIMT COMMENTS"
"  01 Au     FA        OPT   60 0.002 99.999 Results Reported     "
"SAMPLE PREPS"
"  40 SAMPLE TYPE=D      DRILL CORE          "
"  41 P17=  60           Assay Prep          "
"  42 P64= 648           Excessive Wetness   "
"  43 P23=   1           Sample Pickup       "
"REMARKS"
"  50 SAMPLE 401-355-360, SAMPLE BAG WAS RECEIVED    "
"  51 WITH NO SAMPLE IN IT.                          "
"  52 FINAL RESULTS ARE NOW REPORTED.  SOME RESULTS  "
"  53 HAVE CHANGED FROM PRELIMINARY REPORT.          "
"****"
"FORMAT (A8,1X,A1,A1,1X,A20,1(1X,A7,A1))"
"BEGIN " "Type" "Frac" "Sample ID"          "    Au"
"06690001" "D" "2" "R88-401-345-350     "   -0.002
"06690002" "D" "2" "R88-401-350-355     "   -0.002
"06690003" "D" "2" "R88-401-360-365     "   -0.002
"06690004" "D" "2" "R88-401-365-370     "   -0.002
"06690005" "D" "2" "R88-401-370-375     "    0.004
"06690006" "D" "2" "R88-401-375-380     "   -0.002
"06690007" "D" "2" "R88-401-380-385     "   -0.002
"06690008" "D" "2" "R88-401-385-390     "    0.006
"06690009" "D" "2" "R88-401-390-395     "   -0.002
"06690010" "D" "2" "R88-401-395-400     "   -0.002
"06690013" "D" "2" "R88-401-400-405     "    0.003
"06690014" "D" "2" "R88-401-405-410     "    0.008
"06690015" "D" "2" "R88-401-410-415     "   -0.002
"06690016" "D" "2" "R88-401-415-420     "    0.006
"06690017" "D" "2" "R88-401-420-425     "    0.006
"06690018" "D" "2" "R88-401-425-430     "    0.004
"06690019" "D" "2" "R88-401-430-435     "    0.006
"06690020" "D" "2" "R88-401-435-440     "    0.007
"06690021" "D" "2" "R88-401-440-445     "   -0.002
"06690022" "D" "2" "R88-401-445-450     "    0.004
"06690023" "D" "2" "R88-401-450-455     "    0.004
"06690024" "D" "2" "R88-401-455-460     "    0.005
"06690025" "D" "2" "R88-401-460-465     "    0.007
"06690026" "D" "2" "R88-401-465-470     "   -0.002
"06690027" "D" "2" "R88-401-470-475     "    0.002
"06690028" "D" "2" "R88-401-475-480     "   -0.002
"06690029" "D" "2" "R88-401-480-485     "    0.017
"06690030" "D" "2" "R88-401-485-490     "    0.004
"06690031" "D" "2" "R88-401-490-495     "   -0.002
"06690032" "D" "2" "R88-401-495-500     "   -0.002
"06690033" "D" "2" "R88-401-500-505     "   -0.002
"06690034" "D" "2" "R88-401-505-510     "   -0.002
"06690035" "D" "2" "R88-401-510-515     "   -0.002
"06690038" "D" "2" "R88-401-515-520     "   -0.002
"06690039" "D" "2" "R88-401-520-525     "   -0.002
"06690040" "D" "2" "R88-401-525-530     "   -0.002
"06690041" "D" "2" "R88-401-530-535     "   -0.002
"06690042" "D" "2" "R88-401-535-540     "   -0.002
"06690043" "D" "2" "R88-401-540-545     "   -0.002
"06690044" "D" "2" "R88-401-545-550     "   -0.002
```

"06690045"	"D"	"2"	"R88-401-550-555 "	-0.002
"06690046"	"D"	"2"	"R88-401-555-560 "	-0.002
"06690047"	"D"	"2"	"R88-401-560-565 "	-0.002
"06690048"	"D"	"2"	"R88-401-565-570 "	-0.002
"06690049"	"D"	"2"	"R88-401-570-575 "	-0.002
"06690050"	"D"	"2"	"R88-401-575-580 "	-0.002
"06690051"	"D"	"2"	"R88-401-580-585 "	-0.002
"06690052"	"D"	"2"	"R88-401-585-590 "	-0.002
"06690053"	"D"	"2"	"R88-401-590-595 "	-0.002
"06690054"	"D"	"2"	"R88-401-595-600 "	0.004
"06690055"	"D"	"2"	"R88-401-600-605 "	-0.002
"06690056"	"D"	"2"	"R88-401-605-610 "	-0.002
"06690057"	"D"	"2"	"R88-401-610-615 "	0.002
"06690058"	"D"	"2"	"R88-401-615-620 "	-0.002
"06690059"	"D"	"2"	"R88-401-620-625 "	0.003
"06690060"	"D"	"2"	"R88-401-625-630 "	-0.002
"06690063"	"D"	"2"	"R88-401-630-635 "	0.004
"06690064"	"D"	"2"	"R88-401-635-640 "	0.003
"06690065"	"D"	"2"	"R88-401-640-645 "	-0.002
"06690066"	"D"	"2"	"R88-401-645-650 "	0.004

"END"

```
"TITLE 23-08-88 14:41:11 098-0684   J. BARRON            29/07/88"
"CLIENT BROHM MINING CORP.                                  "
"PROJECT GILT EDGE       #SAMPLES:   45 REFERENCE: NONE LISTED                    "
"SPECIAL VALUES"
"  IS Insufficient Sample"
"  -9 No Value Recorded"
" Values above the upper limit are shown as  +uplimt"
" Values below the lower limit are shown as  -lolmt   (ie not detected)"
"DETERMINATIONS"
"     ELNAME METHO ECO UNI #SAM LOLMT UPLIMT COMMENTS"
"  01 Au     FA        OPT   45 0.002 99.999 Results Reported     "
"SAMPLE PREPS"
"  40 SAMPLE TYPE=D      DRILL CORE          "
"  41 P17=  45           Assay Prep          "
"  42 P64= 924           Excessive Wetness   "
"  43 P23=   1           Sample Pickup       "
"REMARKS"
" 50 FINAL RESULTS ARE REPORTED.  RESULT HAS CHANGED"
"  51 SLIGHTLY FOR SAMPLE 401-855-860.                "
"*****"
"FORMAT (A8,1X,A1,A1,1X,A20,1(1X,A7,A1))"
"BEGIN " "Type" "Frac" "Sample ID"         "    Au"
"06840001" "D" "2" "R88-401-815-820     "   -0.002
"06840002" "D" "2" "R88-401-820-825     "    0.003
"06840003" "D" "2" "R88-401-825-830     "   -0.002
"06840004" "D" "2" "R88-401-830-835     "   -0.002
"06840005" "D" "2" "R88-401-835-840     "   -0.002
"06840008" "D" "2" "R88-401-840-845     "   -0.002
"06840009" "D" "2" "R88-401-845-850     "    0.004
"06840010" "D" "2" "R88-401-850-855     "   -0.002
"06840011" "D" "2" "R88-401-855-860     "    0.032
"06840012" "D" "2" "R88-401-860-865     "    0.005
"06840013" "D" "2" "R88-401-865-870     "   -0.002
"06840014" "D" "2" "R88-401-870-875     "   -0.002
"06840015" "D" "2" "R88-401-875-880     "    0.002
"06840016" "D" "2" "R88-401-880-885     "   -0.002
"06840017" "D" "2" "R88-401-885-890     "    0.002
"06840018" "D" "2" "R88-401-890-895     "    0.004
"06840019" "D" "2" "R88-401-895-900     "    0.009
"06840020" "D" "2" "R88-401-900-905     "    0.002
"06840021" "D" "2" "R88-401-905-910     "   -0.002
"06840022" "D" "2" "R88-401-910-915     "    0.002
"06840023" "D" "2" "R88-401-915-920     "   -0.002
"06840024" "D" "2" "R88-401-920-925     "   -0.002
"06840025" "D" "2" "R88-401-925-930     "   -0.002
"06840026" "D" "2" "R88-401-930-935     "   -0.002
"06840027" "D" "2" "R88-401-935-940     "   -0.002
"06840028" "D" "2" "R88-401-940-945     "   -0.002
"06840029" "D" "2" "R88-401-945-950     "   -0.002
"06840030" "D" "2" "R88-401-950-955     "   -0.002
"06840033" "D" "2" "R88-401-955-960     "    0.002
"06840034" "D" "2" "R88-401-960-965     "    0.003
"06840035" "D" "2" "R88-401-965-970     "    0.008
"06840036" "D" "2" "R88-401-970-975     "   -0.002
"06840037" "D" "2" "R88-401-975-980     "   -0.002
"06840038" "D" "2" "R88-401-980-985     "    0.008
"06840039" "D" "2" "R88-401-985-990     "   -0.002
"06840040" "D" "2" "R88-401-990-995     "    0.003
"06840041" "D" "2" "R88-401-995-1000    "   -0.002
"06840042" "D" "2" "R88-401-1000-1005   "   -0.002
"06840043" "D" "2" "R88-401-1005-1010   "   -0.002
"06840044" "D" "2" "R88-401-1010-1015   "   -0.002
"06840045" "D" "2" "R88-401-1015-1020   "   -0.002
"06840046" "D" "2" "R88-401-1020-1025   "   -0.002
```

```
"06840047" "D" "2" "R88-401-1025-1030   "   -0.002
"06840048" "D" "2" "R88-401-1030-1035   "   -0.002
"06840049" "D" "2" "R88-401-1035-1040   "    0.002
"END"
```

R88-401

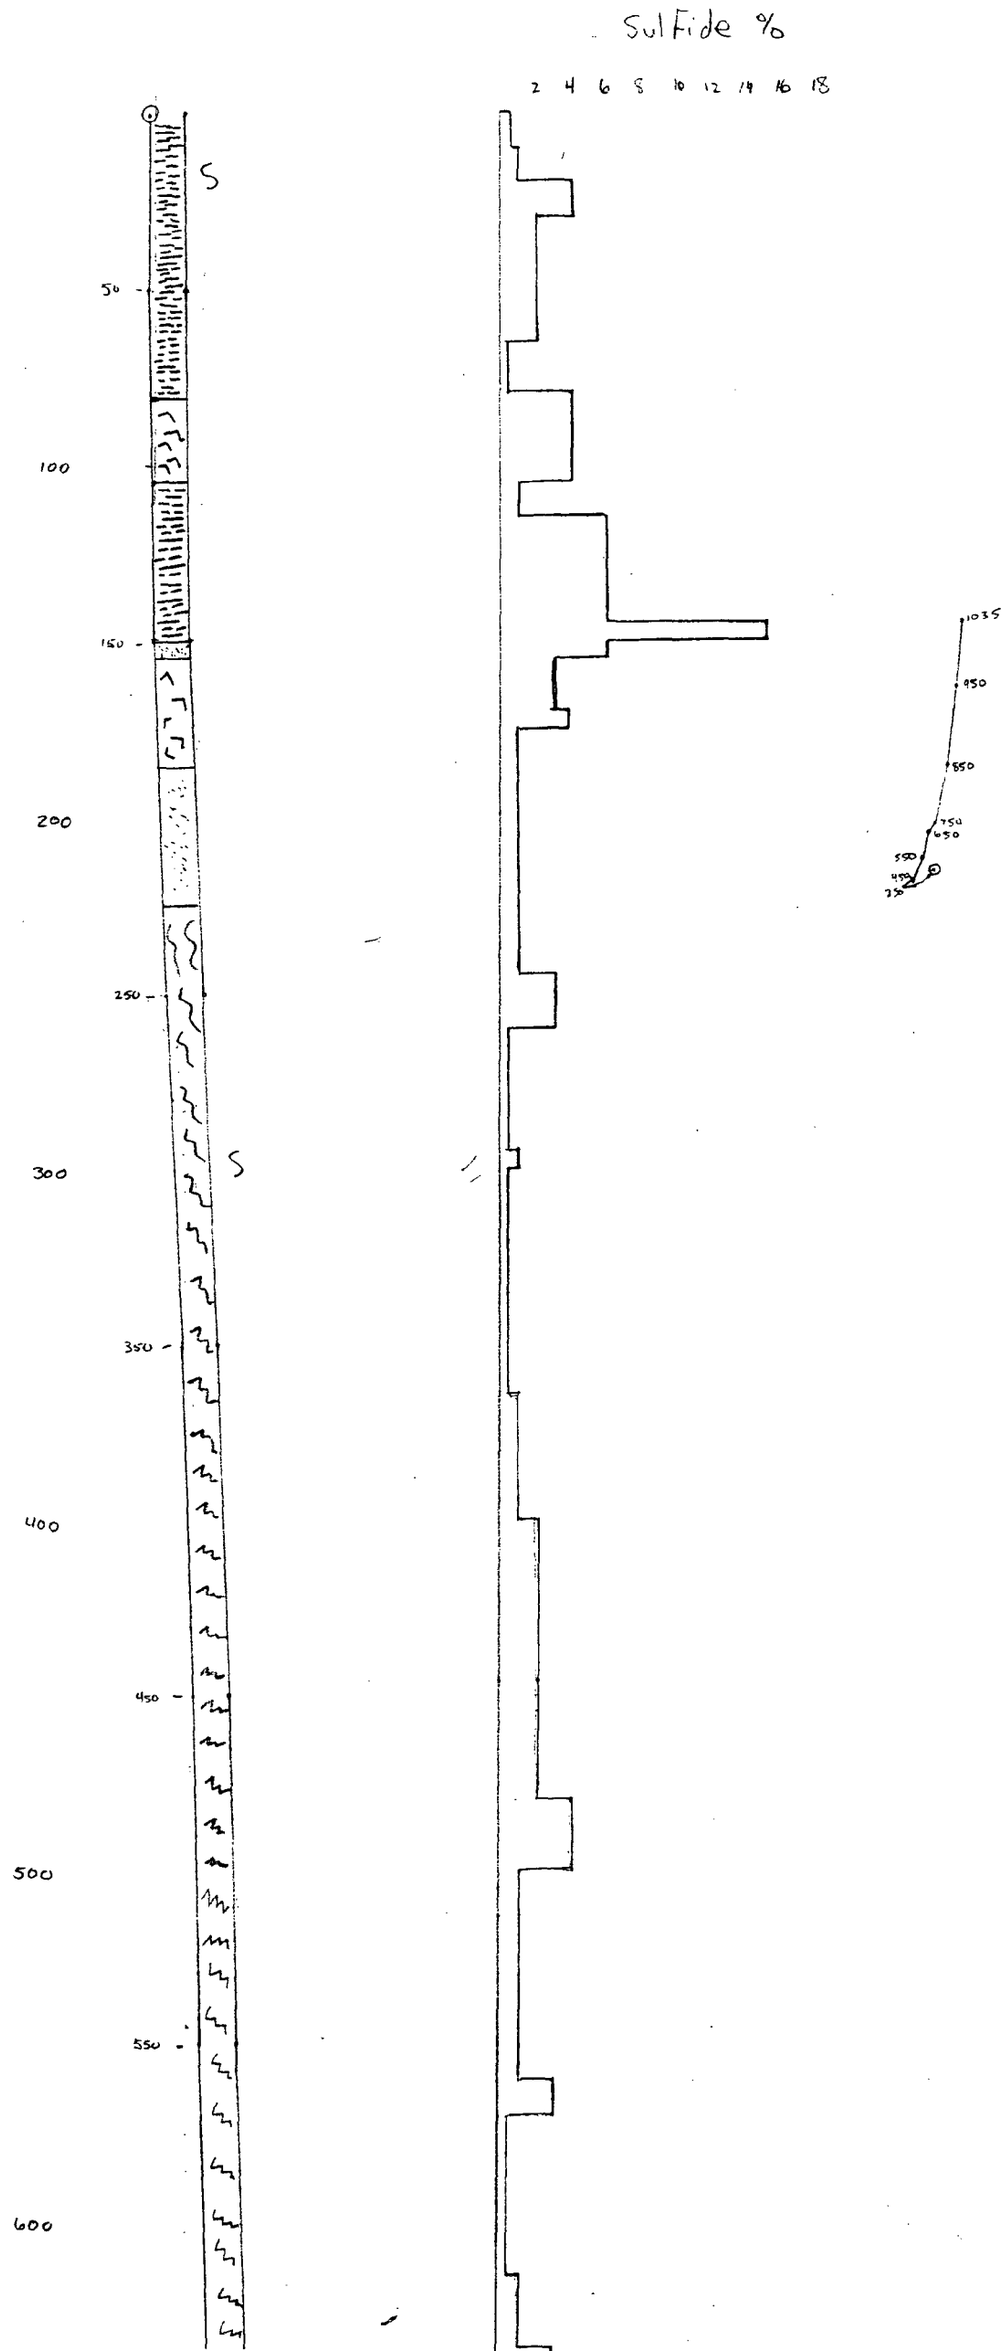
Sulfide %
2 4 6 8 10 12 14 16 18
S
S
50
100
150
200
250
300
350
400
450
500
550
600
1035
950
850
750
650
550
450
250

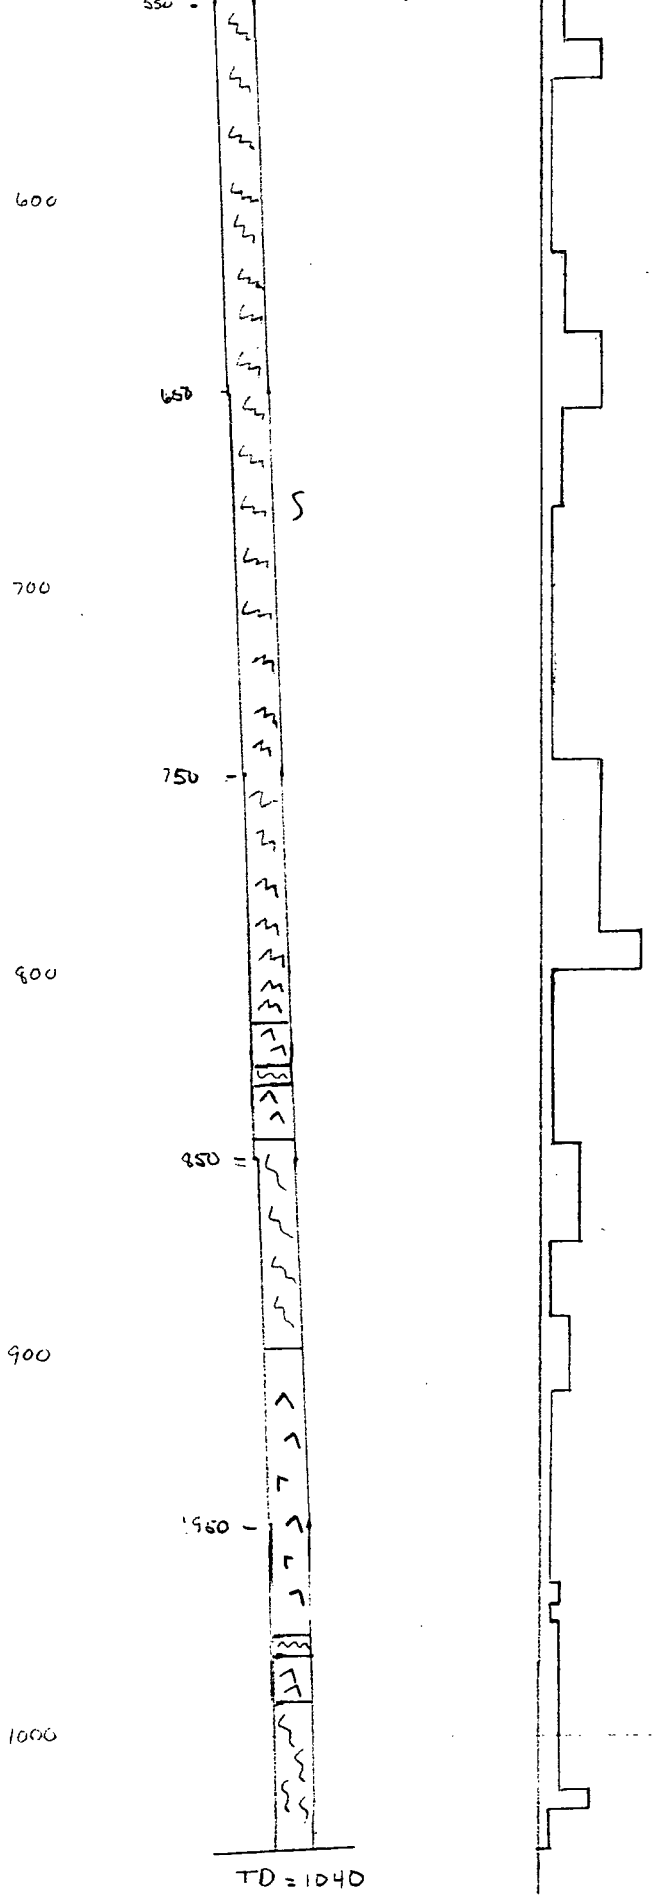
550
600
650
700
750
800
850
900
950
1000
S
TD = 1040
