

**DAMES & MOORE**

A PROFESSIONAL LIMITED PARTNERSHIP

12 COMMERCE DRIVE, CRANFORD, NEW JERSEY 07016-1101 (201) 272-8300

SDMS Document



67923

July 13, 1988

Ms. Janet Feldstein  
US Environmental Protection Agency  
26 Federal Plaza  
New York, New York 10278

Re: Proposed Completion Schedule  
On-Site Feasibility Study  
SCP Site, Carlstadt, New Jersey

Dear Janet:

Attached is a revised schedule for completion of the on-site Feasibility Study (FS) for the SCP Carlstadt site. In his June 24, 1988 letter to Bill Warren, Ray Basso indicated without further discussion that the schedule originally submitted with POP Revision No.8 should be shortened by three weeks. This would allow only 3 1/2 weeks to finish the draft FS Report after completion of the detailed evaluation of alternatives. The attached revised schedule indicates a September 19, 1988 completion date, allowing two more weeks than the agency's suggested completion date.

We believe that this represents the minimum amount of time necessary to provide internal and PRP review of the draft FS Report prior to release to the agency. This is a unique site with complex remediation characteristics, and a thorough PRP review of the draft FS Report will serve two purposes, both of which are important to the PRP group and the agency:

1. The PRP group is comprised of representatives from major corporations who have considerable expertise in site remediations through their experience on other sites. Their thorough review of the draft FS Report will collectively provide valuable quality control of the draft report.
2. The review process will strengthen the PRP group in their understanding of and support for various remedial alternatives.

With this in mind, and in an attempt to accommodate the agency's request for a shorter schedule, we have reduced the original schedule by one week.

Regarding the assumptions listed on the schedule, the agency has requested that those be deleted. These assumptions form the basis for the schedule, and are fundamental to the milestones shown on the

003720



**DAMES & MOORE**

A PROFESSIONAL LIMITED PARTNERSHIP

Ms. Janet Feldstein  
July 13, 1988  
Page - 2 -

schedule. These assumptions cannot be deleted without eliminating the entire basis of the schedule. The schedule makes no real sense without reference to these assumptions.

Please call if you have any questions.

Very truly yours,


DAMES & MOORE

Gerard M. Coscia, P.E.  
Project Manager

GMC/nam  
Attachment

cc: William Warren

003721

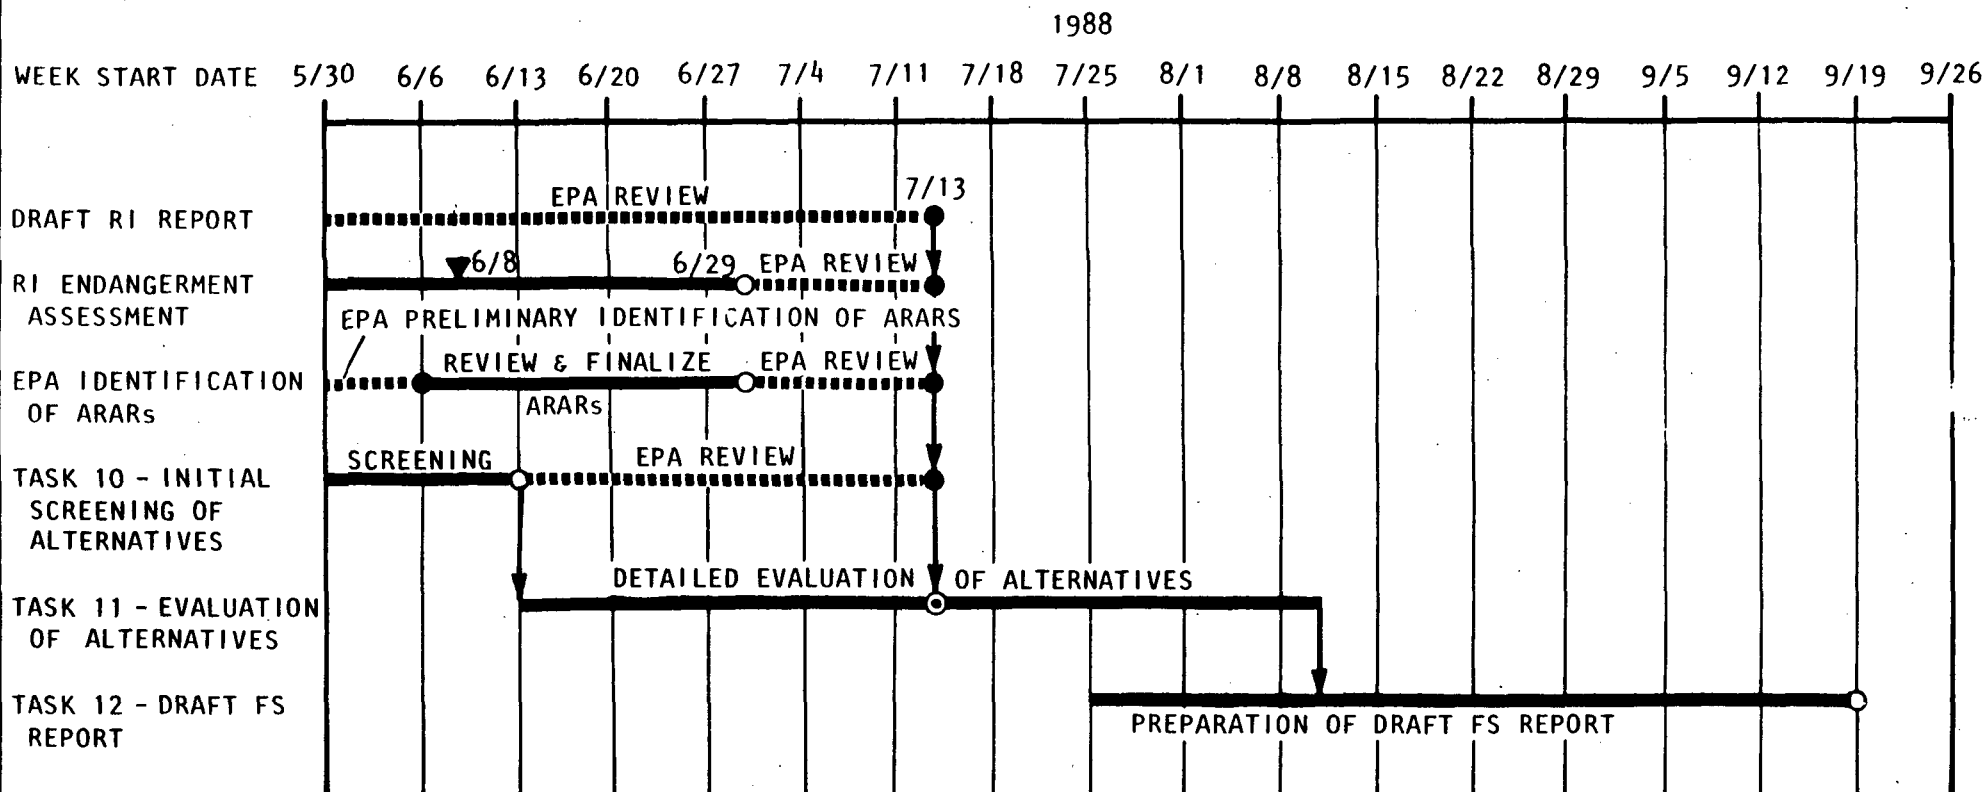

## PROPOSED COMPLETION SCHEDULE ON-SITE (SOURCE CONTROL) FEASIBILITY STUDY

SCP SITE RI/FS  
CARLSTADT, NEW JERSEY

JULY 14, 1988
