

Libby Asbestos Project

*COPY OF
1073989,
margin differs?*

Project Status Briefing

November 13-15, 2007



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

1

Meeting Agenda

**Tuesday November 13, 1:00 pm through
Wednesday November 14, noon**

- 2007 in review (Project organization & accomplishments by WAF)
- Laboratory capacity analysis
- Cost impact of removing visible vermiculite
- ERS position activity and performance



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

2

Meeting Agenda (continued)

Feds-only Session – Wednesday November 13, 1:00 pm – 5:00 pm

- Budget/Spending review
- Contracting status and strategy
 - Status of existing contracts
 - Planned actions for 2008
 - Construction contracting options:
 - Design-build contracting w/A&E firms
 - Other options
 - Staff expansion to cover requirements of non-OU4 work

3



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

Meeting Agenda (continued)

Thursday November 14, 8:00 am – 5:00 pm

- Planning for 2008, setting goals and priorities
- Process improvements planned for 2008
 - Health & Safety auditing
 - Oversight changes
 - GFE tracking and management
 - Program participation risk management

4



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

Planning for 2008

5



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

WAF 1: Database Support

- 2008 Planned and Potential Future Work
 - Ongoing work
 - QualityNet implementation
 - E911
 - New report in the Standard Report application
 - FOCIS Phase II
 - Remediation Status Query/ Property Status Query

6



US Department of Transportation
John A. Volpe National Transportation
Systems Center




US Environmental
Protection Agency
Region 8

CDM

WAF 2: Community Involvement Support

- 2008 Planned and Potential Work
 - Maintain and Staff Info. Center
 - CAG Support
 - Public Meeting Support
 - Communication Support
 - Ask EPA, Superfund and You, CAG & Public Meeting Notices, Q&A's, radio and local press
 - Troy Removals
 - ~~■ Mine Investigation~~
 - 2008 CI Plan to present to EPA



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

7

WAF 2: OU4 (PDI)

Assumed Goals

- Support 2008 Removals – Q2
 - 10 PDIs
- Complete TO9 Contract: Q2-Q3
 - 31 PDIs
- Flower Creek PDI: Q3-Q4

*Assumptions

- Cleanup goal remains 160 properties
- Under current removal/design protocol



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

8

WAF 2: OU4 (Design)

Assumed Goals

- Support 2008 Removals: Q1-Q3
 - 200 Designs
- Cabinet View Country Club: Q1-Q2
 - Removal/restoration designs

Date	Projected Designs (month)	Actual Designs (month)
Sep-07	0	2
Oct-07	20	20
Nov-07	30	
Dec-07	20	
Jan-08	15	
Feb-08	25	
Mar-08	30	
Apr-08	30	
May-08	20	
Jun-08	10	
Total	200*	



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

9

WAF 2: OU4 (Removals)

Assumed Goals

- 160 Removals: Q3 - Q4
 - 9 Troy properties
 - 151 Libby properties
- Continue ERS program
- Revise Response Action Work Plan
Sampling and Analysis Plan (RAWP SAP)
- Revise Landfill Operations Plan and Mine
Operations Plan



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

10

WAF 3: OU1 (Export Plant)

Assumed Goals

- RI – Q2
- Risk Assessment – Q2
- FS – Q2
- RRB – April?? (is it needed with an no action FS)
- Proposed Plan – Q3
- ROD – September

*Assumptions

- ABS data available to support RA
- No RRB
- No action FS

11



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

WAF 3: OU2 (Screening Plant)

Assumed Goals

- Continue Ambient Air sampling: Q1-Q3
- Conceptual site model – Q1
- Finalize data summary report – Q2
- Data gap analysis – Q2
- SAP – Q3
- Sampling – Q3

*Assumptions

- Limited sampling for data gap (bluffs)
- No further sampling at Screening Plant or Flyway
- Ambient Air sampling to end 6/2008
- RI to come in first quarter 2009

12



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

WAF 3: OU4 (Investigations)

Assumed Goals

- Continue Ambient Air sampling: Q1-Q4
 - 7 Location
 - 1 Background
 - 5 Days on, 15 days off
- Continue ABS: Q1-Q3
 - Events 2 and 3: interior only
 - Event 4: interior and exterior
- Finalize site wide QAPP

*Assumptions

- None



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

13

WAF 3: OU4 (Investigations)

Other Potential Goals

■ Exposure pathway evaluation

- Outdoor air near fire location
- Air in attic/crawl space with vermiculite (phase II)
- Indoor air near breached walls
- Outdoor air near highways and rail lines
- Dust in air of vehicles
- Ash from burned wood
- Inhalation from dust in air from disturbances of roofing or other outdoor surface

*Assumptions

- None



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

14

WAF 3: OU4 (Investigations)

Other Potential Goals (cont.)

- Contaminate Screening Study
 - 400 Properties to complete OU4
- Visible Vermiculite Inspection Revisits
 - ~3,200 Properties
- Creeks/Rivers
 - Fisher River
 - Granite, Pipe, Libby, Parmenter, and Calahan, ~~Lake~~, Lake, Iron
- Tox Studies

*Assumptions

- None

15



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

WAF 3: OU4 (Investigations)

Other Potential Goals

- Support 2009 Removals: [Q3 – Q4]
 - 204 PDIs & Field Reviews
- Additional Troy PDIs

*Assumptions

- Cleanup goal remains 160 properties
- Under current removal/design protocol

16



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

WAF 3: OU4 (Design)

Other Potential Goals

- Support 2009 Removals
 - 50 Designs – 2008 - Q4
 - 150 Designs – 2009: Q1-Q3



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

17

WAF 3: OU5 (Stimson)

Assumed Goals

- Complete indoor air sampling – Q1
 - ABS and Aggressive
- Analyze wood chip/waste bark – Q1
- Complete landfarm soil sampling – Q3
- RI – Q4



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

18

WAF 3: OU6 (BNSF)

Assumed Goals

- Continue AA – Q1 – Q3
- CSM – Q1
- Data GAP – Q2
- SAP – Q3
- Sampling – Q3

*Assumptions

- BNSF writes SAP
- BNSF collects samples with CDM oversight



19



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

WAF 3: General Investigative

- Ambient Air Program
- Lab Management & Analytical Method Development & Modification
- Participation in TAU Calls & Development of Tech Memos & Studies
- CSF Support
 - From 2007 - Enter Backlog of Archive Soil from EMSL Libby
 - From 2007 - Process & Enter Wood Chip Samples (~184)
 - 2008 Samples

20



US Department of Transportation
John A. Volpe National Transportation
Systems Center




US Environmental
Protection Agency
Region 8

CDM

1198
- 553

645

WAF 4: Cleanup – 2008 Goals

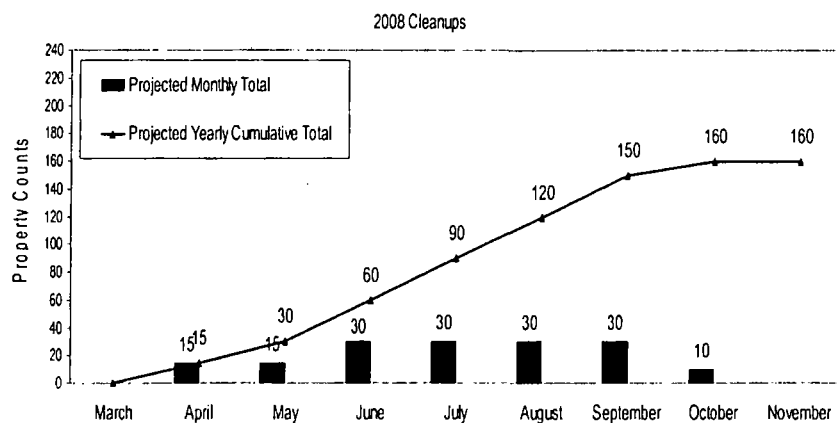

21



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

WAF 7: Troy Support

■ Major Support Activities Included

- Analysis of Dust Samples
- Lab Mentoring (PLM & TEM)
- Additional TBD
 - Evaluation of Troy Properties for Cleanup?

22



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

WAF 8: Toxicology Studies

■ 2008 Accomplishments To-Date

- Initiated ABS Indoor Event 2 (as of Nov 3rd 34 of 80 prop. completed)
- Analysis of ABS Event 1 (to be completed Dec 2007)
- Planning regarding procurement efforts to support toxicology projects
- Sources sought synopsis developed, finalized, & posted (Nov 7, 2007)
- SRC Risk Assessment support

■ Planned for 2008

- Complete ABS Event 2 & 3 (sampling & analysis)
- Complete procurement & preparation of White Paper on Fiber-like Structures
- Support tissue processing and method-development (goal of contract in place by Feb/March 2008)
- Analyze samples from the toxicology projects (Winter 2007-Spring 2008)

23



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

WAF 9: OU3 (Mine)

Assumed Goals

- None

24



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

2008 Summary

Q1	Q2	Q3	Q4
OU1 RI	OU1 FS	OU1 Proposed Plan	OU1 ROD
OU2 CSM	OU1 RA	OU2 SAP	OU2 AA
OU2 DSR	OU2 DSR	OU2 Sampling	OU3 Mine Ops OS
OU2 AA	OU2 Data Gap	OU2 AA	OU3 Quarterly Survey
OU3 Rewrite Mine Ops Plan	OU3 Review SAP	OU3 Sample Oversight	OU4 AA
OU4 ERS Support	OU3 Quarterly Survey	OU3 Mine Ops	OU4 Removal OS
OU4 AA	OU4 PDI	OU3 Quarterly Survey	OU4 PDI for '09
OU4 ABS	OU4 ERS Support	OU4 AA	OU4 CSS
OU4 CVCC Design	OU4 AA	OU4 ABS	OU4 Creek Investigation
OU5 Indoor ABS	OU4 ABS	OU4 Removal OS	OU5 RI
OU5 Analysis of Wood Chip and Waste Bark	OU6 DSR	OU4 PDIs for '08	OU6 AA
OU6 CSM	OU6 Data Gap	OU4 CSS	OU7 Sample Analysis
OU6 AA	OU6 AA	OU4 ERS Support	OU7 PDI at Priority Properties
OU7 Sample Analysis	OU7 ERS Support	OU5 Landfarm Sampling	OU7 Removal OS
OU7 ERS Support		OU6 SAP Review	OU7 ERS Support
		OU6 AA	
		OU6 Sampling OS	
		OU7 PDI at Priority Properties	
		OU7 Removal and OS	
		OU7 ERS Support	

25



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

GFE Tracking and Management

■ Non-IT GFE

Landfill Personal Decontamination Trailer

Sprung Instant Structure (Landfill Tent)

10 Roll-off Vacuum Containers

20 CY roll-off bin w/flip lid

55 Two-way Radios, Chargers, and Repeater

Sub-Soiler Decompactor

Weather Monitor II and Two Mounts

Mine Amphitheater Personal Decontamination Trailer

Mine Amphitheater Water Filtration, Pumping, and Distribution Systems

26



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM

Program Participation and Risk Management

- Drop outs
 - Cleanup program
 - ABS

27



US Department of Transportation
John A. Volpe National Transportation
Systems Center



US Environmental
Protection Agency
Region 8

CDM
