



Outline




- Update on TCRA Progress
 - Tiers 3 & 5
 - Tier 2
 - Tier 1
- What's Next
- Schedule



TCRA Progress – Completed Excavations



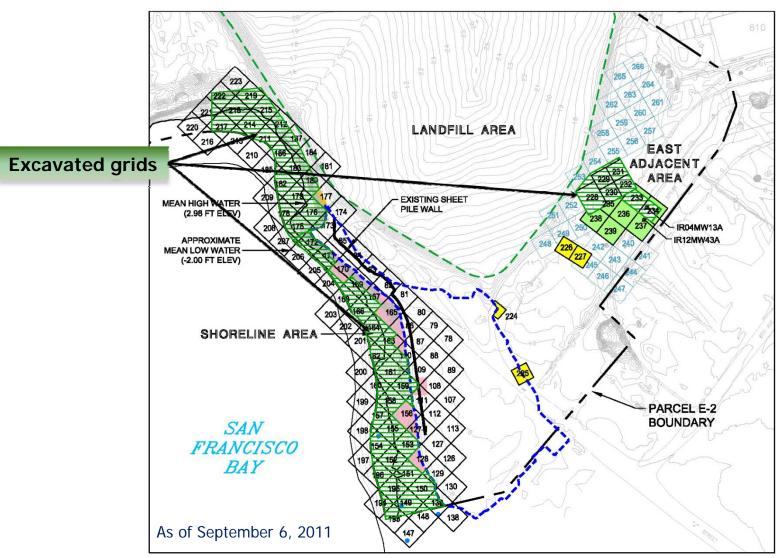



Update Tiers 3 and 5



- Commenced excavation on August 30, 2010
- Tier 3
 - 100% of original Tier 3 grids excavated to depth (3-10 feet bgs) and confirmation sampled
 - Grid 231
 - Sidewall over-excavated on August 18
 - Results received and sidewall still not meeting PALs for TPH and lead
 - Continued over-excavation is planned for September 23
- Tier 5
 - No over-excavation required to date



Update Tiers 3 and 5 (continued)





Parcel E-2 Landfill

Final excavation grade looking north

Tier 3 – September 13, 2011



Update Tier 2



- Commenced excavation on October 19, 2010
 - Stopped excavation December 2010 mid April 2011
- 100% of grids excavated, sampled, and backfilled with clean sand
- Over-excavation was required in six grids
- Over-excavations completed with the exception of Grid 177 sidewall
- Construction access road currently prevents overexcavation of Grid 177 sidewall - will be overexcavated in fall, after geotechnical investigation



Update Tier 2 (continued)





Tier 2 Looking North – September 6, 2011



Update Tier 1



- Commenced excavation on May 11, 2011
- 78% of grids (97.5% volume) excavated, sampled, and backfilled
- Remaining 10 grids (22%): 3 pending confirmation sample results, 4 require over-excavation, 3 remain to be excavated
- Total volume excavated 19,000 cy



Excavating Grid 170 - September 14, 2011



Update Tier 1 (continued)






Tier 1 Shoreline looking South at High Tide – September 13, 2011



Update Tier 1 (continued)



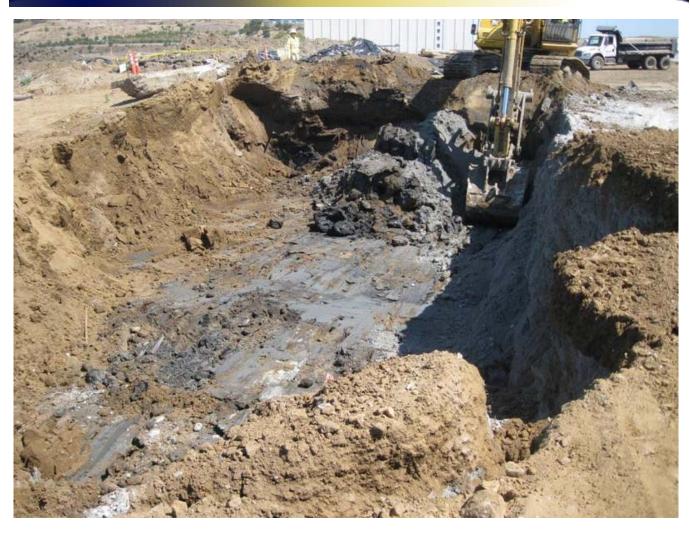

Bottom of Grid 159 at 10 ft bgs – September 1, 2011



Schedule



Activity	Date
Continue Hot Spots Excavation	September – December 2011
Continue Soil Screening and Implementing Acceptance Sampling Procedures	September – February 2011
Continue Backfill and Site Restoration	September 2011 – February 2012
Demobilize	February 2012
Submit Draft Removal Action Completion Report	April 2012
