



Nicholas Clevett  
<Nicholas.Clevett@rmt  
inc.com>

03/25/2005 11:00 AM

To: ACINQUE@dep.state.nj.us, Stephen Cipo/R2/USEPA/US@EPA  
cc: George.Blyskun@dep.state.nj.us, John.Prendergast@dep.state.nj.us,  
Robert Alvey/R2/USEPA/US@EPA, Frances  
Zizila/R2/USEPA/US@EPA, morrissoil@optonline.net,  
cristopher.anderson@Polyone.com, Emie.Schaub@Polyone.com,  
James.Lewis@Polyone.com, Dan Oman <Dan.Oman@rmtinc.com>,  
David Pratt <David.Pratt@rmtinc.com>, Jeff Macri  
<Jeff.Macri@rmtinc.com>, Jim Dexter <Jim.Dexter@rmtinc.com>,  
Nakia Addison <Nakia.Addison@rmtinc.com>, Wally Kurzeja  
<Wally.Kurzeja@rmtinc.com>, jrheinhardt@whartonnj.com  
Subject: LE Carpenter & Company - Source Reduction Construction  
Progress Update No.@ 9 [031805 to 032405]

Find attached Update No. 9 for the LEC source reduction project.  
Please call with questions. Have a good Holiday.  
Regards,

Nicholas J. Clevett  
Senior Project Manager  
RMT, Inc., Michigan  
2025 E. Beltline Ave. SE  
Suite 402  
Grand Rapids, MI 49546  
(616) 975-5415 (Office)  
(616) 975-1098 (Fax)  
(616) 780-2398 (Mobile)  
[Nicholas.Clevett@rmtinc.com](mailto:Nicholas.Clevett@rmtinc.com)

Outgoing messages, along with any attachments, are scanned for  
viruses prior to sending.

NOTICE-- This email may contain confidential and privileged  
information for the sole use of the intended recipient. Any  
review or distribution by others is strictly prohibited. If you  
are not the intended recipient, please contact the sender  
immediately and delete all copies.



Trans 00070 Progress Update No.9 Mar 18 to Mar 24 20

346426



**RMT, Inc.**

2025 E. Beltline Ave SE  
Suite 402  
Grand Rapids, MI 49546

Phone: 616-975-5415  
Fax: 616-975-1098

**TRANSMITTAL****No. 00070****PROJECT:** LEC Remediation Services**DATE:** 3/25/2005

**TO:** NJDEP  
Bureau of Federal Case Management  
Div. of Responsible Site Party Remed  
CN028  
Trenton, NJ 08625

**REF:** PPU No. 9**ATTN:** Anthony Cinque

WE ARE SENDING:	SUBMITTED FOR:	ACTION TAKEN:
<input type="checkbox"/> Shop Drawings	<input type="checkbox"/> Approval	<input type="checkbox"/> Approved as Submitted
<input type="checkbox"/> Letter	<input checked="" type="checkbox"/> Your Use	<input type="checkbox"/> Approved as Noted
<input type="checkbox"/> Prints	<input type="checkbox"/> As Requested	<input type="checkbox"/> Returned After Loan
<input type="checkbox"/> Change Order	<input type="checkbox"/> Review and Comment	<input type="checkbox"/> Resubmit
<input type="checkbox"/> Plans		<input type="checkbox"/> Submit
<input type="checkbox"/> Samples	<b>SENT VIA:</b>	<input type="checkbox"/> Returned
<input type="checkbox"/> Specifications	<input type="checkbox"/> Attached	<input type="checkbox"/> Returned for Corrections
<input checked="" type="checkbox"/> Other: Project Progress Update No. 9	<input checked="" type="checkbox"/> Separate Cover Via: Email 3/25/05	<input type="checkbox"/> Due Date:

ITEM NO.	COPIES	DATE	ITEM NUMBER	REV. NO.	DESCRIPTION	STATUS
01	1	3/25/2005			Project Progress Update No. 9	APP
02	1	3/25/2005			Project Progress Update No. 9 Photos	NEW

CC: S. Cipot, R. Alvey, F. Zizilia, J. Prendergast, G. Blyskun, J. Lewis  
C. Anderson, E. Schaub, C. Clavadetscher, J. Rheinhardt, RMT Project Team

**Signed:**

Nick Clevert

**L.E. CARPENTER & COMPANY ~ NJD002168748**  
**BOROUGH OF WHARTON, MORRIS COUNTY, NEW JERSEY**  
**SOURCE REDUCTION REMEDIAL PROJECT PROGRESS UPDATE NO. 9**

---

**Date:** March 25, 2005

**To:** Stephen Cipot, USEPA  
Anthony Cinque, NJDEP

**From:** Nicholas J. Clevett, RMT

**cc:** Robert Alvey, USEPA  
Frances Zizila, USEPA  
John Prendergast, NJDEP  
George Blyskun, NJDEP  
Jim Lewis, LEC  
Cris Anderson, LEC  
Ernie Schaub, LEC  
Colin Clavadetscher, Morris County

Jon Rheinhardt, Borough of Wharton  
Dan Oman, RMT  
Jim Dexter, RMT  
Walter Kurzeja, RMT  
Jeff Macri, RMT  
Dave Pratt, RMT  
Nakia Addison, RMT

**Project No.:** 00-06527.09

**Subject:** SOURCE REDUCTION REMEDIAL ACTION  
Project Progress Update No. 9

**I. SOURCE REDUCTION REMEDIAL ACTIONS - THROUGH MARCH 18<sup>TH</sup> THROUGH MARCH 24<sup>TH</sup> 2005**

1. Continued morning safety briefings (e.g., discussion of daily work scope and associated health and safety procedures)
2. Maintained air monitoring equipment (e.g., Weather Station, Miniram, PID, data loggers etc.) and air monitoring program (e.g., data log download, grab sampling)
3. Maintained all on-site heavy equipment (e.g., excavators, skid steer, off-road truck, screen, etc.)
4. Performed and documented daily inspections on the silt fence as outlined in the certified SESCO
5. Cleaned all paved areas with a skid steer broom attachment
6. Continued to load, transport and dispose of process wastes from the B-1 and B-2 areas. A total of 450 tons of process wastes have been removed from the site. All process waste has been transported off-site for disposal.
7. Continued PCB impacted soil loading, transportation and disposal. To date, a total of 2,727 tons of PCB impacted soils have been excavated, loaded and transported off-site for disposal as non TSCA PCB wastes. When needed, cement kiln dust (CKD) was added to dry the excavated PCB soils prior to transportation and off-site disposal
8. Maintained the batch plant and ancillary equipment to prepare slurry to facilitate the smear zone excavation within the saturated zone.
9. Continued to receive CKD to facilitate drying materials prior to screening and off-site disposal. To date a total of 1,188 tons of CKD (52 loads) have been delivered to the site.
10. An additional 12 bags (24 tons) of bentonite was delivered to the site for slurry blending.
11. Continued smear zone excavation utilizing the slurry mix. Once excavated, CKD was added to these materials to facilitate screening.

**L.E. CARPENTER & COMPANY ~ NJD002168748**  
**BOROUGH OF WHARTON, MORRIS COUNTY, NEW JERSEY**  
**SOURCE REDUCTION REMEDIAL PROJECT PROGRESS UPDATE NO. 9**

---


**II. PROPOSED SOURCE REDUCTION REMEDIAL ACTIONS - MARCH 25<sup>TH</sup> THROUGH MARCH 31<sup>ST</sup> 2005**

1. Continue smear zone excavation, CKD mixing, and screening activities. Initiate off-site disposal of dry screened smear zone soils.




## Photographic Log Progress Update No. 9

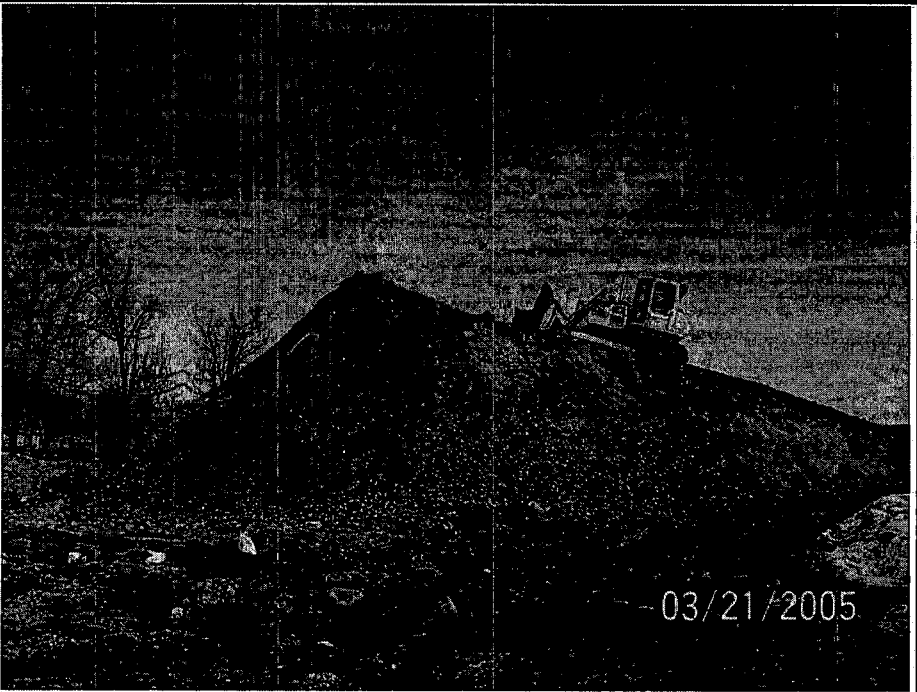
<b>Client Name:</b> L.E. CARPENTER & COMPANY		<b>Site Location:</b> Wharton, Morris County, NJ	<b>Project No.:</b> 00-06527.09
<b>Photo No.</b> 1	<b>Date</b> 3/21/05		
<b>Description</b> Excavating smear zone soils through the slurry			

<b>Photo No.</b> 2	<b>Date</b> 3/21/05	
<b>Description</b> Excavated smear zone cell		



## Photographic Log Progress Update No. 9

<b>Client Name:</b> L.E. CARPENTER & COMPANY		<b>Site Location:</b> Wharton, Morris County, NJ	<b>Project No.:</b> 00-06527.09
<b>Photo No.</b> 3	<b>Date</b> 3/21/05		
<b>Description</b> Mixing and screening smear zone soils			

<b>Photo No.</b> 4	<b>Date</b> 3/21/05		
<b>Description</b> Excavated and screened smear zone stockpile			
