

Confidential Claim Retracted

AUTHORIZED BY: SL

DATE: 5/16/13

REDACTED VERSION

Jackpile Reclamation Project

PUEBLO OF LAGUNA

P.O. BOX 194

LAGUNA, NEW MEXICO 87026

Office of
Reclamation Project Manager

March 10, 1990


(505) 243-7616
(505) 552-6654
(505) 552-6655

TO: Governor Conrad Lucero

FROM: Jim Olsen, Jr., P.E.-Reclamation Project Manager *JS*

SUBJ: Monthly Activities Report-February, 1990

I. OPERATIONS: February, 1990 marked the second month of full-scale earth-moving activities. The primary activity was the continued hauling of procore to backfill the North Paguete Pit. Pile #14 was substantially completed during February and the scraper fleet moved to Pile #15. The truck/loader fleet continued on Pile #1 and is progressing ahead of schedule. The dewatering of the North Pit is almost complete and will be so sometime during March. Preparations to begin dewatering the South Paguete Pit began in February and should commence in March. Dismantling of the Jackpile structures also continued with the old Pit Offices almost completed. Dozer work included sloping a waste dump in the North Paguete and then the majority of the fleet began sloping work in three areas in the South Paguete Pit. Several work packages have been submitted by the LCC for final acceptance and closure and the details are included in Landmark/Westons's report (attached.)

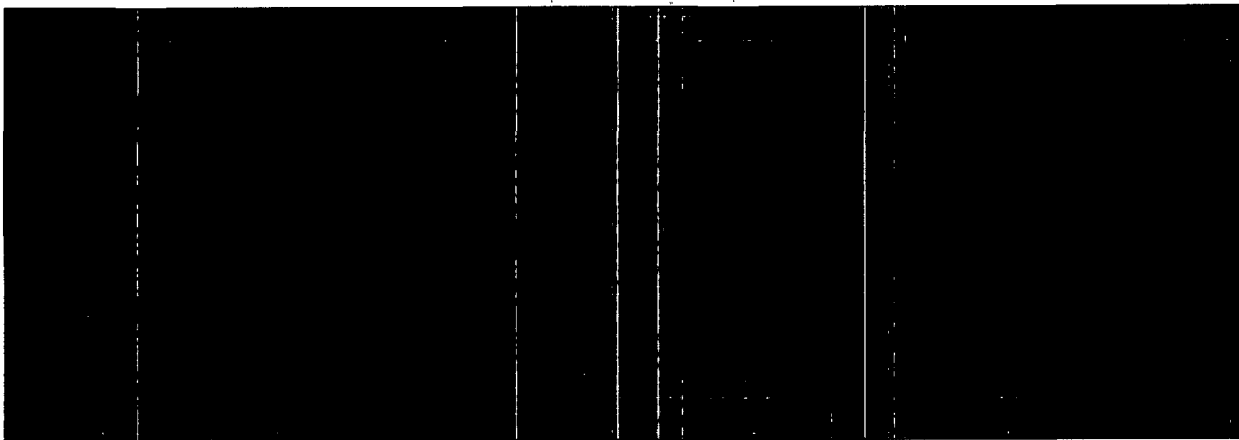

9322312

CONFIDENTIAL

POL-EPA01-0011843

III. ENGINEERING ITEMS: Mike Bone continued the development of his analysis of the slope and erosion control designs and will be making a list of his recommendations in March due to some other commitments of his time. Jacobs delivered the final Specifications summary. Landmark has established Time & Materials contract with Eberline to perform radiological services. The first annual water quality data was delivered by Re/Spec Consulting. They are preparing a cost estimate on developing a Data Base for the water quality work. The monitor well sites will be located in March by LCC. The weather station components have not been completely delivered so its installation will probably not take place until March. Eberline is fabricating some high-volume air samplers which should be placed in-service in March. Further work by Ken King is pending a funding source (possibly the BIA area office.)

IV. OTHER ITEMS: No response from BIA management on the final disposition of the CMC issue has been finalized. Roger Baer has briefed the Area Office management and some of the Washington personnel. Under the "Preliminary Agreement" with Landmark, their services continue at the agreed-upon rates. Requests for authorization of two additional work packages (one for the old highway reconnections & one for some sloping work in the North Paguate that were unanticipated and not included in the 1st Year Plan) were submitted for your approval. The highway reconnections will become especially important since the LCC will need to begin hauling protore across the highway beginning as early as late May, 1990. A request for LCC to perform building construction activities at Laguna Industries was also submitted.

pc: Roger Baer-Project Engineer, BIA
Yamie Leeds-Agency Superintendent, BIA
Pueblo Council & Staff Officers
