



ENVIRON

June 11, 1999

Federal Express

U.S. Environmental Protection Agency
2890 Woodbridge Avenue
Bldg. 209 (MS-211)
Edison, New Jersey 08837
Attention: Cornell-Dubilier Electronics Site On-Scene Coordinator

Chief, New Jersey Superfund Branch
Office of Regional Counsel
United States Environmental Protection Agency
290 Broadway, 17th Floor
New York, New York 10007-1866
Attention: Cornell-Dubilier Electronics Site Attorney

Re: Cornell-Dubilier Electronics Site - Administrative Order on Consent for Removal
Action, Index No. II-CERCLA-99-2006
Progress Report No. 7

Dear Sirs:

As specified in Paragraph 50 of the above-referenced Administrative Order, on behalf of Respondents Cornell Dubilier Electronics, Inc. (CDE) and Dana Corporation (Dana), ENVIRON Corporation (ENVIRON) is submitting this progress report which summarizes activities conducted pursuant to this AOC between May 20, 1999 and June 2, 1999.

Completed Activities

During this period, the following activities were completed:

- Completed revisions to the *Removal Action Work Plan for Tier II Residential Properties* (Work Plan) to address USEPA's comments. The Revised Work Plan was submitted to USEPA on May 21, 1999.
- Completed detailed excavation and restoration plans based on the scope of work presented in the Revised Work Plan.
- As of May 26, 1999, all homeowners having large trees located within proposed excavation areas had been contacted regarding tree removal necessary to implement the required soil excavation.

Ongoing Activities

During this period, the following activities were initiated and/or are in-progress:

- Identification of prospective contractors, including remediation contractors and landscape contractors.
- Validation of verification sampling data.
- Preparation of the request for bid to be issued to prospective remediation contractor(s).
- Follow-up discussions regarding the request for access to Tier II Property W via the Hamilton Industrial Park, and for access to the property adjacent to Tier II Property AA.

Two-Week Schedule of Planned Activities

In addition to the ongoing activities, during the next two-week period (June 3, 1999 through June 16, 1999) the following activities are planned:

- Distribution of the request for bid to prospective remediation contractor(s).
- Completion of validation reports for verification sampling data.


One-Month Schedule of Planned Field Activities

During the next four-week period (June 3, 1999 through June 30, 1999), the following field activities are planned:

- Collection of additional verification samples as needed.

Please call me or Mark Nielsen at (609) 452-9000 if you should have any questions regarding this progress report.

Sincerely,



Michael P. Scott
Principal

MPS:jmn

\\PRINCETON_NT2\HOME\Nielsen\02-5840D\5840d_19.doc

cc: R. Sanoff, Esq.
M. Last, Esq.

5/28/09

PROPERTY B - Cindy Kane, 501 Garibaldi Avenue

- uneven landscape
- pockets where sod did not take
- fence unstable in a few areas.

* resident unhappy with condition of their lawn.
(front + back)

PROPERTY C - A. Chavarriga, 800 Garibaldi, (fence ok)
- looks fine, resident is happy with job.

PROPERTY E - Margaret Reidy, 204 Spicer Avenue
no issues. Resident is happy w/ job
- Geotek left on storm inlet

PROPERTY F - ~~John~~ Diwan War, 210 Spicer Avenue
- Brown Sod front and back lawn.
- excavator tracks visible (front yard left of house)
- Bare pockets, holes (near of house)
- resident very unhappy. (fence o.k.)

PROPERTY I - Frank Riccardi, 305 Spicer (fence ok)
- plant dogwood
- no other issues.

PROPERTY N - Finish planting garden
Nick in vinyl siding
Garden to be completed
(fence completed)


Hamilton Industrial Park

- PUT FENCE BACK UP. 1

501 G

cross hatch
area is uneven

spicer

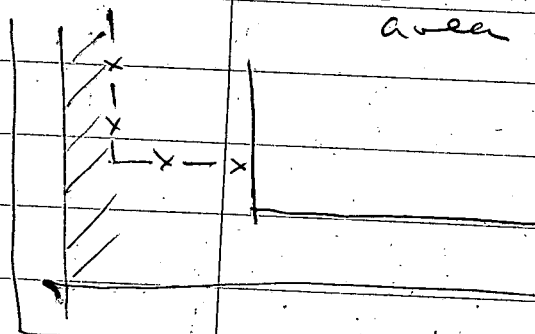


barbaldi

back area w/in fence
is worse than front

got disturbed during
fence installation and
tree planting

-have spots where landscaping
stone was temporarily staged

210 Sprir

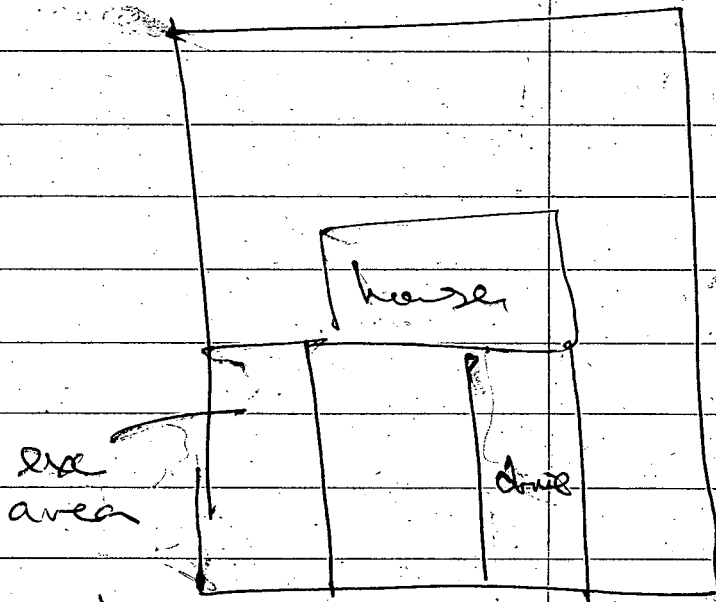

sod is
bad and
trucks visible

Also touch up necessary in
back yard.
