Figure 10
Preliminary RI/FS Schedule - AOI-1

ID	Task Name	Duration	Scheduled Start	Scheduled Finish
1	**REPORTING (Begins after approval of RI/FS Workplan)**	**1428 days**	**Fri 4/15/16**	**Thu 3/12/20**
2	Bi-Monthly Progress Report (Due 15th of every other month)	1428 days	Fri 4/15/16	Thu 3/12/20
3	**SITE CHARACTERIZATION (Assumes approval of RI/FS Work Plan)**	**964 days**	**Fri 4/15/16**	**Tue 12/4/18**
4	Provide Field Notice and Insurance Certificates to EPA	15 days	Fri 4/15/16	Fri 4/29/16
5	Iteration 1 - On-Property Investigations (Soil, GW, SW, Sediment)	360 days	Mon 5/2/16	Wed 4/26/17
6	Iteration 1 - Off-Property Investigations (Soil, Groundwater)	360 days	Mon 5/2/16	Wed 4/26/17
7	Iteration 1 - Background Soil Investigation	360 days	Mon 5/2/16	Wed 4/26/17
8	Iteration 1 - Data Assessment	75 days	Thu 4/27/17	Mon 7/10/17
9	Data Assessment Meeting with EPA/TCEQ	1 day	Tue 7/11/17	Tue 7/11/17
10	Iteration 1 - Development of Draft Workplan Refinement Notice (WRN)	45 days	Wed 7/12/17	Fri 8/25/17
11	***Iteration 1 - Review/Comment on WRN - EPA/TCEQ***	30 days	Sat 8/26/17	Sun 9/24/17
12	Iteration 1 - Prepare Final WRN	15 days	Mon 9/25/17	Mon 10/9/17
13	***Review/Approve Final WRN - EPA/TCEQ***	15 days	Tue 10/10/17	Tue 10/24/17
14	Iteration 2 - Off-Property Investigations (Vince Bayou Surface Water, Sediment)	90 days	Tue 10/10/17	Sun 1/7/18
15	Iteration 2 - Background Sediment/Surface Water Investigation	90 days	Tue 10/10/17	Sun 1/7/18
16	Iteration 2 - Data Assessment	60 days	Mon 1/8/18	Thu 3/8/18
17	Iteration 2 - Data Assessment Meeting with EPA/TCEQ	1 day	Fri 3/9/18	Fri 3/9/18
18	Iteration 2 - Development of Draft WRN	45 days	Sat 3/10/18	Mon 4/23/18
19	***Iteration 2 - Review/Comment on WRN - EPA/TCEQ***	30 days	Tue 4/24/18	Wed 5/23/18
20	Iteration 2 - Prepare Final WRN	15 days	Thu 5/24/18	Thu 6/7/18
21	***Review/Approve Final WRN - EPA/TCEQ***	15 days	Fri 6/8/18	Fri 6/22/18
22	Iteration 3 - Off-Property Investigations (Vince Bayou Biota)	120 days	Fri 6/8/18	Fri 10/5/18
23	Iteration 3 - Background Biota (if needed)	120 days	Fri 6/8/18	Fri 10/5/18
24	Iteration 3 - Data Assessment	60 days	Sat 10/6/18	Tue 12/4/18
25	Iteration 3 - Data Assessment Meeting with EPA/TCEQ	1 day	Tue 12/4/18	Tue 12/4/18
26	**SCREENING LEVEL ECOLOGICAL RISK ASSESSMENT**	**240 days**	**Wed 12/5/18**	**Thu 8/1/19**
27	Prepare Draft SLERA	90 days	Wed 12/5/18	Mon 3/4/19
28	***Review/Comment on SLERA - EPA/TCEQ***	60 days	Tue 3/5/19	Fri 5/3/19
29	Prepare Final SLERA	60 days	Sat 5/4/19	Tue 7/2/19
30	***Review/Approve Final SLERA - EPA/TCEQ***	30 days	Wed 7/3/19	Thu 8/1/19
31	**BASELINE ECOLOGICAL RISK ASSESSMENT (IF NEEDED)**	**TBD**	**Sun 7/22/18**	**Mon 3/25/19**
33	**BASELINE HUMAN HEALTH RISK ASSESSMENT**	**300 days**	**Wed 12/5/18**	**Mon 9/30/19**
34	Prepare Draft BHHRA	120 days	Wed 12/5/18	Wed 4/3/19
35	***Review/Comment on Draft BHHRA - EPA/TCEQ***	60 days	Thu 4/4/19	Sun 6/2/19
36	Prepare Final BHHRA	90 days	Mon 6/3/19	Sat 8/31/19
37	***Review/Approve Final BHHRA - EPA/TCEQ***	30 days	Sun 9/1/19	Mon 9/30/19
38	**REMEDIAL INVESTIGATION REPORT**	**300 days**	**Sun 2/3/19**	**Fri 11/29/19**
39	Prepare Draft RI Report	120 days	Sun 2/3/19	Sun 6/2/19
40	***Review/Comment on Draft RI Report - EPA/TCEQ***	60 days	Mon 6/3/19	Thu 8/1/19
41	Prepare Final RI Report	90 days	Fri 8/2/19	Wed 10/30/19
42	***Review/Approve Final RI Report - EPA/TCEQ***	30 days	Thu 10/31/19	Fri 11/29/19
43	**FEASIBILITY STUDY**	**300 days**	**Sat 11/30/19**	**Thu 9/24/20**
44	Prepare Draft FS Report	120 days	Sat 11/30/19	Sat 3/28/20
45	***Review/Comment on Draft FS Report - EPA/TCEQ***	60 days	Sun 3/29/20	Wed 5/27/20
46	Prepare Final FS Report	90 days	Thu 5/28/20	Tue 8/25/20
47	***Review/Approve Final FS Report - EPA/TCEQ***	30 days	Wed 8/26/20	Thu 9/24/20

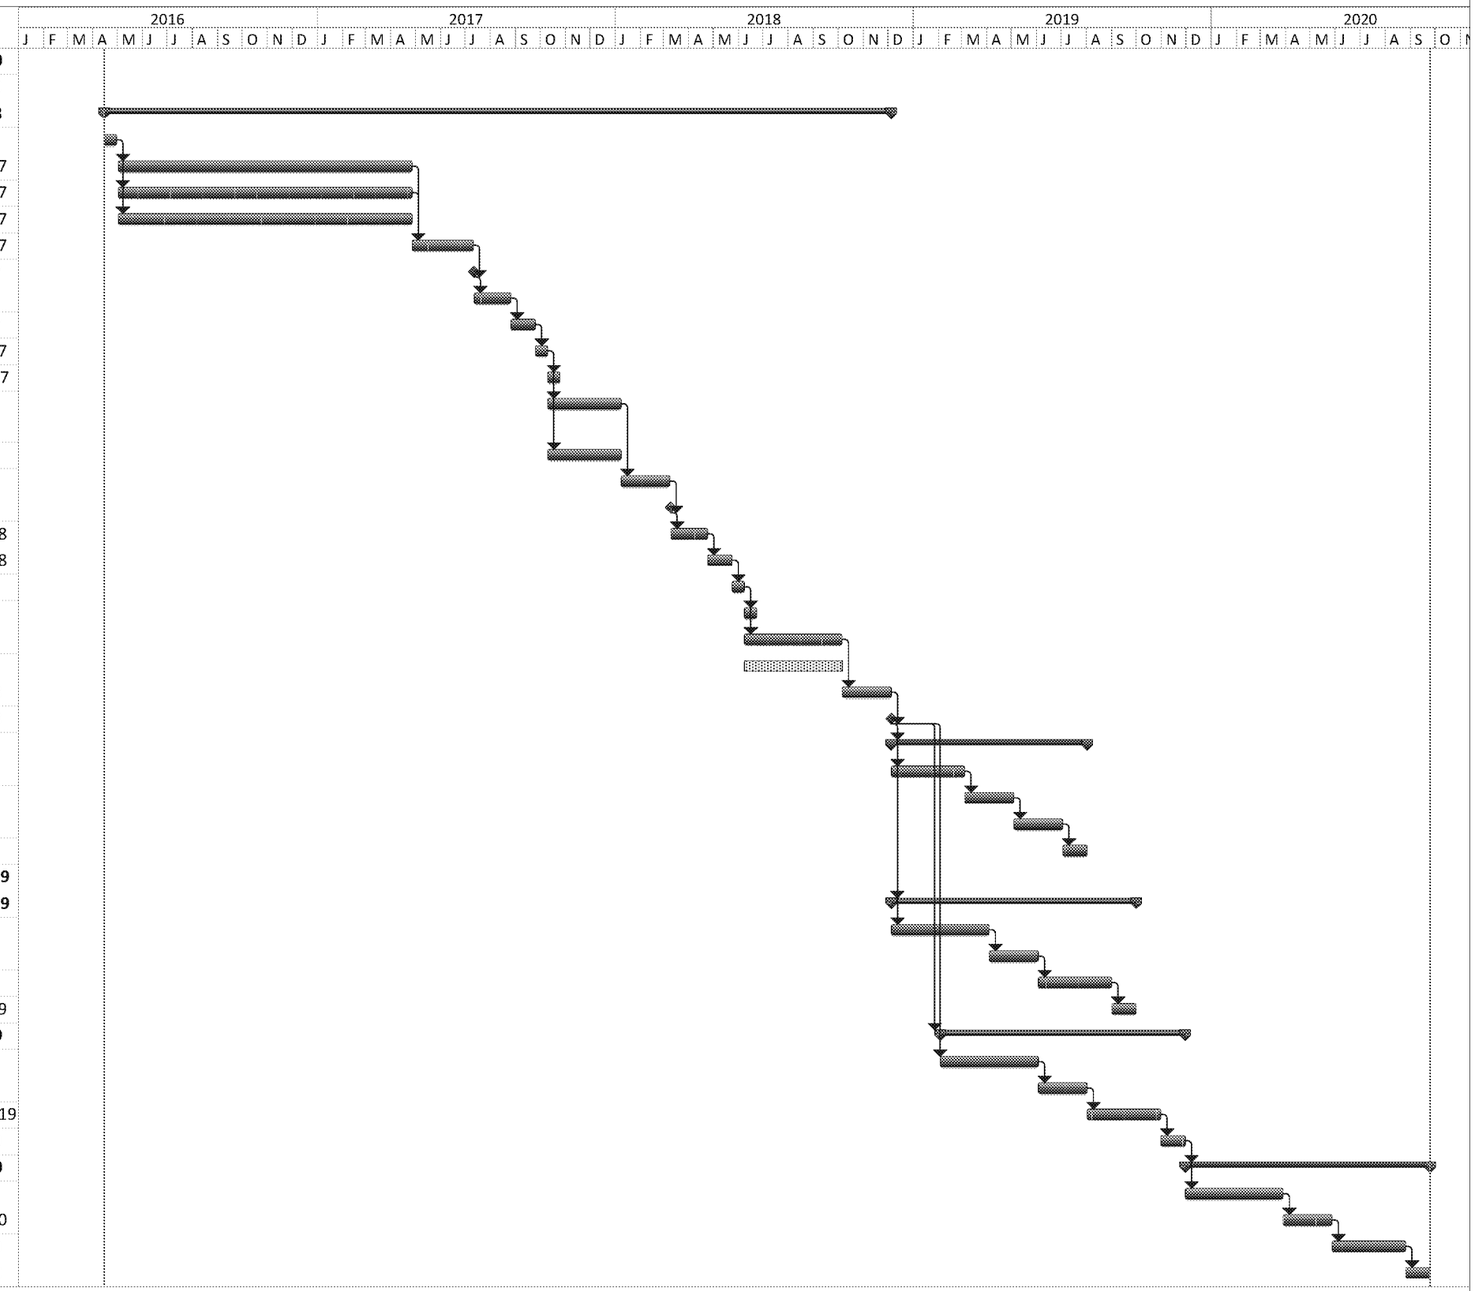

US Oil Superfund Site
Pasadena, Harris County, TX
Page 1 of 1

Task		Project Summary		Inactive Summary		Manual Summary		Deadline	
Milestone		External Milestone		Duration-only		Start-only		Progress	
Summary		Inactive Milestone		Manual Summary Rollup		Finish-only		If Necessary	

This schedule is subject to revision based on changes in assumed EPA review periods, weather, modifications to the scope of work, delays in obtaining access to properties, and/or potential interference with removal actions and associated field work.
