Falcon Refinery Removal Action - Critical Path Diagram

ID	Task Mode	Task Name	Duration	Start	Finish
1		Falcon Refinery Removal Action Start Date	130 days	Mon 4/2/12	Fri 9/28/12
2		**Install Treatment System & Construct Irrigation Field**	3 wks	Mon 4/2/12	Fri 4/20/12
3		**O&M Treatment System & Land Application**	16 wks	Mon 4/23/12	Fri 8/10/12
4		**Reclamation of Oil in Tank 26 - Centrifuge**	6 wks	Mon 8/13/12	Fri 9/21/12
5		**Disposal of Residual Solids throughout Reclamation**	6 wks	Mon 8/20/12	Fri 9/28/12
6		**Removal of Roof Structures/Demolition & Recycling of Tanks**	**136 days**	**Mon 4/2/12**	**Mon 10/8/12**
7		**Tank 12**	**33 days**	**Mon 4/9/12**	**Wed 5/23/12**
8		Roof Removal	6 days	Mon 4/9/12	Mon 4/16/12
9		Cleanout of Tanks / Housekeeping in Tank Area	4 days	Tue 4/10/12	Fri 4/13/12
10		Inspection of Tanks	3 days	Mon 4/16/12	Wed 4/18/12
11		Tank Floor Removal/Excavation	25 days	Thu 4/19/12	Wed 5/23/12
12		**Tank 7**	**123 days**	**Tue 4/10/12**	**Thu 9/27/12**
13		Roof Removal	7 days	Tue 4/10/12	Wed 4/18/12
14		Cleanout of Tanks / Housekeeping in Tank Area	3 days	Thu 8/23/12	Mon 8/27/12
15		Tank Floor Removal/Excavation	23 days	Tue 8/28/12	Thu 9/27/12
16		**Tank 30**	**129 days**	**Wed 4/11/12**	**Mon 10/8/12**
17		Roof Removal	15 days	Wed 4/11/12	Tue 5/1/12
18		Cleanout of Tanks / Housekeeping in Tank Area	4 days	Thu 8/23/12	Tue 8/28/12
19		Tank Floor Removal/Excavation	29 days	Wed 8/29/12	Mon 10/8/12
20		**Tank 26**	**10 days**	**Mon 8/20/12**	**Fri 8/31/12**
21		Demolition and Recycling	3 days	Mon 8/20/12	Wed 8/22/12
22		Cleanout of Tanks / Housekeeping in Tank Area	7 days	Thu 8/23/12	Fri 8/31/12
23		Disposal of Fiberglass from Tanks	3 days	Mon 8/20/12	Wed 8/22/12
24		**Tanks 20, 24, 10, 27**	**7 days**	**Mon 4/2/12**	**Tue 4/10/12**
25		Disposal of Fiberglass from Tanks	7 days	Mon 4/2/12	Tue 4/10/12

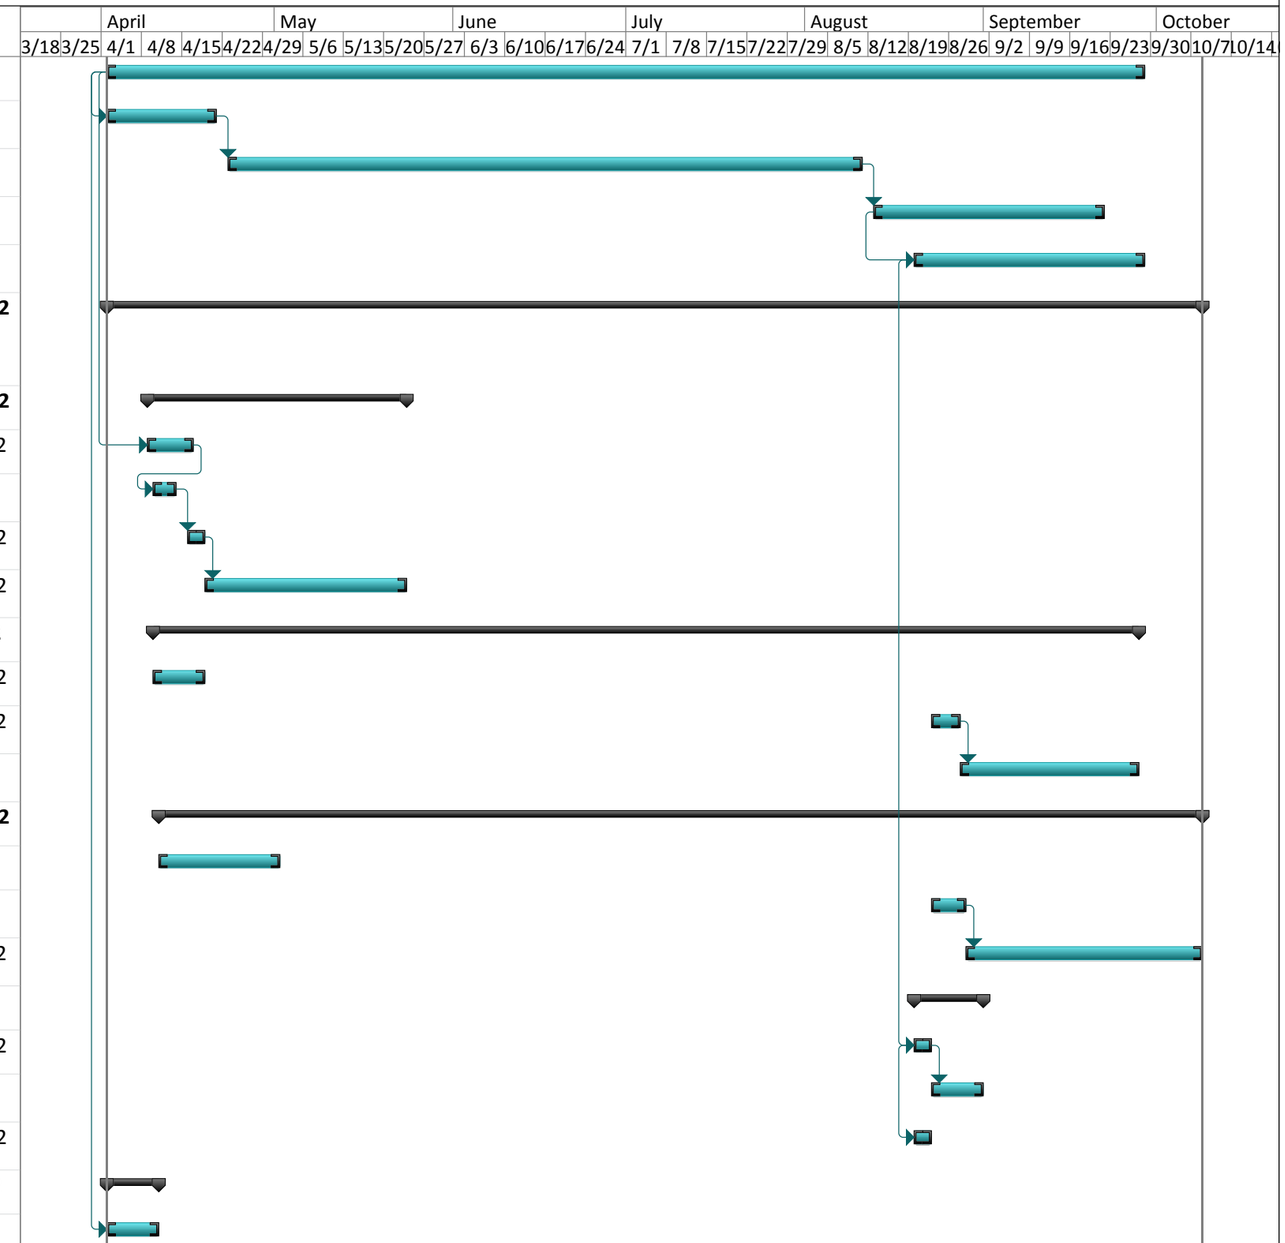

Project: MS Pjt Falcon Draft
Date: Mon 4/2/12

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

9568489
