ID		Task Mode	Task Name	Duration	Start	Finish
1			**OC-0026/308 Hauser (Judy Lee Peters)**	**7 days**	**Mon 6/13/16**	**Wed 6/22/16**
2			One Call/Blind Sweeps	1 day	Mon 6/13/16	Mon 6/13/16
3			Dirt Work/Sod Installation	6 days	Tue 6/14/16	Wed 6/22/16
4			**OC-0006/11 N. Norris (Douglas Violette)**	**14 days**	**Mon 6/13/16**	**Tue 7/5/16**
5			One Call/Blind Sweeps	1 day	Mon 6/13/16	Mon 6/13/16
6			Dirt Work/Sod Installation	11 days	Thu 6/16/16	Tue 7/5/16
7			**OC-0076/100 Mulcahy Rd (Patrick Mulcahy)**	**8 days**	**Mon 6/13/16**	**Thu 6/23/16**
8			One Call/Blind Sweeps	1 day	Mon 6/13/16	Mon 6/13/16
9			Dirt Work/Sod Installation	1 day	Thu 6/23/16	Thu 6/23/16
10			**OC-0004B/1010 Rickards (Pete Reisenauer)**	**10 days**	**Wed 6/22/16**	**Fri 7/8/16**
11			One Call/Blind Sweeps	3 days	Wed 6/22/16	Mon 6/27/16
12			Dirt Work/Sod Installation	9 days	Mon 6/27/16	Fri 7/8/16
13			**OC-0072/75 Ashleigh Drive (David Zimmer)**	**17 days**	**Wed 6/22/16**	**Wed 7/20/16**
14			One Call/Blind Sweeps	8 days	Wed 6/22/16	Tue 7/5/16
15			Dirt Work/Sod Installation	10 days	Tue 7/5/16	Wed 7/20/16
16			**OC-0007/7 Norris (Edward Jones)**	**9 days**	**Wed 6/22/16**	**Wed 7/6/16**
17			One Call/Blind Sweeps	9 days	Wed 6/22/16	Wed 7/6/16
18			Dirt Work/Sod Installation	1 day	Wed 7/6/16	Wed 7/6/16
19			**OC-0093/116 N. Preston St. (Richard Morse)**	**7 days**	**Tue 7/5/16**	**Thu 7/14/16**
20			One Call/Blind Sweeps	3 days	Tue 7/5/16	Thu 7/7/16
21			Dirt Work/Sod Installation	5 days	Thu 7/7/16	Thu 7/14/16
22			**OC-0011/10 N. Hauser (Serge Myers)**	**3 days**	**Mon 7/11/16**	**Wed 7/13/16**
23			One Call/Blind Sweeps	2 days	Mon 7/11/16	Tue 7/12/16
24			Dirt Work/Sod Installation	2 days	Tue 7/12/16	Wed 7/13/16
25			**OC-0095/107 S. Hauser St. (Rick Hamilton)**	**17 days**	**Tue 7/12/16**	**Tue 8/9/16**
26			One Call/Blind Sweeps	3 days	Tue 7/12/16	Thu 7/14/16
27			Dirt Work/Sod Installation	15 days	Thu 7/14/16	Tue 8/9/16
28			**OC-0061/801 Rickards (Shaun Hoolahan)**	**26 days**	**Mon 7/18/16**	**Tue 8/30/16**
29			One Call/Blind Sweeps	3 days	Mon 7/18/16	Wed 7/20/16
30			Dirt Work/Sod Installation	24 days	Wed 7/20/16	Tue 8/30/16
31			**OC-0025/500 S. Hauser (Franklin Cooney)**	**18 days**	**Tue 7/19/16**	**Wed 8/17/16**
32			One Call/Blind Sweeps	1 day	Tue 7/19/16	Tue 7/19/16
33			Dirt Work/Sod Installation	12 days	Thu 7/28/16	Wed 8/17/16
34			**OC-0086/19 S. Hauser St. (Rosemarie Silzly)**	**7 days**	**Thu 8/4/16**	**Tue 8/16/16**
35			One Call/Blind Sweeps	2 days	Thu 8/4/16	Mon 8/8/16
36			Dirt Work/Sod Installation	6 days	Mon 8/8/16	Tue 8/16/16
37			**OC-0014B/808 Stewart St. (Ted Minnehan)**	**7 days**	**Thu 8/4/16**	**Tue 8/16/16**
38			One Call/Blind Sweeps	2 days	Thu 8/4/16	Mon 8/8/16
39			Dirt Work/Sod Installation	6 days	Mon 8/8/16	Tue 8/16/16

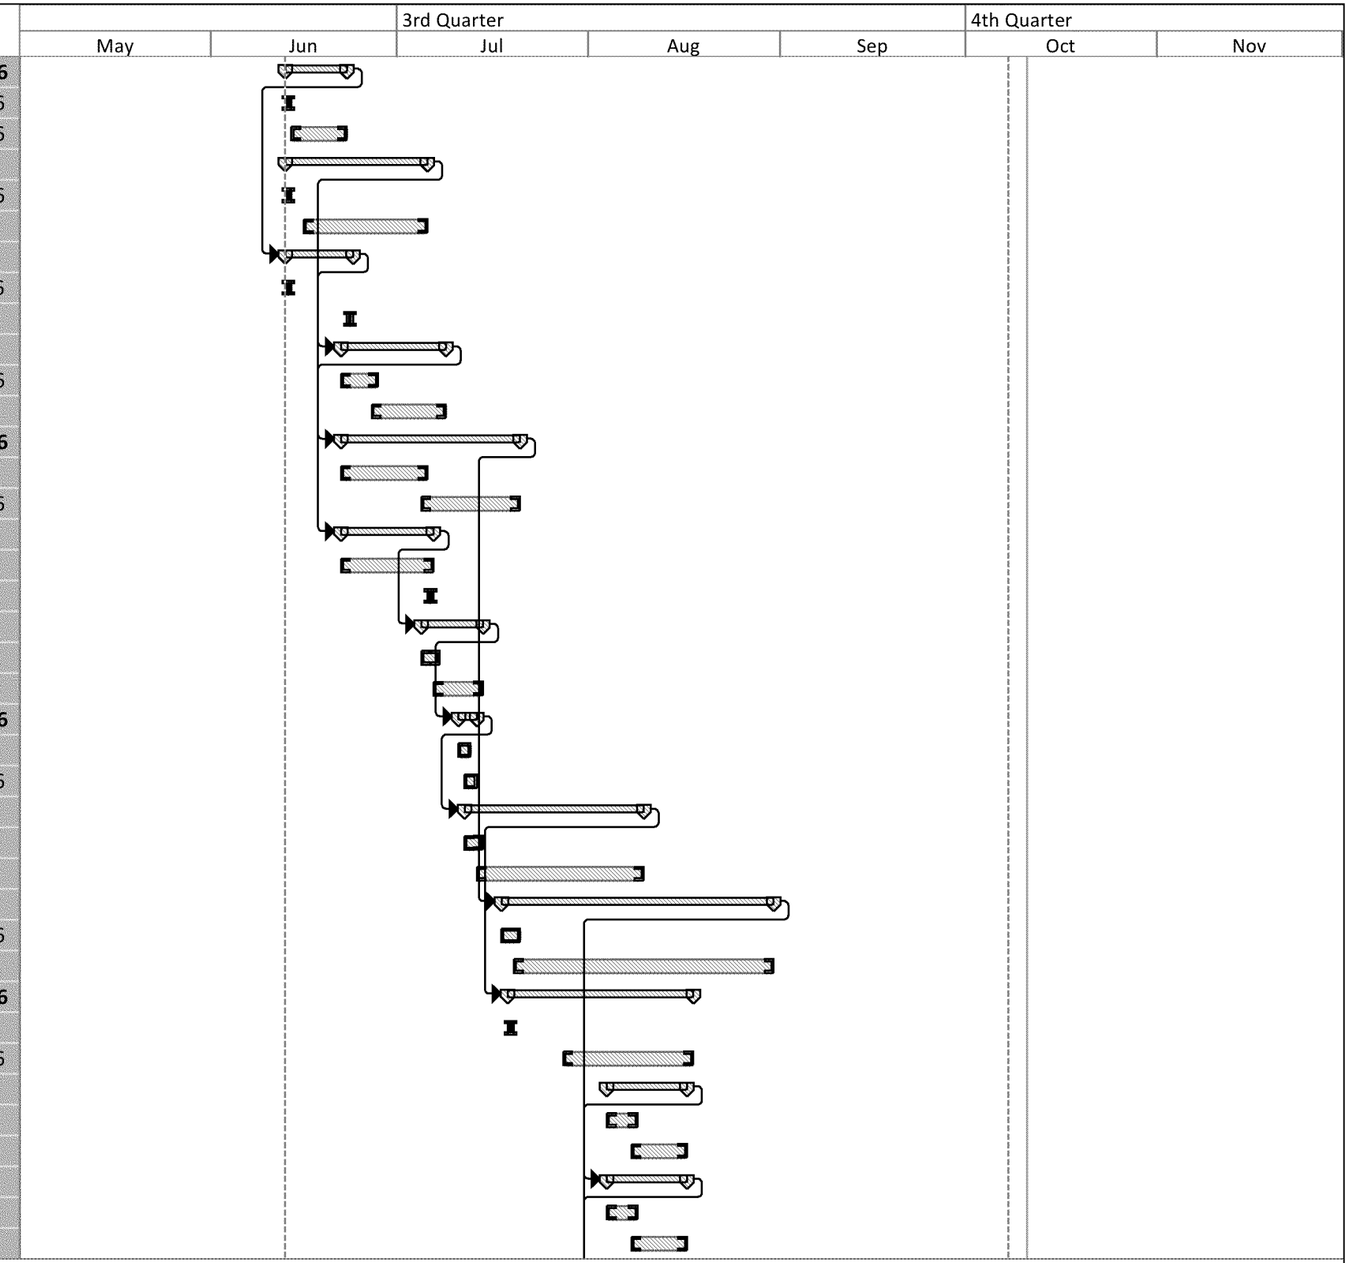

Project: Wasley Excavating CSOU
Date: Tue 10/11/16

Task	Project Summary	Inactive Milestone	Manual Summary Rollup	Deadline
Split	External Tasks	Inactive Summary	Manual Summary	Progress
Milestone	External Milestone	Manual Task	Start-only	
Summary	Inactive Task	Duration-only	Finish-only	

ID		Task Mode	Task Name	Duration	Start	Finish
40			**OC-0016/6S. Hauser (Serge Myers)**	**7 days**	**Thu 8/4/16**	**Tue 8/16/16**
41			One Call/Blind Sweeps	3 days	Thu 8/4/16	Tue 8/9/16
42			Dirt Work/Sod Installation	5 days	Tue 8/9/16	Tue 8/16/16
43			**OC-0029/700 Stewart St. (Charles Walrod)**	**7 days**	**Thu 8/4/16**	**Tue 8/16/16**
44			One Call/Blind Sweeps	5 days	Thu 8/4/16	Thu 8/11/16
45			Dirt Work/Sod Installation	3 days	Thu 8/11/16	Tue 8/16/16
46			**OC-0085/1006 E. Stewart St. (Rosemarie Silzly)**	**8 days**	**Thu 8/4/16**	**Wed 8/17/16**
47			One Call/Blind Sweeps	7 days	Thu 8/4/16	Tue 8/16/16
48			Dirt Work/Sod Installation	2 days	Tue 8/16/16	Wed 8/17/16
49			**OC-0009/1105 Stewart St. (David Schlosser)**	**13 days**	**Tue 8/9/16**	**Tue 8/30/16**
50			One Call/Blind Sweeps	6 days	Tue 8/9/16	Wed 8/17/16
51			Dirt Work/Sod Installation	10 days	Mon 8/15/16	Tue 8/30/16
52			**OC-0018/1019 Crosby St. (James Svendsen)**	**31 days**	**Tue 8/16/16**	**Fri 10/7/16**
53			One Call/Blind Sweeps	3 days	Tue 8/16/16	Thu 8/18/16
54			Dirt Work/Sod Installation	30 days	Thu 8/18/16	Fri 10/7/16
55			**OC-0021/1002 Smith (William Field)**	**3 days**	**Mon 8/29/16**	**Wed 8/31/16**
56			One Call/Blind Sweeps	3 days	Mon 8/29/16	Wed 8/31/16
57			Dirt Work/Sod Installation	1 day	Wed 8/31/16	Wed 8/31/16
58			**OC-0071/169 Ashley Dr. (Douglas Krattiger)**	**4 days**	**Mon 8/29/16**	**Thu 9/1/16**
59			One Call/Blind Sweeps	4 days	Mon 8/29/16	Thu 9/1/16
60			Dirt Work/Sod Installation	1 day	Thu 9/1/16	Thu 9/1/16
61			**OC-0060/700 Rickards (Duane Colwell)**	**0 days**	**No Action**	**No Action**
62			One Call/Blind Sweeps	0 days	No Action	No Action
63			Dirt Work/Sod Installation	0 days	No Action	No Action
64			**OC-0012/8 N. Hauser (Serge Myers)**	**6 days**	**Thu 9/1/16**	**Mon 9/12/16**
65			One Call/Blind Sweeps	3 days	Thu 9/1/16	Tue 9/6/16
66			Dirt Work/Sod Installation	4 days	Tue 9/6/16	Mon 9/12/16
67			**OC-0074/3332 Crackerville (Scott Russ)**	**5 days**	**Wed 8/31/16**	**Wed 9/7/16**
68			One Call/Blind Sweeps	4 days	Wed 8/31/16	Tue 9/6/16
69			Dirt Work/Sod Installation	2 days	Tue 9/6/16	Wed 9/7/16
70			**OC-0078/160 ABC Drive (Andrew Gress)**	**11 days**	**Thu 9/8/16**	**Tue 9/27/16**
71			One Call/Blind Sweeps	4 days	Thu 9/8/16	Wed 9/14/16
72			Dirt Work/Sod Installation	8 days	Wed 9/14/16	Tue 9/27/16

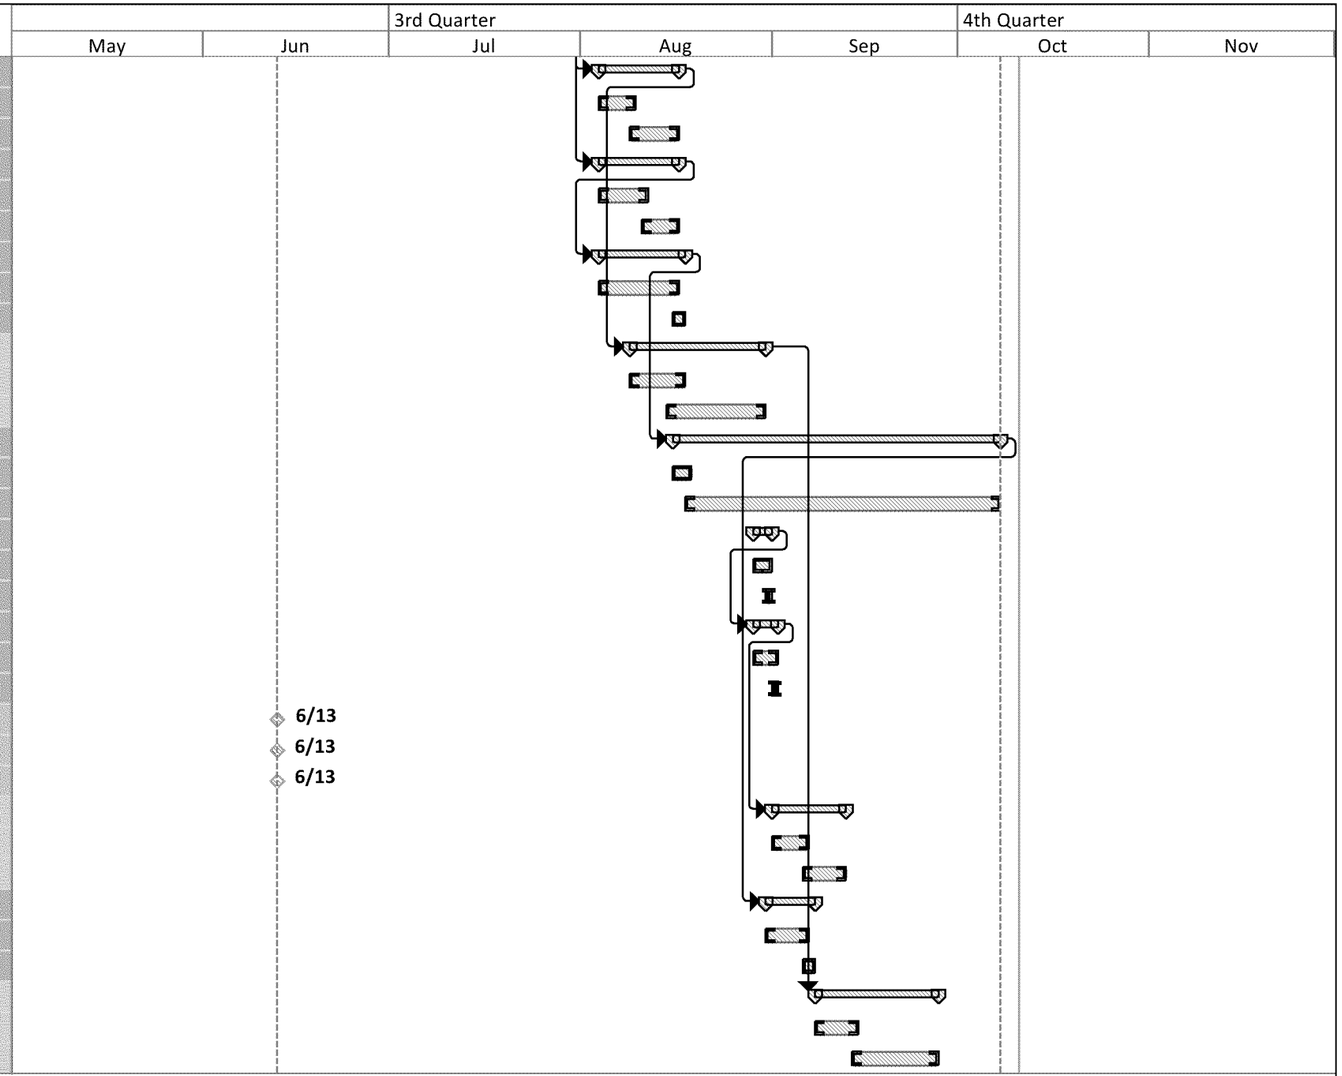

Project: Wasley Excavating CSOU
Date: Tue 10/11/16

Task	Project Summary	Inactive Milestone	Manual Summary Rollup	Deadline
Split	External Tasks	Inactive Summary	Manual Summary	Progress
Milestone	External Milestone	Manual Task	Start-only	
Summary	Inactive Task	Duration-only	Finish-only	
