ID	Task Name	Duration	Start	Finish
1	Site Access Agreement with 216 Slauson	0 days	Tue 6/4/19	Tue 6/4/19
2	Containerized Solid Waste Disposal	0 days	Tue 6/4/19	Tue 6/4/19
3	**Soil and Soil Vapor Investigation Program**	**27 days**	**Thu 5/30/19**	**Fri 7/5/19**
4	Preparation and Coordination	5 days	Thu 5/30/19	Wed 6/5/19
5	Field Work	4 days	Thu 6/6/19	Tue 6/11/19
6	Lab Analysis, Data Evaluation And Report Preparation	18 days	Wed 6/12/19	Fri 7/5/19
7	Report Submittal to EPA and RWQCB	0 days	Fri 7/5/19	Fri 7/5/19
8	Preparation of Soil Excavation Workplan	20 days	Mon 6/24/19	Fri 7/19/19
9	Submittal of Soil Excavation Workplan	0 days	Fri 7/19/19	Fri 7/19/19
10	EPA and RWQCB Review	30 days	Mon 7/8/19	Fri 8/16/19
11	Demolition of 216 Slauson	35 days	Mon 7/1/19	Fri 8/16/19
12	**Remedial Implementation**	**40 days**	**Mon 8/19/19**	**Fri 10/11/19**
13	Planning and Preparation	10 days	Mon 8/19/19	Fri 8/30/19
14	Excavation, Laboratory Evaluation and Backfilling	15 days	Mon 9/2/19	Fri 9/20/19
15	Completion Report Preparation	15 days	Mon 9/23/19	Fri 10/11/19
16	Report Submittal to EPA and RWQCB	0 days	Fri 10/11/19	Fri 10/11/19
17	EPA and RWQCB Review	20 days	Mon 10/14/19	Fri 11/8/19
18	Agency Determination of No Further Action	0 days	Fri 11/22/19	Fri 11/22/19

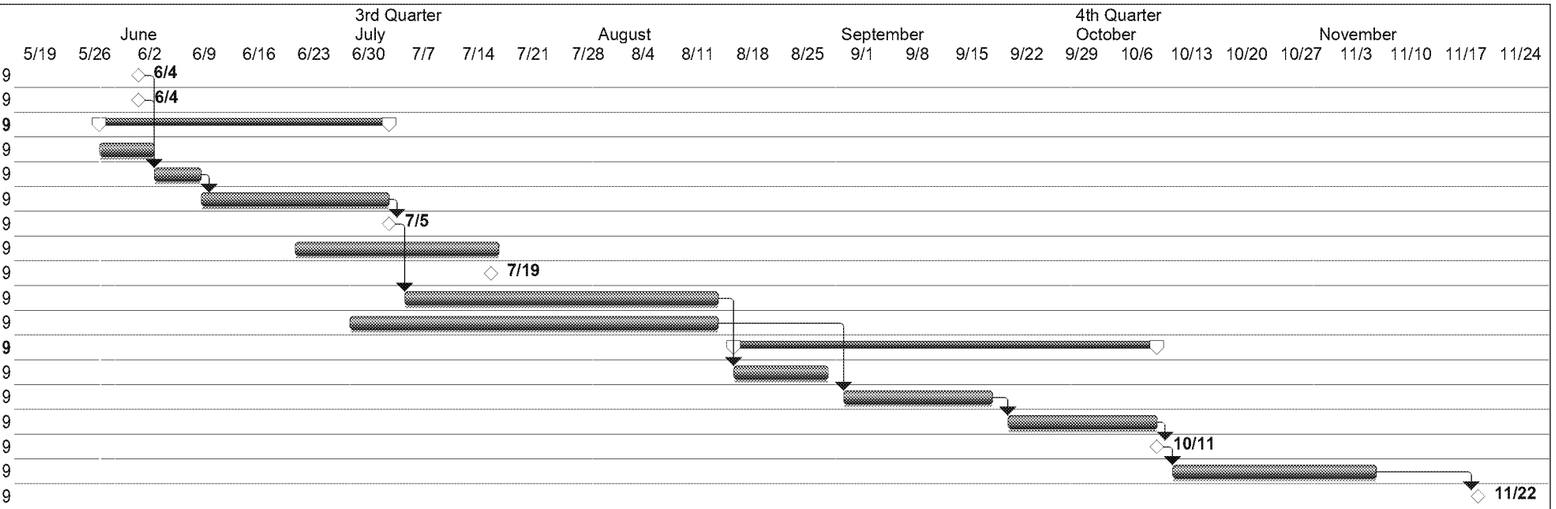

Project: 210 Slauson - Investigation and Remediation Schedule
Date: Thu 5/30/19

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
