November 23, 1987



Ms. Janet Feldstein
SCP - Carlstadt Project Officer
Emergency and Remedial Response Division
U.S. Environmental Protection Agency
26 Federal Plaza
New York, New York 10278

Re: Revision No. 6

Project Operations Plan

SCP Site Remedial Investigation

Carlstadt, New Jersey

Dear Ms. Feldstein:

The following revisions to the March 4, 1987 Project Operations Plan (POP) are based on USEPA requirements for additional soil sampling. These revisions supercede items (6) and (7) of Revision No. 2 to the POP, dated July 2, 1987.

- 1. Paragraph 7.11.5.2: The first sample will be collected at the depth interval from grade to the ground water table, or a total depth of 2 feet, whichever is less. The second sample will be collected at the depth interval of 5-6 feet. The third sample will be collected at the top of the clay layer.
- 2. <u>Table 7-3. Note 1</u>: Sample collected at the depth interval from grade to the ground water table, or a total depth of two feet, whichever is less.
- 3. Table 7-3, Note 2: First sample collected at depth interval of 5-6 feet. Second sample collected at the top of the clay layer. At till well locations (MW-2D, MW-5D, MW-7D), third sample collected at the bottom of the clay layer. Intermediate samples from within the clay layer are addressed in item (2) of Revision No. 5 to the POP dated November 11, 1987
- 4. <u>Figures 4-1 and 4-2</u>: A revised schedule for the Remedial Investigation Phase of the project is attached. This schedule supercedes the schedule in Revision No. 5 to the POP dated November 11, 1987.

Ms. Janet Feldstein November 23, 1987 Page - 2 -

5. Revision No. 5, 11/11/87: Items 1, 2 and 3 - delete MW-1D from program, along with associated samples. Perform stratigraphic sampling below the top of clay sample at MW-1S location to obtain stratum thickness.

To complete our documentation of the revisions, we request that the revisions be approved by the EPA in writing.

Very truly yours,

DAMES & MOORE

Gerard M. Coscia, P.E.

Project Manager

GMC/nam

cc: T. Morris - IBM

T. Armstrong - GE

J. McBurney - Allied


M. Reiser - Nepera

W. Warren

J. Groome - NJDEP

L. Vidulich – EPA-Edison

J. Koczan - D&M

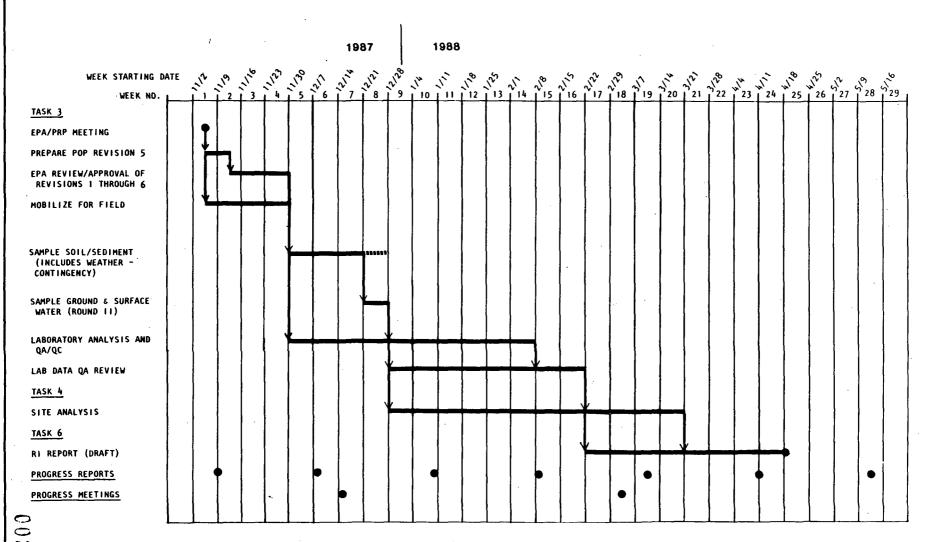

REVISED SCHEDULE
REMEDIAL INVESTIGATION RESAMPLING PROGRAM
AND ADDITIONAL SITE INVESTIGATIONS

SCP SITE CARLSTADT, NEW JERSEY BERGEN COUNTY, NEW JERSEY
