




**VOLUME I  
TABLE OF CONTENTS**

	<u>Page</u>
<b>EXECUTIVE SUMMARY</b>	
PWS 2.7.1	20
PWS 2.7.2	20
PWS 2.7.3–	
2.7.3.9	20
PWS 2.7.4–	
2.7.4.4	21
PWS 2.7.5	21a
PWS 2.7.6	21a
PWS 2.7.7	21a
PWS 2.7.7.1	21a
PWS 2.7.7.2	21
PWS 2.7.7.3	23
PWS 2.7.7.4	24
PWS 2.7.7.5	24
PWS 2.7.7.6	25
PWS 2.7.7.7	25
PWS 2.7.7.8	26
PWS 2.7.7.9	26
PWS 2.7.7.10	26
PWS 2.7.7.11	26a
PWS 2.7.7.12	27



	<u>Page</u>	
PWS 2.7.7.13	Personnel Administration and Policies.....	27
2.3	Management .....	29
2.3 a)	Organization Plan.....	29
2.3 b)	Management Plan .....	29
2.3 b)(i)	Staffing Plan.....	29
2.3 b)(ii)	Subcontract Management Plan.....	29
2.4	Method of Operation .....	30
2.4 a)	Plan to Ensure No Government Activities Interruption .....	30
2.4 b)	Contract Requirements .....	30
<hr/>		
PWS 3.	General Management and Administration (Financial) .....	30
PWS 3.1	Financial Tracking and Reporting System .....	32
PWS 3.1.1	Cost Accounting System .....	33
PWS 3.1.2	Financial Reporting System .....	33
PWS 3.2	Information Security (IS) and Information Assurance (IA) Program Management .....	36
PWS 3.3	Quality Management System (QMS) .....	42
PWS 3.4	Reports.....	43
PWS 3.5	Contractor Personnel Travel .....	43
PWS 3.6	Employee Tracking System .....	43
PWS 3.7	Security Clearances .....	43a
PWS 3.8	Passes and Badges .....	44
PWS 3.9	Safety Requirements. [CDRL A02-07 - Contractor Safety Program Records] .....	45
PWS 3.10	Computerized Maintenance Management System (CMMS) .....	48
PWS 3.11–		
3.12	IDIQ Work Schedule and Proposal Preparation .....	48
PWS 3.13	Phase-In [RFP H.22] .....	49
PWS 3.14	Phase-Out Plan [RFP H.22].....	49
PWS 3.15–		
3.15.7	Acquisition Procedures/Procurement System .....	49
PWS 3.15.1	Procurement System.....	49
PWS 3.15.2	Procurement Initiation, Control, and Documentation .....	50a
PWS 3.15.3	Mandatory Sources of Supply.....	50a
PWS 3.15.4	Bidders List and Commodities Files Maintenance .....	50a
PWS 3.15.5	Office Equipment and Furniture Maintenance .....	50a
PWS 3.15.7	Commercial Acquisition of Government Property .....	50b
PWS 3.16	Variations in Quantities Reporting .....	50b
PWS 4.0	Management and Administration Summary.....	51





Page

This image is a high-contrast, black-and-white scan of a document page. It features a large, dark rectangular area in the center, which appears to be a redacted section of text. This central area has irregular, jagged edges. Above this redacted area, there is a horizontal white band with some dark noise. Below the redacted area, there is another horizontal white band. On the far left edge of the redacted area, there is a vertical white strip containing some small, illegible text. The overall quality is grainy and suggests a low-resolution or heavily processed scan.





Page

[REDACTED]	[REDACTED]
[REDACTED]	[REDACTED]



Page

This image is a high-contrast, black-and-white scan of a document page. It features a large, solid black rectangular area that occupies most of the right side of the frame. On the far left, there is a vertical white stripe, which is likely a binding or gutter from the original document. The overall quality is grainy and pixelated, suggesting it is a low-resolution scan. There is no legible text or other graphical elements present.



Page




	Page



	Page
[REDACTED]	
PWS 3.	
Bachelor Quarters .....	57





	<u>Page</u>
PWS 3.1,	
3.1.1.1      Operations Management .....	57
PWS 3.1.1.1–	
3.1.1.3.1,	
3.1.1.6      Service Desk Operations .....	57
PWS 3.1.1.4    Abandoned Property Management.....	58
PWS 3.1.1.5,	
3.1.4          Resident Relations.....	59
PWS 3.1.2     Storage Management.....	59
PWS 3.1.3,	
3.1.3.1     Budget and Cost Estimates .....	59a
PWS 3.1.5     Unscheduled Services .....	59a
PWS 3.1.6     ENH Intranet .....	60
PWS 3.1.7     Breaches of Discipline .....	60
PWS 3.2       Furnishings, Appliances & Equipment (FA&E) Management .....	60
PWS 3.2.1     Maintenance of Equipment .....	60
PWS 3.3.      Transient Quarters Housekeeping .....	60
PWS 3.3.1,	
3.4          Exterior Cleaning.....	60
PWS 3.5       Change of Occupancy Maintenance, Repair, and Custodial Services .....	60
PWS 3.6       Grounds Maintenance.....	60
PWS 4.       IDIQ Work .....	60



PWS 1.–2.	General Information/Management and Administration of Fire and Emergency Services .....	66
PWS 3.	Fire and Emergency Services Procedures .....	68
PWS 3.1	General Requirements .....	68
PWS 3.1.1	Standard Operating Procedures (SOP) .....	68
PWS 3.1.1.1	Emergency Medical Service (EMS) Standard Procedures .....	68
PWS 3.1.2	Communications Center .....	68
PWS 3.1.3	Contractor-Furnished Equipment (CFE) Maintenance, Repair, and Replacement.....	69
PWS 3.1.4	Communication Records and Reports .....	69
PWS 3.2	Emergency Medical Services (EMS) .....	69



	<u>Page</u>	
PWS 3.2.1	EMS Response .....	70
PWS 3.2.2	Patient Stabilization and Care.....	70
PWS 3.2.3	Transport Services.....	70
PWS 3.2.4	Medical Rehabilitation Services.....	70
PWS 3.3	Fire Protection Services.....	70
PWS 3.3.1	Hazardous Materials (HM) Response.....	70
PWS 3.3.1.1	Weapons of Mass Destruction (WMD) and Chemical, Biological, Radiological, Nuclear, High Yield Explosives (CBRNE) Response.....	71
PWS 3.3.2	Rescue Services .....	71
PWS 3.3.2.1	Confined Space Rescue .....	71
PWS 3.3.2.2	Water Rescue .....	71
PWS 3.3.2.3	Vehicle Rescue .....	71
PWS 3.3.3	Fire Suppression Response.....	71
PWS 3.3.3.1	Structural Fire Suppression Response .....	72
PWS 3.3.3.2	Wildland Fire Suppression Response.....	72
PWS 3.3.3.3	Shipboard Fire Suppression Services.....	72
PWS 3.3.3.4	Aircraft Fire Suppression Services.....	72
PWS 3.3.4	Mutual Aid and Off-base Responses .....	72
PWS 3.3.4.1	Mutual Aid .....	72
PWS 3.3.4.2	Off-Base Responses .....	73
PWS 3.4	Fire Prevention Services.....	73
PWS 3.4.1	Code Enforcement .....	73
PWS 3.4.2,		
3.4.3, 3.4.3.1	Fire Prevention Inspections .....	73
PWS 3.4.5	Public Education .....	73
PWS 3.4.6	Fire Safety and Education.....	73
PWS 3.4.7	Fire Investigation.....	73
PWS 3.5	Other Support.....	74
PWS 3.5.1	Public Works Department (PWD) Support.....	74
PWS 3.5.2	Employee Recall System .....	74
PWS 3.5.3	Emergency Standby for Hazardous Operations .....	74
PWS 3.5.4	Classified Material Destruction .....	74
PWS 3.5.5	Key Control Activities .....	74
PWS 4.	IDIQ Work .....	74
PWS 4.1	Surge.....	74a





	Page	
[REDACTED]		
PWS 3.	Custodial Service Procedures.....	80
PWS 3.1	Scheduled Services .....	80
PWS 3.1.1	Room/Space Cleaning .....	80
PWS 3.1.2-		
3.1.2.8	Floor Care .....	81
PWS 3.1.3-		
3.1.3.2	Restroom Service.....	81
PWS 3.1.4-		
3.1.4.2	Perimeter Services.....	82
PWS 3.2	Unscheduled Work.....	82
PWS 3.3	Tables Update.....	82
PWS 4.-4.1	IDIQ and Surge Custodial Services .....	82
[REDACTED]		
[REDACTED]		
[REDACTED]		
PWS 2.2.3	Utility Manager .....	88
PWS 2.4	Work Coordination .....	88
PWS 3.	Electrical Utility Systems.....	88
PWS 3.1	Electrical Power Generation Plants .....	89
PWS 3.1.1	Plant Controls and Monitoring System.....	91
PWS 3.1.2	Range Operations .....	91
PWS 3.1.3	Various Support .....	91
PWS 3.1.4	Operating Records and Logs—Diesel/Gas.....	91
PWS 3.1.4.1	Engine-Generator Logs.....	91
PWS 3.1.4.2	Power Plant Logs .....	91
PWS 3.1.5	Fuel Oil Receiving .....	91
PWS 3.2	Operation—Auxiliary Engine-Generators .....	92
PWS 3.2.1	Test-Run .....	92
PWS 3.2.2	Operations Plan .....	92
PWS 3.2.3	Launching Operations .....	92
PWS 3.2.4	Operating Records and Logs—Auxiliary Engine-Generators.....	92
PWS 3.3	Electrical Power Distribution Systems .....	92
PWS 3.3.1	Medium Voltage Systems .....	93



	<u>Page</u>	
PWS 3.3.2	Low-Voltage Systems .....	93
PWS 3.3.2.1	Exterior Systems Operation .....	93
PWS 3.3.2.2	Interior Systems .....	93
PWS 3.3.2.3	Lightning Protection/Grounding Systems.....	93
PWS 3.3.2.4	DC Power Systems .....	93
PWS 3.3.2.5	Cathodic Protection Systems.....	93
PWS 3.3.2.6	Special Frequency Systems .....	93
PWS 3.3.2.7	Uninterruptible Power Supplies (UPS).....	93
PWS 3.3.2.8	Exterior Lighting Systems .....	93
PWS 3.3.2.9	Airfield Lighting Systems.....	94
PWS 3.3.3	Critical Failures .....	94
PWS 3.3.4	Range Operations Support .....	94
PWS 3.3.5	Various Support .....	94
PWS 3.4	Maintenance.....	94
PWS 3.4.1	Power Plant Maintenance .....	95
PWS 3.4.1.1	Power Plant Electrical Equipment Service and Calibration .....	95
PWS 3.4.2	Auxiliary Engine and Engine Generator Maintenance and Repair .....	96
PWS 3.4.3	Medium-Voltage Systems .....	96
PWS 3.4.4	Low-Voltage Systems .....	96
PWS 3.4.4.1	Exterior Systems .....	96
PWS 3.4.4.2	Interior Systems .....	96
PWS 3.4.4.3	Lightning Protection/Grounding Systems.....	96
PWS 3.4.4.4	DC Power Supplies and Distribution Systems.....	96
PWS 3.4.4.5	Cathodic Protection Systems.....	96
PWS 3.4.4.6	Special Frequency Systems .....	97
PWS 3.4.4.7	Uninterruptible Power Supplies (UPS).....	97
PWS 3.4.4.8	Exterior Lighting Systems .....	97
PWS 3.4.4.9	Airfield Lighting Systems.....	97
PWS 3.4.5	Spare Parts .....	97
PWS 3.4.6	Records and Logs .....	97
PWS 3.4.6.1	Warranty/Guarantee Certificates .....	97
PWS 3.4.6.2	Major Equipment Maintenance History.....	97
PWS 3.4.6.3	Outage Logs.....	98
PWS 3.4.6.4	Leak Detection Records.....	98
PWS 3.4.6.5-		
3.4.6.5.4	Maps, Drawings, and Tables .....	98
PWS 3.5	Energy Conservation.....	98
PWS 3.5.1	Energy Consumption Violations.....	99
PWS 3.5.2	Energy Consumption Approvals .....	99
PWS 3.6	Reports.....	99
PWS 4.	IDIQ Work .....	99



Page

PWS 2.8	Safety .....	106
PWS 3.	Grounds Maintenance Procedures .....	106
PWS 3.1	Maintenance of Improved Grounds.....	106
PWS 3.2	Semi-Improved Grounds Maintenance .....	109
PWS 3.3	Unimproved Grounds Maintenance .....	109a
PWS 3.4	Special Vegetation Control Areas.....	109a
PWS 3.5	Street Sweeping.....	109b
PWS 4.	IDIQ Work .....	109b

PWS 1.-2.	General Information/Management and Administration of Compressed Air .....	115
PWS 3.	Compressed Air Services .....	115
PWS 3.1	Compressed Air System Operation .....	115
PWS 3.1.1	Operating Records, Logs, and Reports .....	115
PWS 3.2	Integrated Maintenance Program (IMP).....	115
PWS 3.2.1	Preventive Maintenance (PM).....	116
PWS 3.2.2	Repairs .....	116
PWS 4.	IDIQ/Surge Work.....	116



	Page	
PWS 1.-2.	General Information/Management and Administration of Wastewater and Treatment System.....	122
PWS 3.	Wastewater Collection and Treatment System Operation.....	122
PWS 3.1	Wastewater Effluent Quality.....	122
PWS 3.2	Integrated Maintenance Plan (IMP) .....	122
PWS 3.2.1	Modular Plant Maintenance—Grease Control.....	123
PWS 3.2.2	Modular Plant Maintenance—Floatables Control.....	123
PWS 3.2.3	Modular Plant Maintenance—Determination of Sludge Buildup .....	123
PWS 3.2.4	Lagoon Grounds Maintenance.....	123
PWS 3.2.5	Service Calls .....	123
PWS 4.	IDIQ Work .....	123
 <u>Figures</u>		
PWS 1.-2.	General Information/Management and Administration of Water .....	129
PWS 3.	Potable Water Production and Distribution .....	129
PWS 3.1	Operation of Water Treatment Facilities and Distribution Systems .....	129
PWS 3.1.1-	3.1.1.4 Water Quality .....	129
PWS 3.1.2	Operating Logs, Reports, and Procedures .....	130
PWS 3.1.3	Contingencies for Drought Conditions .....	130
PWS 3.1.4	Emergency Measures .....	130
PWS 3.1.5	Water Conservation .....	130
PWS 3.2	Integrated Maintenance Program (IMP).....	130
PWS 3.2.1	Preventive Maintenance (PM) and Inspection .....	131
PWS 3.2.2	Inspections .....	131
PWS 3.2.3	Critical Maintenance and Repair.....	131



	<u>Page</u>
PWS 3.2.4 Daily Inspections and Adjustments .....	131
PWS 3.2.5 Service Calls .....	132
PWS 4. IDIQ Work .....	132

[REDACTED]

[REDACTED]

[REDACTED]

[REDACTED]

PWS 1.-2. General Information/Management and Administration of Solid Waste.....	137
PWS 3. Solid Waste Management Program .....	137
PWS 3.1 Solid Waste Collection .....	137
PWS 3.1.1-3.1.4 Residential Collection Services.....	137
PWS 3.1.2-3.1.5 Non-Residential Collection Services.....	137
PWS 3.2-3.2.2 Solid Waste Disposal .....	138
PWS 3.3 Sanitation .....	138
PWS 3.4-3.4.4 Solid Waste Containers .....	138
PWS 4.-4.1 IDIQ and Surge Work.....	138

[REDACTED]

[REDACTED]

[REDACTED]

[REDACTED]



	<u>Page</u>	
PWS 3.	Base Support Vehicles and Equipment (BSVE) .....	144
PWS 3.1	Operations.....	144
PWS 3.1.1	Intermittent Bus Services .....	144
PWS 3.1.2	WHE/MHE/CESE Services .....	145
PWS 3.1.2.1	Heavy Trucking Service .....	145
PWS 3.1.2.2	MHE and Crane Service .....	145
PWS 3.1.2.3	Construction Equipment Service.....	145
PWS 3.2	Support Services.....	145
PWS 3.2.1	Operator Testing and Licensing.....	145
PWS 3.2.2,		
3.2.2.1	Dispatching Service .....	146
PWS 3.2.3	Government Operated Vehicle Pool .....	147
PWS 3.2.4	Emergency Road Service .....	147
PWS 3.2.5	Tow Truck Service Calls .....	147
PWS 3.2.6	Non-Government Owned Leased Vehicles .....	147
PWS 3.2.6.1	GSA Leased Vehicles .....	147a
PWS 3.3,		
3.3.1	Maintenance.....	148
PWS 3.3.1.1	Inspection and Test Schedule.....	149
PWS 3.3.1.2,		
3.3.1.3	Preventive Maintenance (PM) Inspections .....	149
PWS 3.3.1.3.1	Battery Maintenance .....	149
PWS 3.3.1.3.2	Tire Maintenance .....	149
PWS 3.3.1.4	BSVE Repair .....	149
PWS 3.3.1.4.1	SROs.....	149
PWS 3.3.1.4.2	Repainting .....	150
PWS 3.3.1.4.3	Glass Replacement.....	150
PWS 3.3.1.4.4	Upholstery .....	150
PWS 3.3.1.5	BSVE Service Calls.....	150
PWS 3.3.1.5.1	Interim/Breakdown Inspections and Repairs .....	151
PWS 3.3.1.5.2	Maintenance and Repair of Government Utilized CESE, WHE, and MHE .....	151
PWS 3.3.1.5.3	Emergency Work.....	151
PWS 3.3.1.5.4	Ground Support Equipment (GSE) Sandblasting and Painting .....	151
PWS 3.3.1.6	Warranties and Recalls (3.3.1.6.1) .....	151
PWS 3.3.1.7,		
3.3.1.7.1	General Maintenance and Repair of Other Equipment Operated by Contractor.....	152
PWS 3.3.1.8,		
3.3.1.8.1	Inspection and Load Test Certification of WHE and MHE .....	152
PWS 3.3.1.8.2	Battery Recharging .....	152
PWS 3.3.1.8.3	Rigging Material Procurement and Maintenance.....	152
PWS 3.3.1.9	New and Reassigned Use Vehicle Service .....	152
PWS 3.3.2	Maintenance (Non-Government-Owned).....	153
PWS 3.4, 3.4.1	Records Management.....	153
PWS 3.4.2	Down Equipment List .....	153
PWS 3.4.3	Contingency Plans .....	153
PWS 3.5	Replacement Equipment (Contractor-Furnished Equipment).....	153
PWS 3.6	Equipment Disposition .....	154
PWS 4.	IDIQ Work .....	154
PWS 4.1	Surge.....	154



	Page
PWS 3.	Airfield Facilities ..... 160
PWS 3.1	ATC Services ..... 160
PWS 3.2	Aviation Safety Programs ..... 161
PWS 3.2.1	Bird Air Strike Hazard (BASH) ..... 161
PWS 3.2.2	Foreign Object Debris (FOD) ..... 162
PWS 3.3	Airfield Equipment and Operation Maintenance ..... 162
PWS 3.3.1	Arresting Gear Operations and Maintenance ..... 163
PWS 3.3.1.1	E-28 Aircraft Arresting Gear Operations ..... 163
PWS 3.3.1.2	Arresting Gear Maintenance and Repair ..... 163
PWS 3.3.1.3	Arresting Gear Report (CDRL A13-04) ..... 163a
PWS 3.3.2	Optical Landing Systems (OLS) O&M ..... 164
PWS 3.3.2.1	FOLDS Operations ..... 164
PWS 3.3.2.2	FOLDS Maintenance ..... 164
PWS 3.3.3	Airfield Lighting Maintenance ..... 164
PWS 3.3.4	Preventive Maintenance (PM) ..... 165
PWS 3.3.5	Corrective Maintenance (CM) ..... 165
PWS 4.	IDIQ Work ..... 165
PWS 4.1	Surge Operations ..... 165



Page

	Page	
PWS 2.5	Records and Reports .....	172
PWS 2.6	Historical Preservation .....	172
PWS 3.	Buildings and Structures Maintenance and Repair.....	173
PWS 3.1	Service Calls .....	173
PWS 3.1.1	Emergency Service Calls .....	174
PWS 3.1.2	Routine Service Calls.....	174
PWS 3.2	Preventive Maintenance Inspection (PMI) Program and the Integrated Maintenance Plan (IMP) .....	174
PWS 3.2.1	Critical HVAC and Refrigeration Systems.....	175
PWS 3.2.2	Critical PMI of Petroleum, Oil, and Lubricants (POL) Lines and Equipment .....	176
PWS 3.2.3	Fire Protection.....	176
PWS 3.3	Corrosion Control .....	176
PWS 3.3.1	Building Exterior Annual Painting.....	176
PWS 3.3.2	Building Interior Annual Painting.....	176
PWS 3.3.3	Building Foamed Roof Top Coating.....	176
PWS 3.3.4	Metal Building Washing of Exterior and Roofs .....	177
PWS 3.3.5	POL Lines and Equipment .....	177
PWS 3.3.6	Tower, Antenna Support, Antennas, Vans, Launchers, Trailers .....	177
PWS 3.3.7	Aerial Targets Corrosion Control .....	177
PWS 3.3.8	Ordnance Corrosion Control .....	177
PWS 3.3.9	Range and Information Plans and Programs Office (IPPO) Assets Corrosion Control.....	177
PWS 3.4	Preventive Maintenance (PM) Program.....	177
PWS 3.4.1	Non-Critical HVAC and Refrigeration Systems PM .....	178
PWS 3.4.2	Food Service Equipment PM .....	178
PWS 3.5	Corrective Maintenance & Repair (CM&R) .....	178
PWS 3.5.1	Non-installed Equipment CM&R .....	179
PWS 3.5.2	Installed Equipment CM&R .....	179
PWS 3.5.3	Swimming Pool CM&R.....	179
PWS 3.5.4	Eyewash Station .....	179
PWS 3.5.5	Fire Protection Systems & Equipment CM&R .....	179
PWS 3.5.6	Ground Structures .....	179
PWS 3.6	Inspection, Testing, and Certification.....	180
PWS 3.6.1	Boilers and Unfired Pressure Vessels (UPV) .....	180
PWS 3.7	Other Recurring Services.....	180
PWS 4.	IDIQ Work .....	181



	<b>Page</b>
<b>FACTOR A, ANNEX 15—RANGE COMMUNICATIONS SYSTEMS</b>	
PWS 3.	Range Communications Systems.....
PWS 3.1.1	Range Communication O&M .....
PWS 3.1.2	Network O&M.....
PWS 3.1.2.1	Network Information Assurance (IA) Compliance .....
PWS 3.1.2.2	Network Scanning .....
PWS 3.1.2.3	DREN Support .....
PWS 3.2.1	Standard Operating Procedures (SOP) .....
PWS 3.2.2	Preventive Maintenance (PM).....
PWS 3.2.3	Corrective Maintenance (CM) .....
PWS 3.2.4	Corrosion Control (CC) .....
PWS 3.2.5	Quality Inspections.....
PWS 3.2.6	Equipment Inventory .....
PWS 3.2.7	Emergency Repairs.....
PWS 3.3.1	Configuration Control .....
PWS 3.3.1.1	Facility Cable Plant Configuration Control .....
PWS 3.3.1.2	RF Interference Control .....
PWS 3.3.1.3	Systems Documentation .....
PWS 3.4	Work Control .....
PWS 3.4.1	Scheduled Outages.....
PWS 3.4.2	Unscheduled Outages and Repairs .....
PWS 3.4.3-	
3.4.4	NSR and CSR .....
PWS 3.4.5	Technical Directive Work Requests (TDWR).....
PWS 3.5.1	Project Planning Support .....
PWS 3.5.2	Mission Communications Planning .....
PWS 3.5.3	Network Testing .....
PWS 3.5.4	UDS Requirements Review .....
PWS 3.5.5	Cost Estimating .....
PWS 3.5.6	Power Outage Support .....
PWS 3.6	Network Engineering.....
PWS 3.6.1	Network Engineering Support .....
PWS 3.6.2	Information Assurance (IA) Network Support .....
PWS 3.7	Systems Integration Installation Support .....
PWS 3.8	Information Security (INFOSEC) and Information Assurance (IA) Program Management .....
PWS 3.9	Naval Messaging System .....
PWS 3.9.1	Messaging System Equipment .....
PWS 3.9.2	Messaging Operational Coordination/Liaison .....
PWS 3.10.1	COMSEC Accountability and Inventory .....
PWS 3.10.2	COMSEC Range Operations Support .....
PWS 3.10.3	Crypto Maintenance .....
PWS 3.10.4	CMS Security Violations .....





	<u>Page</u>
PWS 4.	IDIQ Work .....
PWS 4.1	Surge.....
PWS 4.2	Systems Integration Installation Support .....
PWS 4.3	Reimbursable Mission Support Installations.....
	203
	203
	203
	204



PWS 3.	Data Systems.....	212
PWS 3.1.1	RDPG Operations .....	213
PWS 3.1.2	RDPG Maintenance .....	214
PWS 3.1.3	Quality Assurance (QA) .....	214
PWS 3.1.4	Data Handling .....	215
PWS 3.1.5	Data Retention .....	215
PWS 3.1.6	Data Handbook .....	215
PWS 3.1.7	Database of all Data Items Delivered .....	215
PWS 3.1.8	Data Request Summary.....	215
PWS 3.1.9	Data Transmittal.....	215
PWS 3.2.1	RTCC Operations.....	216
PWS 3.2.2,		
3.4.2, 3.6.2,		
3.7.2	RTCC, ROCC, DAC, TOSR, and BMIC Maintenance .....	216
PWS 3.3.1	ROCC Operations .....	216
PWS 3.4.1	DAC Operations .....	217
PWS 3.5	Media Center.....	217
PWS 3.6.1	TOSR Operations.....	217
PWS 3.7.1	BMIC Operations.....	217
PWS 3.7.2	BMIC Maintenance.....	218
PWS 3.8,		
3.8.1	NTDS/RNUS and JTIDS .....	218
PWS 4.-4.2	IDIQ Work .....	218



Page



PWS 3.	Environmental .....	226
PWS 3.1,		
3.1.2	Sampling, Field Testing, and Laboratory Services (CDRL A17-06) .....	226
PWS 3.1.1	Sampling (CDRL A17-05) .....	226
PWS 3.1.3	Laboratory Services .....	227
PWS 3.2–3.2.2	Used Oil Management Services (CDRLs A17-08, A17-09) .....	227
PWS 3.2.1	Used Oil Collection.....	227
PWS 3.2.1.1	Used Oil Pick-up and Transport.....	229
PWS 3.2.1.2	Used Oil Recovery, Collection, Storage, Recycling, or Disposal.....	230
PWS 3.2.1.3	Used Oil/Processor Annual Report.....	230b
PWS 3.2.1.4	Used Oil Biennial Report.....	230b
PWS 3.2.2	Used Oil Recycling and Disposal.....	230c
PWS 3.3	HM/HW Management.....	230d
PWS 3.3.1	HM/HW Accumulation Sites and Storage Facilities Operations .....	230d
PWS 3.3.1.1	Accumulation Sites.....	230e
PWS 3.3.1.2,		
3.3.2	HW Storage.....	230f
PWS 3.3.1.3	Proper Container with Correct Labeling.....	230f
PWS 3.3.3	Transportation of HM/HW .....	230f
PWS 3.3.3.1	HW Transfer Document (CDRL A17-10) .....	230g
PWS 3.3.4–		
3.3.4.1	HW Disposal .....	230g
PWS 3.3.4.1	Annual HW Report, P2ADS (CDRL A17-11) .....	230h
PWS 3.3.4.2	Monthly HW Report (CDRL A17-12) .....	230i
PWS 3.3.4.3	Disposal of HW (CDRL A17-13) .....	230i
PWS 3.4	Oil and Hazardous Substance Spill Response and Cleanup Ashore and Offshore .....	230j
PWS 3.4.1,		
3.4.3.1	Oil and Hazardous Substance Spill Containment.....	230j
PWS 3.4.2	Oil and Hazardous Substance Spill Cleanup and Disposal .....	230j




	<u>Page</u>
PWS 3.4.3	Oil and Hazardous Substance Spill Reporting and Documentation ..... 230k
PWS 3.4.3.1	Spill Response Team (CDRL A17-15) ..... 230k
PWS 3.4.3.3	Government Approved OHS Spill Training Program ..... 230l
PWS 3.5	HW, Universal Waste, and Used Oil Management Plan (CDRL A17-16)..... 230m
PWS 3.6	Periodic Inspections of HW and Used Oil at Points of Generation..... 230m
PWS 3.7	Sampling and Analysis of Unknown Wastes ..... 230m
PWS 3.8	Maintain, Repair, Monitor and Diagnose Alarms of Underground Storage Tanks (UST) Leak Detection Systems (LDS) ..... 230n
PWS 3.9	CFCs/Halons (CDRL A17-17)..... 230n
PWS 3.10	Sand Blast Pit..... 230n
PWS 3.11	Chemical Inventory List (CDRL A17-18)..... 230n
PWS 4.	IDIQ Work ..... 230n
PWS 4.1	Surge..... 230n



PWS 3.1	Facility Engineering..... 239
PWS 3.1.1	Excavation Permit Preparation ..... 240
PWS 3.1.2	TDWR Engineering ..... 240
PWS 3.1.3	Facility Engineering Studies..... 241
PWS 3.1.4	Facility Project Design..... 241
PWS 3.1.5	Construction Control Support..... 241
PWS 3.1.6	New Facilities Contract Change Support..... 241a
PWS 3.2	Systems Engineering ..... 241a
PWS 3.2.1	Improvement and Modernization Planning ..... 242
PWS 3.2.2	Engineering Analysis..... 242
PWS 3.2.3	Modification Support ..... 243
PWS 3.2.4	Installation Support ..... 243
PWS 3.2.5	O&M Procedures..... 244
PWS 3.2.6	Preventive Maintenance (PM) Procedures ..... 244
PWS 3.2.7	Corrective Maintenance (CM) ..... 245
PWS 3.2.8	Computer System Administration (CSA)..... 245
PWS 3.2.9	Database Application Support ..... 245
PWS 3.2.10	Depot-Level Maintenance (DLM) ..... 245
PSW 3.2.11	Systems Corrosion Control (CC) ..... 246



	<u>Page</u>
PWS 3.2.12	Depot Level Repairable for Instrumentation Radar Support Program (IRSP) ..... 246
PWS 3.2.13	Equipment Records..... 246
PWS 3.2.14	Configuration Management..... 246
PWS 3.2.15	Configuration Control ..... 247
PWS 3.2.16	Task Accounting..... 247
PWS 3.3	Test Equipment Calibration..... 248
PWS 3.3.1	MEASURE Program..... 249
PWS 3.3.2	Loan Pool ..... 249
PWS 3.3.3	On-Site Calibration..... 249
PWS 3.3.4	Pickup and Delivery ..... 249
PWS 3.4	Work Control ..... 249a
PWS 3.4.1	Work Status..... 250
PWS 3.4.2	Service Call Desk..... 251
PWS 3.5	Drafting and Documentation ..... 251
PWS 3.5.1	Facilities Record Drawings ..... 251a
PWS 3.5.2	Systems Drawing ..... 252
PWS 3.5.3	Reproduction Services..... 252
PWS 3.5.4	Technical Library ..... 252
PWS 4.	IDIQ Work ..... 252
PWS 4.1	Surge..... 252
PWS 4.2	Archaeological Surveys ..... 253
PWS 4.3	Topographic/Geodetic Land Surveying..... 253
PWS 4.4	Range Tasking ..... 253



PWS 3.-3.3	Food Service ..... 259
PWS 3.4	Meal Schedule ..... 259
PWS 3.5	Meal Services..... 259




	Page	
PWS 3.5.1	Food Stock Levels.....	260
PWS 3.5.2	Table Service .....	260
PWS 3.5.3–		
3.5.5	Cashiering Service .....	261
PWS 3.6	Quality and Quantity of Food .....	261
PWS 3.7–3.7.8	Food Serving.....	261
PWS 3.8–3.8.6	Self Service .....	262
PWS 3.8.7	Waste Control and Salvage .....	262
PWS 3.9–		
3.9.10.15	Sanitation Requirements.....	262
PWS 3.10–		
3.10.2	Dishwashing Service.....	264
PWS 3.11–		
3.11.15	Equipment Cleaning Service.....	264
PWS 3.12–		
3.12.2	Trash and Garbage .....	265
PWS 3.13	Storerooms.....	265
PWS 3.14	Sidewalks .....	265
PWS 3.15	Restrooms .....	265
PWS 3.16	Equipment Restrictions .....	265
PWS 3.17	Employee Lockers.....	265
PWS 3.18	Insect, Birds, and Rodent Control .....	265
PWS 3.19–		
3.19.11	Personnel Health and Cleanliness.....	265
PWS 3.20–		
3.20.5	Maintenance.....	265a
PWS 3.21–		
3.21.7	Additional Services.....	265b
PWS 4.	IDIQ Work .....	265b
PWS 4.1	Surge.....	265b

PWS 3.	Aircraft Refueling and Fuel Management .....	271
PWS 3.1–3.1.5	Common Procedures .....	271

	<u>Page</u>
PWS 3.2–3.2.4 POL Facility Storage .....	272
PWS 3.3–3.6 POL Product Operations .....	272
PWS 3.3.7 Blend FSII into the Fuel .....	273
PWS 3.4– 3.4.4 Fuel Receipt and Issue .....	273
PWS 3.5– 3.5.8 Aircraft Refueling/Defueling .....	274
PWS 3.6– 3.6.6 Fuel Accounting/Inventory Control.....	275



	<u>Page</u>	
PWS 3.6.7	Aviation Fuel Turn-in for Credit.....	276
PWS 3.6.8	Other Product Turn-in for Credit (Defuel) .....	277
PWS 3.7	Non-Aircraft Refueling.....	277
PWS 3.8	Preventive Maintenance (PM) Program.....	277
PWS 3.9–3.9.5	Petroleum Laboratory.....	281
PWS 3.10–		
3.10.4	Operations of Base Gas Station .....	281
PWS 3.10.5–		
3.10.7	Ground Fuel Alternate Issues, Method, and Manning .....	282
PWS 3.10.8	Automated System Chips/Keys Maintenance.....	282
PWS 3.11	General Precautions .....	283
PWS 3.12	Contractor Quality Control Program/Plan .....	285
PWS 3.13–		
3.13.2	Reporting and Disposing of Waste Fuel .....	285
PWS 3.14–		
3.14.5	Documentation Preparation .....	285
PWS 3.15–		
3.15.5	Records, Files, and Reports .....	286
PWS 3.16	Procedures/Instructions .....	286
PWS 3.17–		
3.17.3	Environmental Compliance .....	286
PWS 3.18	Naval Reserve Training .....	286
PWS 3.19	Inspection, Surveys, and Audits.....	287
PWS 3.20	Copy of the Contract .....	287
PWS 3.21	Contract Turnover .....	287
PWS 3.22	Fire Protection Compliance.....	287
PWS 3.23	Fire/Emergency Drills.....	287
PWS 3.24	Energy Conservation Participation.....	287
PWS 3.25	Destructive Weather Preparedness Plan.....	287
PWS 3.26	Spare Parts and Equipment.....	287
PWS 3.27–		
3.27.6	PMRF Specific Training and Plans .....	287
PWS 3.28	Non-Aviation Fuel Support.....	288
PWS 3.29	Product Trucks and Administrative Vehicles Listed.....	288
PWS 4.	IDIQ.....	288
PWS 4.1	Surge.....	288





	Page
[REDACTED]	
PWS 3.	Base Communications ..... 293a
PWS 3.1, 3.2	Configuration Control ..... 294
PWS 3.1.3	PBX Configuration Control ..... 294
PWS 3.1.4	PMRF Telephone Directory ..... 294
PWS 3.2,	
3.2.1	Planning—Cost Estimating and Installation ..... 294
PWS 3.2.2	PMRF Excavation Permit Support ..... 294
PWS 3.2.3	Power Outage ..... 295
PWS 3.2.4,	
3.3.7	PDS Support and Installations ..... 295
PWS 3.3, 3.3.1	Maintenance and O&M Installation ..... 295
PWS 3.3.2	PBX and Telephone Support Services ..... 295
PWS 3.3.3–	
3.3.5	Alarm Systems O&M and Testing ..... 295
PWS 3.3.6	Video Teleconferencing (VTC) System Maintenance ..... 296
PWS 3.3.7	Protected Distribution System ..... 297
PWS 3.3.8	Civil Defense Warning Systems ..... 297
PWS 3.3.9	Cable Plant O&M ..... 297
PWS 3.3.10	Aerial Cable Plant O&M PUC-Provider Subcontract ..... 297
PWS 3.3.11	Battery Maintenance O&M ..... 297
PWS 3.3.12	Security Dispatch Center Maintenance ..... 297
PWS 3.4, 3.4.1	Logistics/DISA Telecommunications Request ..... 298
PWS 3.5, 3.5.3	Work Control and TSR/TDWR ..... 298
PWS 3.5.1,	
3.5.2	Outages—Scheduled and Unscheduled ..... 298
PWS 3.5.3	Telecommunications Service Request ..... 299
PWS 3.6–3.6.4	Customer Support ..... 299
PWS 3.7–3.7.5	Cost Control and Account Billing ..... 300
PWS 3.7.6	System Integration Installation Support ..... 300
PWS 4.	IDIQ Work ..... 300
PWS 4.1	Surge ..... 300a



	Page	
[REDACTED]		
[REDACTED]		
PWS 3.	Launch Ordnance Systems.....	307
PWS 3.1	Launch Operations.....	307
PWS 3.1.1	Launch Systems Maintenance, Operation, and Testing.....	307
PWS 3.1.2	Launch Pad Auxiliary Systems Maintenance, Operation, and Testing.....	307a
PWS 3.2	Torpedo Post-Op Maintenance.....	307a
PWS 3.2.1	MK 46 and MK 48 Post-Operational Flushing Facility Operations and Maintenance.....	308
PWS 3.3	HM or Waste Operations (3.3.1-3.3.3).....	308
PWS 3.4	Recovery Systems .....	308
PWS 3.5	Storage Facilities.....	308
PWS 3.5.1	Ordnance Facility Management.....	309
PWS 3.6, 3.6.1	Delivery of Ordnance .....	309
PWS 3.7–3.7.7	Ammunition and Ordnance Management .....	309
PWS 3.8	Missile Ordnance Systems .....	310
PWS 3.8.1	AQM 37 Missile Target System .....	310
PWS 3.8.2	Missile Targets .....	310
PWS 3.8.3	Missile Target Configuration Buildup for ARAV .....	310
PWS 3.8.4	Support for THAAD .....	310
PWS 3.9	Missile Accident Emergency .....	310a
PWS 3.10	Area Clearance .....	310a
PWS 3.11	Aircraft Offload .....	310a
PWS 3.12	Material Control.....	310a
PWS 3.12.1	Material Control Quality Assurance Program .....	311
PWS 3.13	Standard Operating Procedures (SOP) .....	311
PWS 3.13.1	Preventive Maintenance (PM) and Corrosion Control (CC) .....	311
PWS 3.13.2	Systems/Equipment Maintenance SOP.....	311
PWS 3.14–		
3.14.2	RF Transmitter Requirement .....	311
PWS 3.15	Other Maintenance Requirements (3.15.1–3.15.2) .....	311
PWS 3.15.3	New Launch Systems .....	312
PWS 3.15.4	Aircraft Maintenance Support .....	312
PWS 3.15.5	Lightning Detector Maintenance and Repair .....	312
PWS 3.15.6	Periodic and Scheduled Grounding Tests Inspections .....	312
PWS 3.15.7	Testing, Inspection, Maintenance, and Repair of Torpedo Facilities .....	312
PWS 3.15.8	Ground and Air Launching and Missile Systems Maintenance .....	312
PWS 3.15.9	AQM 37 Series Missile Target System Log Books .....	312
PWS 3.16–		
3.16.2	Training .....	312
PWS 3.17–		
3.17.4	Contractor Safety Performance .....	313
PWS 3.18,		
3.18.1	Security .....	313
PWS 3.18.2	Department of Navy Explosive Safety practices and Ammunition Management .....	313
PWS 3.19	Inter-Functional Coordination.....	313
PWS 4.	IDIQ Work .....	313
PWS 4.1	Surge.....	313



PWS 3.	Measurement Systems .....	319
PWS 3.1–3.1.2	Operations and Maintenance .....	321
PWS 3.2	Underwater Tracking System (UTS) .....	321
PWS 3.2.1– 3.2.2	BARSTUR & BSURE .....	321
PWS 3.2.3– 3.2.3.10	UTS Processing Equipment .....	322
PWS 3.2.4– 3.2.4.6	Naval Gunfire Scoring System (NGSS) .....	322
PWS 3.2.5– 3.2.5.4	Portable Underwater Tracking Range (PUTR) .....	323
PWS 3.3, 3.3.6	Precision Tracking Radar O&M .....	323
PWS 3.3.1	Verification that Tracking Radars are Operational .....	324
PWS 3.3.2, 3.3.3, 3.3.12	Operate the Radar Console .....	325
PWS 3.3.4, 3.3.5	Satellite and Solar Calibrations .....	325
PWS 3.3.7– 3.3.10	COSIP / ROSA / XDAS Mission Planning and Upgrades .....	325
PWS 3.3.11	Pre- and Post-Operational Calibrations .....	325a
PWS 3.3.13	Radar Data Reduction and Analysis .....	325b
PWS 3.3.14	Doppler Receive Station .....	325b
PWS 3.4–3.4.2	Surveillance Radar Systems .....	325b
PWS 3.5–3.5.2	Data Fusion/SPECTRE .....	326
PWS 3.6– 3.6.1.11	GPS Tracking Systems - LATR .....	326
PWS 3.6.2– 3.6.2.7	GPS Tracking Systems - NCTS .....	327
PWS 3.6.3– 3.6.3.4	C-Band Radar Beacons .....	328
PWS 3.6.3.5	Intuitcom GPS .....	328




	<u>Page</u>
PWS 3.7–	
3.7.1.4,	
3.7.1.8,	
3.7.1.11 Telemetry Systems .....	328
PWS 3.7.1.5,	
3.7.1.6,	
3.7.1.10 Telemetry Coordinator Requirement.....	329
PWS 3.7.1.7 Software Development.....	330
PWS 3.7.1.8 Range Safety Display Operation.....	330
PWS 3.7.1.9 COMSEC Keys .....	330
PWS 3.7.1.10 Operation Support Plan .....	330
PWS 3.7.1.11 Network Support .....	330
PWS 3.7.1.12,	
3.7.1.13 Post-Mission Calibration, Data Product Quality, and Quick Look Reports .....	330
PWS 3.7.1.14,	
3.7.1.15 Telemetry Activity Report and Mission Support Detail CDRL.....	331
PWS 3.7.2–	
3.7.2.5 Maintenance Support.....	331
PWS 3.7.2.6,	
3.7.3 Test Equipment Utilization and Non-Mission Support .....	331a
PWS 3.7.4 Engineering Support .....	331a
PWS 3.7.5–	
3.7.5.2 TM work storage and Configuration Integrity .....	331a
PWS 3.8	
PWS 3.8.1–	
3.8.1.7 Target Control System - SNTC .....	331a
PWS 3.8.2–	
3.8.2.3 Target Control System – Portable Command Control Unit (PCCU) .....	332
PWS 4.	
PWS 4.1 Off-Site GPS Operational Support.....	332
PWS 4.2 SIS Software Development/Upgrade.....	332






	<u>Page</u>	
PWS 1.-2.	General Information/Management and Administration of Pest Control .....	338
PWS 3.	Technical Approach and Methods—Pest Control.....	339d
PWS 3.1	Preventive Pest Management.....	339d
PWS 3.2	Scheduled Pest Control Services .....	339d
PWS 3.3	Service Calls—Unscheduled Pest Control Operations .....	339e
PWS 3.4	Carcass Disposal .....	339e
PWS 3.5	Encroachment.....	339e
PWS 4.	IDIQ and Surge Work.....	339e
PWS 4.1	Surge.....	339e



PWS 3.	Range Operations .....	345
PWS 3.1–3.1.4	Range Contractor Coordinators (RCC).....	347
PWS 3.1.5–		
3.1.7	AIC and ASTAC Air Controllers .....	348
PWS 3.2–		
3.2.11	Instrumentation Control Coordinator (ICC) .....	348
PWS 3.3–3.3.2	Range Facility Control Office (RFCO) and Air Control Support.....	349
PWS 3.3.3	Instrumentation and Logistic Services .....	349
PWS 3.4–3.4.1	Range Operations Planning.....	349
PWS 3.4.2–		
3.4.4	Range Scheduling System (RSS).....	350
PWS 3.4.5–		
3.4.7	Range Scheduling System Inputs.....	350
PWS 3.5–3.5.2	Operational Scheduling Documentation .....	351
PWS 3.5.3	Operational Instrumentation Plans (IP).....	352
PWS 3.5.4	Least Cost Operational Support Plan .....	352
PWS 3.6–3.6.2	Weather Station .....	352
PWS 3.7	New Systems and Cross-Utilization Training.....	352
PWS 3.8–3.8.7	Video Support .....	352a
PWS 3.9	AQM-37C Telemetry Support .....	353
PWS 4.	IDIQ Work .....	353



Page





	Page
[REDACTED]	
[REDACTED]	
[REDACTED]	
[REDACTED]	
PWS 2.4	Communications Equipment..... 361
PWS 2.5	Security Vehicles..... 361
PWS 2.6	Government Security Force and Law Enforcement Agency Interface..... 361
PWS 2.7–2.7.4	Jurisdiction ..... 361
PWS 2.8	Use of Deadly Force ..... 362
PWS 2.9	Disclosure ..... 362
PWS 2.10	Inspections and Searches..... 362
PWS 2.11	General & Post Orders of a Sentry ..... 362
PWS 2.12	Standards of Conduct ..... 362
PWS 2.13.1–6	Personnel Requirements ..... 362
PWS 2.13.7–	
2.13.7.3	Security Clearance Requirements ..... 362
PWS 2.13.8	Random Drug Screen Program ..... 362
PWS 2.13.9,	
3.7.1	Training and Employee Development..... 363
PWS 2.14	Firearms Licensing & Permits ..... 364
PWS 2.15	Safety Requirements..... 364
PWS 2.16, 3.6	Weapons & Ammunition ..... 365
PWS 2.17, 3.5	Records & Reports/Administrative and Clerical Services ..... 365
PWS 2.18.1,	
2.20.1	Basic Duty Shifts ..... 365
PWS 2.18.2	Meals..... 366
PWS 2.18.3–	
2.19	Deviation from Prescribed Duties/Positions Government-Directed ..... 366
PWS 2.20.1–	
2.20.2	Staffing ..... 366
PWS 2.21–	
2.21.2	Procedures..... 366
PWS 3.1	Entry Control Point (ECP) Services ..... 366
PWS 3.2, 3.4.6	Roving Guard Services ..... 366
PWS 3.3	Pass & ID Office Services..... 367
PWS 3.4	Dispatching Services..... 367
PWS 3.8	Key Control Activities ..... 367
PWS 3.9	Staff Briefings..... 367
PWS 3.10	Miscellaneous Guard Support..... 368
PWS 4.–4.1	IDIQ Work/Surge Requirements ..... 368



Page

[Redacted]	[Redacted]
------------	------------

[Redacted]	[Redacted]
------------	------------

PWS 3.	Technical Directive Work Request (TDWR) Procedures .....	374
PWS 3.1	Alteration and Construction Work .....	374
PWS 3.2	Repair and Maintenance .....	375
PWS 4.	IDIQ Work .....	375
PWS 4.1	Disaster Preparation and Relief Support .....	375

[Redacted]	[Redacted]
------------	------------

[Redacted]	[Redacted]
------------	------------


PWS 3.	Supply and Logistics Support .....	381
PWS 3.1	Management Functions .....	381
PWS 3.1.1-		
3.1.6	Performance Data Collection .....	381
PWS 3.1.7	Warehouse Issues Expensed to PMRF Government Offices, Tenants, Reimbursable Customers, and Other Support Contractors .....	381a
PWS 3.1.8	Data Requiring Government Approval .....	381a
PWS 3.1.9	Maintain and Keep Current the Supply Reference Documents .....	381a

	<u>Page</u>
PWS 3.1.10	381a
PWS 3.1.11	382
PWS 3.1.12	382
PWS 3.1.13,	
3.1.14	382
PWS 3.1.15	382
PWS 3.1.16,	
3.1.17	382
PWS 3.1.18	382
PWS 3.1.19	383
PWS 3.2-3.2.6	383
PWS 3.2.7	383
PWS 3.2.8	384
PWS 3.2.9	384
PWS 3.2.10	384
PWS 3.2.11	384
PWS 3.2.12	384
PWS 3.2.13-	
3.2.15	384
PWS 3.3-3.3.5	385
PWS 3.3.6	386
PWS 3.3.7-	
3.3.11	386
PWS 3.3.12	386
PWS 3.3.13	386
PWS 3.4	387
PWS 3.4.1	387
PWS 3.4.2-	
3.4.15	387
PWS 3.5-3.5.2	388
PWS 3.5.3-	
3.5.6	388
PWS 3.5.7	388a
PWS 3.5.8	388a
PWS 3.5.9-	
3.5.11	388a
PWS 3.5.12-	
3.5.14	389
PWS 3.5.15-	
3.5.18	389
PWS 3.5.19	389
PWS 3.5.20	389
PWS 3.5.21	389
PWS 3.5.22	390
PWS 3.5.23	390
PWS 3.5.24	390
PWS 3.5.25	390
PWS 3.5.26	390
PWS 3.6	390
PWS 3.6.1	390
PWS 3.6.2-	
3.6.8, 3.6.10	391
PWS 3.6.2-	
Outgoing Material and Equipment Transportation, Packing and Crating, Handling, Receipt, Acceptance, and Rejection	391

	<u>Page</u>	
PWS 3.6.9	Navy Wood Packing Material Compliance.....	391
PWS 3.6.11	Hazardous Materials (HM) and Explosive Shipments Packing, Crating, Marking, Labeling, and Certification .....	391
PWS 3.7	Acquisition (Simplified Acquisition Procedures [SAP]/Large Contracting).....	392
PWS 3.8–3.8.2	Personal Property .....	392
PWS 3.8.1	Contractor Personnel Shipment of Household Goods and Personal Property .....	392
PWS 3.9	Hazardous Material Control .....	392
PWS 3.9.1	Watchstanding .....	392
PWS 3.9.2	Hazardous Material Control and Management (HMCN) .....	392
PWS 3.9.3	Uniform Policies and Procedures.....	392
PWS 3.9.4	Consolidated Hazardous Material Reutilization and Inventory Management Program (CHRIMP).....	393
PWS 3.9.5	Single Centralized Control Point .....	393
PWS 3.9.6	Hazardous Substance Management Systems (HSMS) .....	393
PWS 3.9.7	Emergency Response Plan for the HAZMINCEN .....	393
PWS 3.9.8	Rinse, Dry, Clean, and Crush Type 55-Gallon Drums.....	394
PWS 3.10– 3.10.9	Mail Services/Postal.....	394
PWS 3.11, 3.11.1	Petroleum Management (POL) .....	395
PWS 3.12	Property Management .....	395
PWS 3.12.1– 3.12.3	Management and Administration .....	395
PWS 3.12.4, 3.12.16	Physical Inventory Program .....	395
PWS 3.12.5	Equipment, Supplies, and Materials Surveys .....	396
PWS 3.12.6	Property Responsibility and Accountability .....	396
PWS 3.12.7	Property Management Procedures .....	396
PWS 3.12.8	Authorized Sources of Government Property .....	396
PWS 3.12.9	Identification, Records, and Reports of Government Property .....	396
PWS 3.12.10	Property in Storage is Properly Protected and Preserved .....	397
PWS 3.12.11	Use of Government Property .....	397
PWS 3.12.12	Maintenance and Replacement of all Government Equipment .....	397
PWS 3.12.13	Control Records .....	397
PWS 3.12.14	Commingling .....	397
PWS 3.12.15	Government-Furnished Equipment (GFE) Kept Clean .....	397
PWS 3.12.17– 3.12.20	Submittals to the Government Property Administrator .....	397
PWS 3.12.21	Government and Personal Property Unrecorded, Found on Location and Abandoned.....	397a
PWS 3.12.22	Government-Owned Plant and Other Plan Equipment Identification .....	397a
PWS 3.12.23	Government Property Utilization and Maintenance .....	397a
PWS 3.12.24	Report Government Serviceable Excess Property .....	397a
PWS 3.12.25– 3.12.28	Excess Property Turn-In, Screening, Reporting and Disposal .....	397a
PWS 3.12.29	Master Property Listing Updates.....	397b
PWS 3.12.30	New Modified Incoming Materials and Equipment for Range Instrumentation not Under O&M Responsibility .....	397b
PWS 3.12.31	DPAS Management .....	397b
PWS 3.12.32	RITA Management .....	397c
PWS 3.13– 3.13.3	GSE and Target Supply Support .....	397c
PWS 3.13.4	Flight Clothing Requisitions .....	398



	<u>Page</u>
PWS 3.13.5–	
3.13.6	Depot-Level Repairable (DLR) Carcass Tracking ..... 398
PWS 3.13.7	Pre-Expended Bins ..... 398
PWS 3.14,	
3.14.1	SEPTAR Supply Support ..... 398
PWS 3.15–	
3.15.5	Materials and Equipment ..... 398
PWS 3.15.2.1–	
3.15.2.4	Government-Furnished Equipment (GFE) ..... 399
PWS 3.15.3	Contractor-Furnished Material (CFM) ..... 399
PWS 3.15.3.1	Parts, New and Rebuilt ..... 399
PWS 3.15.3.2	Acceptable Industrial Grade and Quality ..... 399
PWS 3.15.4.1–	
3.15.4.2	Contractor-Acquired Property (CAP)/Contractor-Acquired Material (CAM)..... 399
PWS 3.16	Legacy Computer Systems ..... 399
PWS 4.	IDIQ Work ..... 399
PWS 4.1	Surge..... 399





PWS 3.	Optics ..... 406
PWS 3.1	PMRF Launch Area Photographic Systems (LAPS)..... 408
PWS 3.1.1	Operations Planning..... 408
PWS 3.1.2	Launch Area Photographic System (LAPS) Augmentation ..... 408
PWS 3.1.3–	
3.1.5.1, 3.1.6.2	Pre-Deployment, Mission Execution, Modifications, and Post-Mission Breakdown ..... 409
PWS 3.1.6,	
3.1.6.1	Post-Mission Data Retrieval, Reduction, and Delivery ..... 409
PWS 3.1.7	Unscheduled Services ..... 410
PWS 3.1.8–	
3.1.8.3	Maintenance..... 410
PWS 3.1.8.4	Equipment Systems Diagrams..... 410
PWS 3.2, 3.3	Versatile Tracking Mount and SHOTS..... 411

	<u>Page</u>
PWS 3.2.1.1,	
3.3.1.1	Pre-Mission Flight Test Planning ..... 411
PWS 3.2.1.2,	
3.3.1.2	Pre-Mission/on-Site Flight Test Data ..... 412
PWS 3.2.2-	
3.2.2.2, 3.3.2-	
3.3.2.2	Pre-Mission and Mission Support ..... 412
PWS 3.2.3.1,	
3.3.3.1	Post-Flight Effort ..... 412
PWS 3.2.4.1,	
3.3.4.1	Operations Manuals ..... 413
PWS 3.2.4.2,	
3.3.4.2	Information Technology ..... 413
PWS 3.2.4.3,	
3.3.4.3	Configuration Management (CM) ..... 413
PWS 3.2.4.4,	
3.3.4.4	Monthly Status Reports ..... 413
PWS 3.2.4.5,	
3.3.4.5	Trip Reports ..... 413
PWS 3.2.5,	
3.3.5	Unscheduled Services ..... 414
PWS 3.2.6-	
3.2.6.5, 3.3.6-	
3.3.6.5	VTM & SHOTS Maintenance ..... 414
PWS 3.2.7-	
3.2.7.2, 3.3.7-	
3.3.7.2	Engineering Services ..... 415
PWS 3.2.7.3,	
3.3.7.3	System Obsolescence Prevention ..... 415
PWS 3.2.7.4,	
3.3.7.4	Equipment Systems Diagrams ..... 415
PWS 3.4-3.4.3	Surveillance Camera ..... 415
PWS 3.4.4	Unscheduled Services ..... 416
PWS 3.4.5-	
3.4.5.2	Maintenance ..... 416
PWS 3.4.6	Equipment Systems Diagrams ..... 416
PWS 3.5	Real-Time Object and Atmospheric Reconstruction System (ROARS) ..... 416
PWS 3.5.1	Operations Planning ..... 416
PWS 3.5.2,	
3.5.2.1	Post-Mission ..... 416
PWS 3.5.2.3	Data Management Support ..... 416
PWS 3.5.3-	
3.5.3.3	Engineering Support ..... 417
PWS 3.5.4	Training ..... 417
PWS 3.5.5	Trip Reports ..... 417
PWS 3.5.6	ROARS Maintenance ..... 417
PWS 3.6	Travel ..... 417
PWS 3.7	Plant Account Equipment Material and Spare Parts ..... 418
PWS 3.8	Real-Time Object and Atmospheric Reconstruction System (ROARS) Phase II ..... 418
PWS 3.8.1	Program Management ..... 418
PWS 3.8.1.1	Program Manager ..... 418
PWS 3.8.1.2	Industry-to-Government Transition Plans ..... 419
PWS 3.8.2	ROARS Phase II Development ..... 419



	<u>Page</u>
PWS 3.8.2.1,	
3.8.2.2	Software Design and Development ..... 419
PWS 3.8.2.3	Information Security ..... 419
PWS 3.8.2.4	Software Design and Development Software Modules ..... 419
PWS 3.8.3	ROARS Phase II Engineering Efforts ..... 419
PWS 3.8.3.1	Engineering Analysis..... 420
PWS 3.8.3.2	Technical Data ..... 420
PWS 3.8.3.3	System Engineering Analysis ..... 420
PWS 3.8.3.4	Statements of Functionality..... 420
PWS 3.8.3.5	Statements of Tests ..... 420
PWS 3.8.3.6	System Test Plans ..... 421
PWS 3.8.3.7	System #3 and System #4 Design Update and Subsystem Assembly ..... 421
PWS 3.8.3.8	System #3 and System #4 Assembly and Test ..... 421
PWS 3.8.3.9	System #3 and System #4 Delivery and Installation..... 421
PWS 3.8.4	ROARS Phase II Program Reviews..... 421
PWS 3.8.4.1	Test Readiness Reviews ..... 422
PWS 3.8.5	ROARS Phase II Facilities and Meetings ..... 422
PWS 3.8.5.1,	
3.8.5.2	Other Ranges..... 422
PWS 3.8.5.3	Technical Interchange Meeting (TIM) ..... 422
PWS 3.8.6	ROARS Phase II Documentation..... 422
PWS 3.8.6.1	Inputs to Documentation ..... 422
PWS 3.8.6.2	Configuration Management..... 422
PWS 3.8.6.3	Technical Reports and Technical Studies ..... 423
PWS 3.8.6.4	System Specifications ..... 423
PWS 3.8.6.5	Software Test Description (STD) ..... 423
PWS 3.8.6.6	Version Descriptions ..... 423
PWS 3.8.7,	
3.8.7.1	ROARS Phase II Training ..... 423
PWS 3.9	Planning ..... 423
PWS 3.9.1	Weekly Meetings ..... 424
PWS 4.	IDIQ Tasks ..... 424
PWS 4.1	Surge..... 424
PWS 4.2	Field Upgrades and Maintenance Modifications ..... 424





Page

[REDACTED]		
PWS 3.1–		
3.1.2	Planning Reporting.....	430
PWS 3.1.3	Reporting and Resources Tracking Needed to Support Individual Assets .....	431
PWS 3.2–		
3.2.4, 3.4.2,		
3.4.6	Installation, Removal, and Relocation.....	431
PWS 3.3–		
3.3.4, 3.4.3	Modification, Testing, Evaluation, and Development.....	432
PWS 3.3.5–		
3.3.6	Modification of the PADS Systems and Development and Modification of EO/IR and Video/Optics Systems.....	432
PWS 3.3.7,		
3.4.16, 3.5.8	Design, Fabrication, Maintenance, and Deployment of Target Mockups .....	432
PWS 3.4,		
3.4.1, 3.4.4,		
3.4.5, 3.4.7–		
3.4.10, 3.4.12–		
3.4.15	Operations.....	433
PWS 3.4.2	Installation, Removal, and Relocation in Support of Operations .....	435
PWS 3.4.3	Modification in Support of Operations .....	435
PWS 3.4.11	Operation of Vans and Trailers .....	435
PWS 3.4.16	Deployment of Target Mockups .....	435
PWS 3.4.17	Unscheduled Services .....	435
PWS 3.4.18	Provide Training, Instructions, and Pre-ex Brief for Airborne Threat Simulation Systems .....	435a
PW 3.5–		
3.5.3, 3.5.5–		
3.5.7	Maintenance (PWS).....	436
PW 3.5.4	Maintenance of EO/IR and Video/Optics Systems .....	437
PWS 3.6–3.6.3	Engineering Support .....	437
PWS 3.6.4	Maintenance, Modifications, and Management of EW Systems Software .....	437
PWS 3.6.5	Internal Liaison/Coordination .....	438
PWS 4.	IDIQ Work .....	438



	Page
PWS 3.	444
PWS 3.1	444
PWS 3.1.1–	
3.1.1.3	444
PWS 3.1.1.4	445
PWS 3.1.1.5	445
PWS 3.1.1.6	445
PWS 3.1.1.7	446
PWS 3.1.1.8	446
PWS 3.1.1.9	446
PWS 3.1.2–	
3.1.2.1, 3.1.3–	447
3.1.3.1	
PWS 3.1.2.2–	
3.1.2.4, 3.1.3.2–	
3.1.3.4	450
PWS 3.1.2.5,	
3.1.3.5	451
PWS 3.1.2.6,	
3.1.3.6	451
PWS 3.1.2.7,	
3.1.3.7	452
PWS 3.1.4–	
3.1.4.4	452
PWS 3.1.5,	
3.1.5.1	452
PWS 4.	452
PWS 4.1	452a
PWS 4.2	452a
PWS 4.3	452b
PWS 4.4	452b
PWS 4.5	452b



	Page
PWS 3.	Aerial Target Systems..... 457
PWS 3.1.1–	
3.1.1.2	Pre-Mission Briefing and Mission Planning ..... 457
PWS 3.1.1.3–	
3.1.1.6	Pre-Flight Launch Process..... 458
PWS 3.1.1.7	Launch and Control of BQM-34 and BQM-74..... 459
PWS 3.1.1.8	AQM-37C Flight Control..... 459
PWS 3.1.2–	
3.1.2.8	Maintenance and Buildup ..... 459
PWS 3.1.2.9	Weight and Balance Procedures ..... 460
PWS 3.1.2.10	Preparation of Targets for Transport..... 460
PWS 3.1.2.11	Decontamination of Targets..... 461
PWS 3.1.2.12–	
3.1.2.14	Inspections, Records, and QA Functions ..... 461
PWS 3.2	Other Responsibilities ..... 462
PWS 3.2.1	Target Operations at Sea..... 462
PWS 3.2.2	Individual Material Readiness List (IMRL) ..... 462
PWS 3.2.3	Shipment of Aerial Targets ..... 462
PWS 3.2.4	Plant Account Equipment and Spare Parts ..... 462
PWS 3.2.5	Travel ..... 462
PWS 3.2.6	Support for Visiting Target Activities ..... 462
PWS 4.	IDIQ Work ..... 462
PWS 4.1	Surge Requirements-RIM of the Pacific (RIMPAC) Exercise ..... 462



Page


A large black rectangular redaction box covers the central portion of the page, obscuring several lines of text. On the far left edge, there are six small black vertical rectangles of varying heights, and one larger black T-shaped rectangle at the bottom-left corner.



## **ACRONYM LIST**

The figure consists of four binary images arranged in a 2x2 grid. The top row images show vertical stacks of black bars, while the bottom row images show horizontal bars at different levels of abstraction. The left column images are more detailed, while the right column images are more generalized.



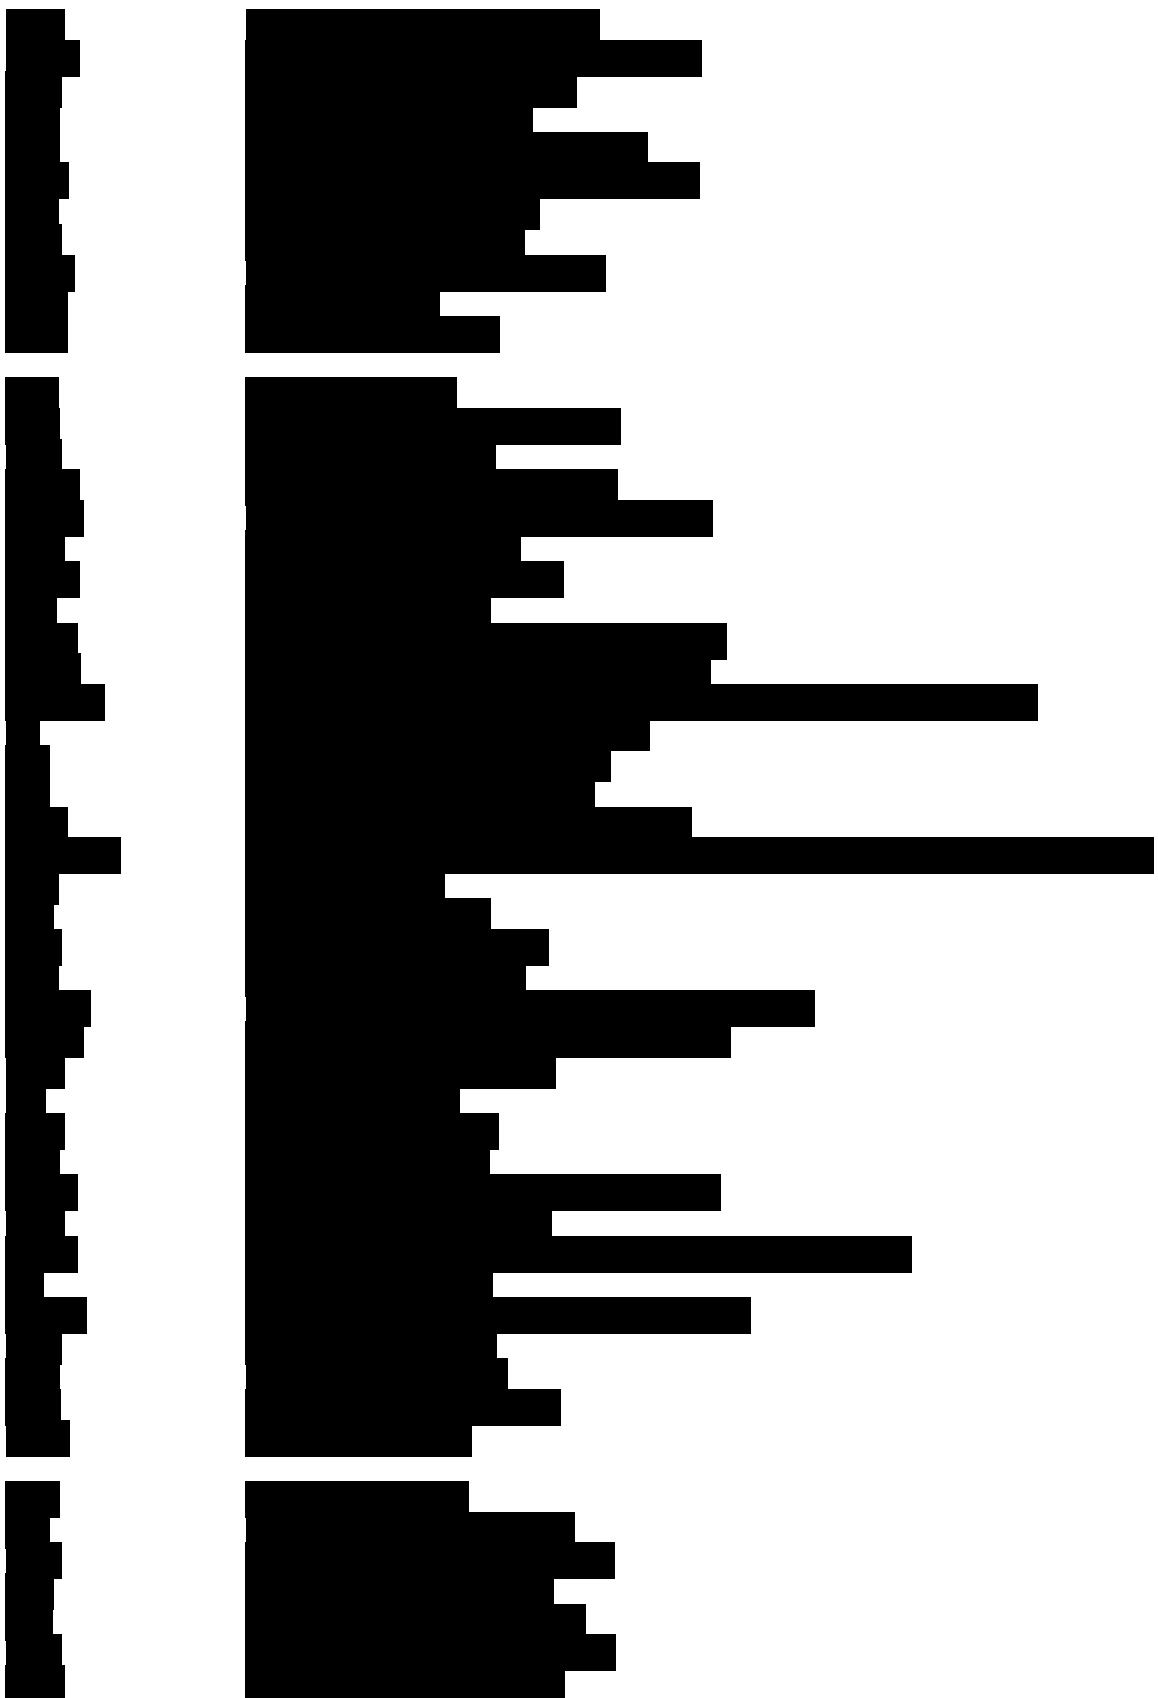








Figure 1. The five panels show the evolution of the density field of the dark matter particles in the simulation box. The panels are arranged vertically from top to bottom, showing the evolution from left to right. The panels are labeled with their respective snapshots: 1, 2, 3, 4, and 5.

The figure consists of five separate horizontal bar charts stacked vertically. Each chart has a black background and features white bars of varying widths. The top chart has 5 bars. The second chart from the top has 6 bars. The third chart has 5 bars. The fourth chart has 6 bars. The bottom chart has 7 bars. The bars are positioned such that they overlap slightly, creating a stepped effect across the entire stack.





The image is a highly pixelated, black-and-white graphic representation of the Seal of the Commonwealth of Massachusetts. The seal consists of a shield featuring a Native American figure with a bow and arrow. A five-pointed star is located in the lower-left quadrant of the shield. Above the shield is a crest showing a bent arm holding a broadsword. The entire design is enclosed within a decorative scroll or scrollwork border.







[REDACTED]

[REDACTED]

[REDACTED]

[REDACTED]

[REDACTED]

[REDACTED]
